

Application for Federal Assistance SF-424

* 1. Type of Submission:

- Preapplication
 Application
 Changed/Corrected Application

* 2. Type of Application:

- New
 Continuation
 Revision

* If Revision, select appropriate letter(s):

* Other (Specify):

* 3. Date Received:

4. Applicant Identifier:

3-12-0075-055-2025

5a. Federal Entity Identifier:

3-12-0075-055-2025

5b. Federal Award Identifier:

State Use Only:

6. Date Received by State:

7. State Application Identifier:

8. APPLICANT INFORMATION:

* a. Legal Name:

Pinellas, County of dba Board of County Commissioners

* b. Employer/Taxpayer Identification Number (EIN/TIN):

59-6000800

* c. Organizational DUNS:

0552002160000

d. Address:

* Street1:

c/o Office of Management and Budget

Street2:

14 S. Ft. Harrison, 5th Floor

* City:

Clearwater

County/Parish:

Pinellas

* State:

FL: Florida

Province:

* Country:

USA: UNITED STATES

* Zip / Postal Code:

33756-5165

e. Organizational Unit:

Department Name:

St. Pete-Clearwater Int'l Apt

Division Name:

St. Pete-Clearwater Int'l Apt

f. Name and contact information of person to be contacted on matters involving this application:

Prefix:

Mr.

* First Name:

Thomas

Middle Name:

R.

* Last Name:

Jewsbury

Suffix:

Title:

Airport Director

Organizational Affiliation:

The Airport is a department of Pinellas County Government

* Telephone Number:

727 453-7801

Fax Number:

727 453-7846

* Email:

jewsbury@fly2pie.com

Application for Federal Assistance SF-424

*** 9. Type of Applicant 1: Select Applicant Type:**

B: County Government

Type of Applicant 2: Select Applicant Type:

Type of Applicant 3: Select Applicant Type:

* Other (specify):

*** 10. Name of Federal Agency:**

Federal Aviation Administration

11. Catalog of Federal Domestic Assistance Number:

20-106

CFDA Title:

Airport Improvement Program. This grant is PIE's FY22 apportionment of the BIL AIG program.

*** 12. Funding Opportunity Number:**

Not Applicable

* Title:

N/A

13. Competition Identification Number:

Not Applicable

Title:

14. Areas Affected by Project (Cities, Counties, States, etc.):

Add Attachment

*** 15. Descriptive Title of Applicant's Project:**

Design and Pre-Construction Activities for PIE's Passenger Terminal Improvements project.

Attach supporting documents as specified in agency instructions.

Add Attachments

Delete

Application for Federal Assistance SF-424

16. Congressional Districts Of:
* a. Applicant * b. Program/Project

Attach an additional list of Program/Project Congressional Districts if needed.

17. Proposed Project:
* a. Start Date: * b. End Date:

18. Estimated Funding (\$):

* a. Federal	<input type="text" value="4,914,957.00"/>
* b. Applicant	<input type="text" value="0.00"/>
* c. State	<input type="text" value="0.00"/>
* d. Local	<input type="text" value="1,126,284.00"/>
* e. Other	<input type="text" value="0.00"/>
* f. Program Income	<input type="text" value="0.00"/>
* g. TOTAL	<input type="text" value="6,041,241.00"/>

*** 19. Is Application Subject to Review By State Under Executive Order 12372 Process?**
 a. This application was made available to the State under the Executive Order 12372 Process for review on .
 b. Program is subject to E.O. 12372 but has not been selected by the State for review.
 c. Program is not covered by E.O. 12372.


*** 20. Is the Applicant Delinquent On Any Federal Debt? (If "Yes," provide explanation in attachment.)**
 Yes No
If "Yes", provide explanation and attach

21. *By signing this application, I certify (1) to the statements contained in the list of certifications and (2) that the statements herein are true, complete and accurate to the best of my knowledge. I also provide the required assurances** and agree to comply with any resulting terms if I accept an award. I am aware that any false, fictitious, or fraudulent statements or claims may subject me to criminal, civil, or administrative penalties. (U.S. Code, Title 218, Section 1001)**
 ** I AGREE
** The list of certifications and assurances, or an internet site where you may obtain this list, is contained in the announcement or agency specific instructions.

Authorized Representative:
Prefix: * First Name:
Middle Name:
* Last Name:
Suffix:
* Title:
* Telephone Number: Fax Number:
* Email:

* Signature of Authorized Representative: * Date Signed:

ID	Task Name	Duration	Start	Finish
1	Task 1 - Conceptual / Preliminary Design	498 days	Tue 7/16/24	Tue 6/30/26
2	Task 2 - Conceptual / Preliminary Design	153 days	Tue 7/16/24	Thu 2/20/25
3	Design Kick-Off Meeting/Workshop	2 days	Tue 7/16/24	Wed 7/17/24
4	T2.01 - Data Collection	5 days	Tue 7/16/24	Mon 7/22/24
5	T2.05 - Master Plan Review	7 days	Thu 7/18/24	Fri 7/26/24
6	T2.06 - Terminal Planning Validation	20 days	Mon 7/29/24	Fri 8/23/24
7	T2.08 - Conceptual Design Dev	25 days	Mon 8/26/24	Mon 9/30/24
8	T2.02.01 - Site Survey (Area 1) / Scan	20 days	Tue 10/1/24	Mon 10/28/24
9	T2.02.01 - Site Survey (Area 2)	15 days	Tue 10/29/24	Mon 11/18/24
10	T2.02.01 - Site Survey (Area 3)	15 days	Tue 11/19/24	Wed 12/11/24
11	T2.02.01 - Site Survey (Area 4)	15 days	Thu 12/12/24	Fri 1/3/25
12	T2.02.01 - Site Survey (Area 5)	10 days	Mon 1/6/25	Fri 1/17/25
13	T2.02.02 - Geotech Testing / Report	20 days	Tue 10/1/24	Mon 10/28/24
14	T2.04 - Existing Cond Revit Model	14 days	Tue 10/29/24	Fri 11/15/24
15	T2.07 - CMAR Selection Assistance	70 days	Thu 7/18/24	Thu 10/24/24
16	T2.09 - Concept Review Workshop	1 day	Wed 11/6/24	Wed 11/6/24
17	T2.03 - Site Walkthrough	1 day	Thu 11/7/24	Thu 11/7/24
18	Design Team Internal Kickoff (Engineering)	1 day	Fri 11/22/24	Fri 11/22/24
19	T2.10 - Concept Refinement	41 days	Thu 11/7/24	Wed 1/8/25
20	T2.11 - Phasing and Constructability	42 days	Thu 11/7/24	Thu 1/9/25
21	T2.12 - Cost Estimating	36 days	Thu 11/7/24	Tue 12/31/24
22	T2.13 - Refined Concept Review Mtg	1 day	Mon 1/13/25	Mon 1/13/25
23	T2.15 - QA/QC	10 days	Thu 1/9/25	Wed 1/22/25
24	T2.16 - Concept Submission	1 day	Thu 1/23/25	Thu 1/23/25
25	Owner/Stakeholder Review	15 days	Fri 1/24/25	Thu 2/13/25
26	T2.14 - Concept Design Report Mtg	1 day	Thu 2/20/25	Thu 2/20/25
27	Task 3 - 30% Schematic Design	105 days	Fri 1/24/25	Fri 6/20/25
28	Merge Concept into Revit Model	15 days	Fri 1/24/25	Thu 2/13/25
29	SUE Quality Level B (Designing) - Phase 1	25 days	Fri 1/24/25	Thu 2/27/25
30	SUE Quality Level B (Designing) - Phase 2	6 days	Fri 2/28/25	Fri 3/7/25
31	T3.01 - Architectural	69 days	Fri 1/24/25	Wed 4/30/25
32	T3.02 - Interiors/FF&E	69 days	Fri 1/24/25	Wed 4/30/25
33	T3.03 - Terminal Simulation Modeling	59 days	Fri 2/7/25	Wed 4/30/25
34	T3.04 - Schematic Design Documents	59 days	Fri 2/7/25	Wed 4/30/25
35	T3.05 - AHU Outreach	69 days	Fri 1/24/25	Wed 4/30/25
36	T3.06 - CMAR Estimating & VE	69 days	Fri 1/24/25	Wed 4/30/25
37	T3.07 - Design Workshop #1	2 days	Fri 2/21/25	Mon 2/24/25
38	T3.07 - Design Workshop #2	3 days	Wed 3/26/25	Fri 3/28/25
39	T3.08 - Federal Agency Coordination	69 days	Fri 1/24/25	Wed 4/30/25
40	Model Lock	2 days	Thu 4/17/25	Fri 4/18/25
41	T3.09 - QA/QC	15 days	Thu 5/1/25	Wed 5/21/25
42	T3.10 - SD Documents Submission	1 day	Thu 5/22/25	Thu 5/22/25

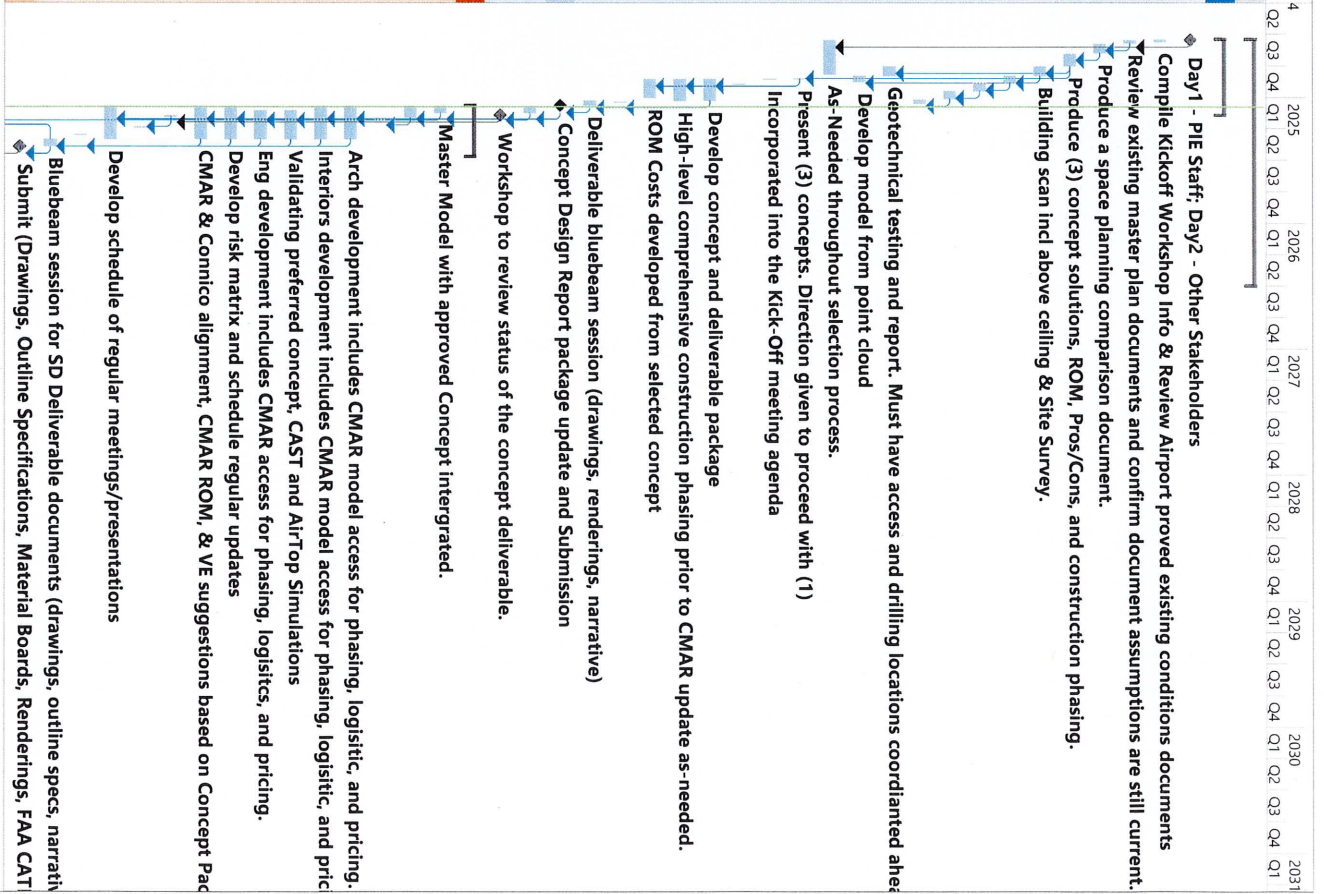

ID	Task Name	Duration	Start	Finish
43	Owner/Stakeholder Review	15 days	Fri 5/23/25	Fri 6/13/25
44	T3.11 - SD Review Meeting	1 day	Fri 6/20/25	Fri 6/20/25
45	Task 4 - 60% Design Development	102 days	Mon 6/16/25	Thu 11/6/25
46	T4.01 - Comment Resolution	30 days	Mon 6/16/25	Mon 7/28/25
47	SUE Quality Level A (Locating - 40 test holes) - Ph1 10 days	10 days	Mon 6/16/25	Fri 6/27/25
48	SUE Quality Level A (Locating - 24 test holes) - Ph2 6 days	6 days	Mon 6/30/25	Tue 7/8/25
49	Issue Revised Model	1 day	Tue 7/29/25	Tue 7/29/25
50	T4.02 - Design Development	67 days	Mon 6/16/25	Thu 9/18/25
51	T4.03 - AHJ Outreach	67 days	Mon 6/16/25	Thu 9/18/25
52	T4.04 - CMAR Estimating & VE	67 days	Mon 6/16/25	Thu 9/18/25
53	T4.05 - Design Workshop #3	2 days	Tue 7/22/25	Wed 7/23/25
54	T4.05 - Design Workshop #4	3 days	Thu 8/21/25	Mon 8/25/25
55	T4.06 - Federal Agency Coordination	67 days	Mon 6/16/25	Thu 9/18/25
56	Model Lock	2 days	Fri 9/5/25	Mon 9/8/25
57	T4.07 - QA/QC	15 days	Fri 9/19/25	Thu 10/9/25
58	T4.08 - DD Documents Submission	1 day	Fri 10/10/25	Fri 10/10/25
59	Owner/Stakeholder Review	15 days	Mon 10/13/25	Fri 10/31/25
60	T4.09 - DD Review Meeting	1 day	Thu 11/6/25	Thu 11/6/25
61	Task 5 - 90% Construction Documents	135 days	Mon 11/3/25	Thu 5/14/26
62	T5.01 - Comment Resolution	30 days	Mon 11/3/25	Tue 12/16/25
63	T5.02 - 90% Construction Documents	74 days	Mon 11/3/25	Wed 2/18/26
64	T5.02.03 - FDOT R/W Permit	90 days	Mon 11/3/25	Thu 3/12/26
65	T5.02.03 - SWFWMD Permit	120 days	Mon 11/3/25	Thu 4/23/26
66	T5.03 - AHJ Outreach	74 days	Mon 11/3/25	Wed 2/18/26
67	T5.04 - CMAR Estimating & VE	74 days	Mon 11/3/25	Wed 2/18/26
68	T5.05 - Design Workshop #5	2 days	Tue 12/9/25	Wed 12/10/25
69	T5.05 - Design Workshop #6	3 days	Fri 1/16/26	Tue 1/20/26
70	T5.06 - Federal Agency Coordination	74 days	Mon 11/3/25	Wed 2/18/26
71	Model Lock	2 days	Thu 1/29/26	Fri 1/30/26
72	T5.07 - QA/QC	15 days	Thu 2/19/26	Wed 3/11/26
73	T5.08 - CD Documents Submission	1 day	Thu 3/12/26	Thu 3/12/26
74	Owner/Stakeholder Review	15 days	Fri 3/13/26	Thu 4/2/26
75	T5.09 - CD Review Meeting	1 day	Fri 4/10/26	Fri 4/10/26
76	T5.12 - Permitting	45 days	Fri 3/13/26	Thu 5/14/26
77	Task 6 - IFC Documents	62 days	Fri 4/3/26	Tue 6/30/26
78	T6.01 - Comment Resolution	20 days	Fri 4/3/26	Thu 4/30/26
79	T6.02 - 100% CDs Documentation	40 days	Fri 4/3/26	Fri 5/29/26
80	T6.05 - QA/QC	10 days	Mon 6/1/26	Fri 6/12/26
81	Resubmit to Plan Check	20 days	Fri 5/15/26	Fri 6/12/26
82	T6.06 - Submit 100% CDs	1 day	Mon 6/15/26	Mon 6/15/26
83	Owner/Stakeholder Review	10 days	Tue 6/16/26	Mon 6/29/26
84	T6.07 - CD Review Meeting	1 day	Tue 6/30/26	Tue 6/30/26



ID	Task Name	Duration	Start	Finish
85	CMAR & Construction Services	1698 days	Mon 5/27/24	Tue 12/17/30
86	CMAR	1614 days	Mon 5/27/24	Wed 8/21/30
87	RFQ Proposal Evaluations	5 days	Mon 5/27/24	Fri 5/31/24
88	Notification of Shortlist	17 days	Mon 6/3/24	Tue 6/25/24
89	Interviews and Selection	1 day	Wed 7/24/24	Wed 7/24/24
90	Fee Negotiations	31 days	Thu 7/25/24	Fri 9/6/24
91	County Contract Review	87 days	Mon 9/9/24	Mon 1/13/25
92	Board Award - Preconstruction Services	1 day	Tue 1/14/25	Tue 1/14/25
93	Pre-Construction Services	382 days	Tue 1/28/25	Mon 7/27/26
94	Preliminary Estimate and Construction Phasing	54 days	Fri 2/14/25	Wed 4/30/25
95	30% Estimate and Construction Phasing Deliverable	20 days	Thu 5/1/25	Thu 5/29/25
96	Estimate and Construction Phasing Development	78 days	Fri 5/30/25	Thu 9/18/25
97	60% Estimate and Construction Phasing Deliverable	20 days	Fri 9/19/25	Thu 10/16/25
98	Early Procurement Bidding	45 days	Mon 10/13/25	Tue 12/16/25
99	GMP	66 days	Fri 3/13/26	Mon 6/15/26
100	County Contract Review	20 days	Tue 6/16/26	Mon 7/13/26
101	Board Award - Construction Services	1 day	Tue 7/14/26	Tue 7/14/26
102	Construction	1062 days	Tue 7/28/26	Wed 8/21/30
103	Owners Representative	1497 days	Fri 11/8/24	Wed 8/21/30
104	Advertise RFP	1 day	Fri 11/8/24	Fri 11/8/24
105	Site Visit	1 day	Thu 11/21/24	Thu 11/21/24
106	Deadline for Questions	1 day	Thu 12/5/24	Thu 12/5/24
107	Submittal of Written Proposals	1 day	Fri 12/20/24	Fri 12/20/24
108	Evaluation of Written Proposals	34 days	Mon 12/23/24	Mon 2/10/25
109	Notification of Shortlist	1 day	Tue 2/11/25	Tue 2/11/25
110	Oral Presentations and Selection	1 day	Thu 3/6/25	Thu 3/6/25
111	Scoping and Fee Negotiation	46 days	Fri 3/7/25	Fri 5/9/25
112	County Contract Review	30 days	Mon 5/12/25	Mon 6/23/25
113	Board Award	1 day	Tue 6/17/25	Tue 6/17/25
114	PreConstruction Services	230 days	Mon 7/14/25	Mon 6/8/26
115	Construction Services	1062 days	Tue 7/28/26	Wed 8/21/30
116	Task 7 - Construction Administration	1145 days	Wed 7/29/26	Tue 12/17/30
117	T7.01 - Pre-Construction Conference	1 day	Wed 7/29/26	Wed 7/29/26
118	T7.02 - RFI/Submittal Reviews	1000 days	Thu 7/30/26	Wed 5/29/30
119	T7.03 - Site Visits / Meetings	1000 days	Thu 7/30/26	Wed 5/29/30
120	T7.04 - Change order and Supplemental Instruction	1000 days	Thu 7/30/26	Wed 5/29/30
121	T7.05 - Punchlist Final Observation	120 days	Fri 3/8/30	Thu 8/22/30
122	Task 8 - Project Closeout	107 days	Mon 7/22/30	Tue 12/17/30
123	Receive As-Built Documents	1 mon	Fri 8/23/30	Thu 9/19/30
124	T8.01 - Record Documents	63 days	Fri 9/20/30	Tue 12/17/30
125	T8.02 Warranty Period Inspection	1 day	Mon 7/22/30	Mon 7/22/30

