

CONSTRUCTION AGREEMENT

This Construction Agreement ("Agreement") is made as of June 4, 2025, by and between CSX TRANSPORTATION, INC., a Virginia corporation with its principal place of business in Jacksonville, Florida ("CSXT"), and PINELLAS COUNTY, FLORIDA BOARD OF COUNTY COMMISSIONERS, a body corporate and political subdivision of the State of Florida ("Agency").

EXPLANATORY STATEMENT

1. Agency has proposed to construct, or to cause to be constructed, upgrading the existing asphalt crossing surface with a tub-platform to accommodate roadway improvements, which include roadway milling, resurfacing, and striping with the implementation of the dynamic envelope, along with curb and gutter installation, and installation of concrete sidewalks on both sides of the roadway, within the CSXT right of way at 46th Avenue North with Department of Transportation Crossing Inventory Number 626693F, Railroad Milepost Number ARE 894.46, located within the Florida Zone, Clearwater Subdivision, in Saint Petersburg, Pinellas County, Florida (the "Project").
2. Agency has obtained, or will obtain, all authorizations, permits and approvals from all local, state and federal agencies (including Agency), and their respective governing bodies and regulatory agencies, necessary to proceed with the Project and to appropriate all funds necessary to construct the Project.
3. Agency acknowledges that: (i) by entering into this Agreement, CSXT will provide services and accommodations to promote public interest in this Project, without profit or other economic inducement typical of other Agency contractors; (ii) neither CSXT nor its affiliates (including their respective directors, officers, employees or agents) will incur any costs, expenses, losses or liabilities in excess of payments made to CSXT, by or on behalf of Agency or its contractors, pursuant to this Agreement; and (iii) CSXT retains the paramount right to regulate all activities affecting its property and operations.
4. It is the purpose of this Agreement to provide for the terms and conditions upon which the Project may proceed.

NOW, THEREFORE, in consideration of the foregoing Explanatory Statement and other good and valuable consideration, the receipt and sufficiency of which are acknowledged by the parties, the parties agree as follows:

1. Project Plans and Specifications

- 1.1 Preparation and Approval. Pursuant to Exhibit A of this Agreement, all plans, specifications, drawings and other documents necessary or appropriate to the design and construction of the Project shall be prepared, at Agency's sole cost and expense, by

Agency or CSXT or their respective contractors. Project plans, specifications and drawings prepared by or on behalf of Agency shall be subject, at CSXT's election, to the review and approval of CSXT. Such plans, specifications and drawings, as prepared or approved by CSXT, are referred to as the "Plans", and shall be incorporated and deemed a part of this Agreement. Plans prepared or submitted to and approved by CSXT as of the date of this Agreement are set forth in Exhibit B to this Agreement.

- 1.2 Effect of CSXT Approval or Preparation of Plans. By its review, approval or preparation of Plans pursuant to this Agreement, CSXT signifies only that such Plans and improvements constructed in accordance with such Plans satisfy CSXT's requirements. CSXT expressly disclaims all other representations and warranties in connection with the Plans, including, but not limited to, the integrity, suitability or fitness for the purposes of Agency or any other persons of the Plans or improvements constructed in accordance with the Plans.
- 1.3 Compliance with Plans. The Project shall be constructed in accordance with the Plans.

2. Allocation and Conduct of Work

Work in connection with the Project shall be allocated and conducted as follows:

- 2.1 CSXT Work. Subject to timely payment of Reimbursable Expenses as provided by Section 4, CSXT shall provide, or cause to be provided, the services as set forth by Exhibit A to this Agreement. Agency agrees that CSXT shall provide all services that CSXT deems necessary or appropriate (whether or not specified by Exhibit A) to preserve and maintain its property and operations, without impairment or exposure to liability of any kind and in compliance with all applicable federal, state and local regulations and CSXT's contractual obligations, including, but not limited to, CSXT's existing or proposed third party agreements and collective bargaining agreements.
- 2.2 Agency Work. Agency shall perform, or cause to be performed, all work as set forth by Exhibit A, at Agency's sole cost and expense.
- 2.3 Conduct of Work. CSXT shall commence its work under this Agreement following: (i) delivery to CSXT of a notice to proceed from Agency; (ii) payment of Reimbursable Expenses (as provided by Section 4.1) as required by CSXT prior to the commencement of work by CSXT; (iii) issuance of all permits, approvals and authorizations necessary or appropriate for such work; and (iv) delivery of proof of insurance acceptable to CSXT, as required by Section 9. The initiation of any services by CSXT pursuant to this Agreement, including, but not limited to, the issuance of purchase orders or bids for materials or services, shall constitute commencement of work for the purposes of this Section. The parties intend that all work by CSXT or on

CSXT property shall conclude no later than **March 31, 2026**, unless the parties mutually agree to extend such date.

3. **Special Provisions.** Agency shall observe and abide by, and shall require its contractors (“Contractors”) to observe and abide by the terms, conditions and provisions set forth in Exhibit C to this Agreement (the “Special Provisions”). To the extent that Agency performs Project work itself, Agency shall be deemed a Contractor for purposes of this Agreement. Agency further agrees that, prior to the commencement of Project work by any third party Contractor, such Contractor shall execute and deliver to CSXT Schedule I to this Agreement to acknowledge Contractor’s agreement to observe and abide by the terms and conditions of this Agreement.

4. **Cost of Project and Reimbursement Procedures**

- 4.1 **Reimbursable Expenses.** Agency shall reimburse CSXT for all costs and expenses incurred by CSXT in connection with the Project, including, without limitation: (1) all out of pocket expenses, (2) travel and lodging expenses, (3) telephone, facsimile, and mailing expenses, (4) costs for equipment, tools, materials and supplies, (5) sums paid to CSXT’s consultants and subcontractors, and (6) CSXT labor in connection with the Project, together with CSXT labor overhead percentages established by CSXT pursuant to applicable law (collectively, “**Reimbursable Expenses**”). Reimbursable Expenses shall also include expenses incurred by CSXT prior to the date of this Agreement to the extent identified by the Estimate provided pursuant to Section 4.2.
- 4.2 **Estimate.** CSXT has estimated the total Reimbursable Expenses for the Project as shown on Exhibit D (the “**Estimate**”, as amended or revised). In the event CSXT anticipates that actual Reimbursable Expenses for the Project may exceed such Estimate, it shall provide Agency with the revised Estimate of the total Reimbursable Expenses, together with a revised Payment Schedule (as defined by Section 4.3.1), for Agency’s approval and confirmation that sufficient funds have been appropriated to cover the total Reimbursable Expenses of such revised Estimate. CSXT may elect, by delivery of notice to Agency, to immediately cease all further work on the Project, unless and until Agency provides such approval and confirmation. Furthermore, the Agency acknowledges and understands that any estimated cost to construct the project shall only be good for a limited period of time and that any delays to move to construction, if CSXT agrees to such construction, shall result in increased costs.
- 4.3 **Payment Terms.**
 - 4.3.1 Agency shall pay CSXT for Reimbursable Expenses in the amounts and on the dates set forth in the Payment Schedule as shown on Exhibit E (the “**Payment Schedule**”, as revised pursuant to Section 4.2). CSXT agrees to submit invoices to Agency for such amounts and Agency shall remit payment to CSXT at the later

of thirty (30) days following delivery of each such invoice to Agency or, the payment date (if any) set forth in the Payment Schedule.

- 4.3.2 Following completion of the Project, CSXT shall submit to Agency a final invoice that reconciles the total Reimbursable Expenses incurred by CSXT against the total payments received from Agency. Agency shall pay to CSXT the amount by which Reimbursable Expenses exceed total payments as shown by the final invoice, within thirty (30) days following delivery of such invoice to Agency. In the event that the payments received by CSXT from Agency exceed the Reimbursable Expenses, CSXT shall remit such excess to Agency.
- 4.3.3 In the event that Agency fails to pay CSXT any sums due CSXT under this Agreement: (i) Agency shall pay CSXT interest at the lesser of 1.0% per month or the maximum rate of interest permitted by applicable law on the delinquent amount until paid in full; and (ii) CSXT may elect, by delivery of notice to Agency: (A) to immediately cease all further work on the Project, unless and until Agency pays the entire delinquent sum, together with accrued interest; and/or (B) to terminate this Agreement.

- 4.3.4 All invoices from CSXT shall be delivered to Agency in accordance with Section 16 of this Agreement. All payments by Agency to CSXT shall be made by certified check and mailed to the following address or such other address as designated by CSXT's notice to Agency:

CSX Transportation, Inc.
P.O. Box 530192
Atlanta, GA 30353-0192

- 4.4 Effect of Termination. Agency's obligation to pay to CSXT Reimbursable Expenses in accordance with Section 4 shall survive termination of this Agreement for any reason.
5. Appropriations Agency represents to CSXT that: (i) Agency has appropriated funds sufficient to reimburse CSXT for the Reimbursable Expenses encompassed by the Estimate attached as Exhibit D; (ii) Agency shall use its best efforts to obtain appropriations necessary to cover Reimbursable Expenses encompassed by subsequent Estimates approved by Agency; and (iii) Agency shall promptly notify CSXT in the event that Agency is unable to obtain such appropriations.
6. Easements and Licenses
 - 6.1 Agency Obligation. Agency shall acquire all necessary licenses, permits and easements required for the Project.

- 6.2 **Temporary Construction Licenses.** Insofar as it has the right to do so, CSXT hereby grants Agency a nonexclusive license to access and cross CSXT's property, to the extent necessary for the construction of the Project (excluding ingress or egress over public grade crossings), along such routes and upon such terms as may be defined and imposed by CSXT and such temporary construction easements as may be designated on the Plans approved by CSXT.
 - 6.3 **Temporary Construction Easements.** CSXT may grant without warranty to Agency, if required, a temporary non-exclusive easement for access to the extent necessary for the project on terms and conditions and at a price acceptable to the parties..
 - 6.4 **Maintenance Agreement.** Contemporaneous with the execution of this Agreement, CSXT and Agency have executed that certain Maintenance Agreement providing for Agency's ongoing use, maintenance, repair, renewal and removal of the Project.
 - 6.5 **Permanent Easements.** Insofar as it has the right to do so, CSXT shall grant, without warranty to Agency, easements for the use and maintenance (in accordance with the provisions of the Maintenance Agreement described in 6.4) of the Project wholly or partly on CSXT property as shown on the Plans approved by CSXT, if any, on terms and conditions and at a price acceptable to both parties. Upon request by CSXT, Agency shall furnish to CSXT descriptions and plat plans for the easements.
7. **Permits At its sole cost and expense,** Agency shall procure all permits and approvals required by any federal, state, or local governments or governmental agencies for the construction, maintenance and use of the Project, copies of which shall be provided to CSXT.
 8. **Termination**
 - 8.1 **By Agency.** For any reason, Agency may, as its sole remedy, terminate this Agreement by delivery of notice to CSXT. Agency shall not be entitled to otherwise pursue claims for consequential, direct, indirect or incidental damages or lost profits as a consequence of CSXT's default or termination of this Agreement or Work on the Project by either party.
 - 8.2 **By CSXT.** In addition to the other rights and remedies available to CSXT under this Agreement, CSXT may terminate this Agreement by delivery of notice to Agency in the event Agency or its Contractors fail to observe the terms or conditions of this Agreement and such failure continues more than ten (10) business days following delivery of notice of such failure by CSXT to Agency.
 - 8.3 **Consequences of Termination.** If the Agreement is terminated by either party pursuant to this Section or any other provision of this Agreement, the parties understand that it may be impractical for them to immediately stop the Work. Accordingly, they agree that, in such instance a party may continue to perform Work until it has reached a point

where it may reasonably and safely suspend the Work. Agency shall reimburse CSXT pursuant to this Agreement for the Work performed, plus all costs reasonably incurred by CSXT to discontinue the Work and protect the Work upon full suspension of the same, the cost of returning CSXT's property to its former condition, and all other costs of CSXT incurred as a result of the Project up to the time of full suspension of the Work. Termination of this Agreement or Work on the Project, for any reason, shall not diminish or reduce Agency's obligation to pay CSXT for Reimbursable Expenses incurred in accordance with this Agreement. In the event of the termination of this Agreement or the Work for any reason, CSXT's only remaining obligation to Agency shall be to refund to Agency payments made to CSXT in excess of Reimbursable Expenses in accordance with Section 4.

9. **Insurance** In addition to the insurance that Agency requires of its Contractor, Agency shall acquire or require its Contractor to purchase and maintain insurance in compliance with CSXT's insurance requirements attached to this Agreement as Exhibit F. Neither Agency nor Contractor shall commence work on the Project until such policy or policies have been submitted to and approved by CSXT's Risk Management Department.

10. Ownership and Maintenance

- 10.1 **By Agency**. Agency shall maintain and repair, at its sole cost and expense, all parts comprising the permanent aspects of the Project, as shown by the Plans, consisting of roadway pavement up to the outer ends of the railroad cross ties, sidewalks, guardrails, and curbs, in good and safe condition to CSXT's satisfaction. In the event Agency fails to do so after reasonable notice from CSXT (unless an emergency condition exists or is imminent in the opinion of CSXT that requires immediate action), CSXT may perform such maintenance and repair, at Agency's sole cost and expense.
- 10.2 **By CSXT**. CSXT shall maintain and repair the crossing surface between the ends of its cross ties and its signal facilities at the crossing, at Agency's sole cost and expense.
- 10.3 **Alterations**. Agency shall not undertake any alteration, modification or expansion of the Project, without the prior written approval of CSXT, which may be withheld for any reason, and the execution of such agreements as CSXT may require. CSXT may undertake alterations of its property, track or facilities and shall be reimbursed by Agency for the expenses incurred by CSXT with respect to the removal and restoration of the crossing in connection with such alteration.

11. Indemnification

- 11.1 **Generally**. To the maximum extent permitted by applicable law, Agency and its Contractors shall indemnify, defend, and hold CSXT and its affiliates harmless from and against all claims, demands, payments, suits, actions, judgments, settlements, and damages of every nature, degree, and kind (including direct, indirect, consequential,

incidental, and punitive damages), for any injury to or death to any person(s) (including, but not limited to the employees of CSXT, its affiliates, Agency or its Contractors), for the loss of or damage to any property whatsoever (including but not limited to property owned by or in the care, custody, or control of CSXT, its affiliates, Agency or its Contractors, and environmental damages and any related remediation brought or recovered against CSXT and its affiliates), arising directly or indirectly from the negligence, recklessness or intentional wrongful misconduct of the Contractors, Agency, and their respective agents, employees, invitees, contractors, or its contractors' agents, employees or invitees in the performance of work in connection with the Project or activities incidental thereto, or from their presence on or about CSXT's property. The foregoing indemnification obligation shall not be limited to the insurance coverage required by this Agreement, except to the extent required by law or otherwise expressly provided by this Agreement. Notwithstanding the aforementioned requirements, and without limiting the Agency's Contractors' liability, the Agency's liability to indemnify CSXT shall be limited to the "per person" and "per occurrence" sovereign immunity limits as set forth in Florida Statutes, Section 768.28(5), as may be amended, applicable to the date of the incident giving rise to the obligation to indemnify.

- 11.2 Compliance with Laws. Agency shall comply, and shall require its Contractors to comply, with any federal, state, or local laws, statutes, codes, ordinances, rules, and regulations applicable to its construction and maintenance of the Project. Agency's Contractors shall indemnify, defend, and hold CSXT and its affiliates harmless with respect to any fines, penalties, liabilities, or other consequences arising from breaches of this Section.
- 11.3 "CSXT Affiliates". For the purpose of this Section 11, CSXT's affiliates include CSX Corporation and all entities, directly or indirectly, owned or controlled by or under common control of CSXT or CSX Corporation and their respective officers, directors, employees and agents.
- 11.4 Notice of Incidents. Agency and its Contractor shall notify CSXT promptly of any loss, damage, injury or death arising out of or in connection with the Project work.
- 11.5 Survival. The provisions of this Section 11 shall survive the termination or expiration of this Agreement.
12. Independent Contractor The parties agree that neither Agency nor its Contractors shall be deemed either agents or independent contractors of CSXT. Except as otherwise provided by this Agreement, CSXT shall exercise no control whatsoever over the employment, discharge, compensation of, or services rendered by Agency or Agency's Contractors, or the construction practices, procedures, and professional judgment employed by Agency or its Contractor to complete the Project. Notwithstanding the foregoing, this Section 12 shall in no way affect the absolute authority of CSXT to prohibit Agency or its Contractors or anyone from entering CSXT's property, or to require the removal of any person from its property, if

it determines, in its sole discretion, that such person is not acting in a safe manner or that actual or potential hazards in, on or about the Project exist.

13. **Entire Agreement** This Agreement embodies the entire understanding of the parties, may not be waived or modified except in a writing signed by authorized representatives of both parties, and supersedes all prior or contemporaneous written or oral understandings, agreements or negotiations regarding its subject matter. In the event of any inconsistency between this Agreement and the Exhibits, the more specific terms of the Exhibits shall be deemed controlling.
 14. **Waiver** If either party fails to enforce its respective rights under this Agreement, or fails to insist upon the performance of the other party's obligations hereunder, such failure shall not be construed as a permanent waiver of any rights or obligations in this Agreement.
 15. **Assignment** CSXT may assign this Agreement and all rights and obligations herein to a successor in interest, parent company, affiliate, or future affiliate. Upon assignment of this Agreement by CSXT and the assumption of CSXT's assignee of CSXT's obligations under this Agreement, CSXT shall have no further obligation under this Agreement. Agency shall not assign its rights or obligations under this Agreement without CSXT's prior consent, which consent may be withheld for any reason.
 16. **Notices** All notices, consents and approvals required or permitted by this Agreement shall be in writing and shall be deemed delivered upon personal delivery, upon the expiration of three (3) days following mailing by first class U.S. mail, or upon the next business day following mailing by a nationally recognized overnight carrier, to the parties at the addresses set forth below, or such other addresses as either party may designate by delivery of prior notice to the other party:

If to CSXT: CSX Transportation, Inc.
500 Water Street, J-301
Jacksonville, Florida 32202
Attention: Director Project Management – Public Projects

If to Agency: Pinellas County, Florida Board of County Commissioners
315 Court Street, Number 501
Clearwater, Florida 33756
Attention: County Engineer

17. **Severability** The parties agree that if any part, term or provision of this Agreement is held to be illegal, unenforceable or in conflict with any applicable federal, state, or local law or regulation, such part, term or provision shall be severable, with the remainder of the Agreement remaining valid and enforceable.

St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. FL2922

18. Applicable Law This Agreement shall be governed by the laws of the State of Florida, exclusive of its choice of law rules. The parties further agree that the venue of all legal and equitable proceedings related to disputes under this Agreement shall be situated in Duval County, Florida, and the parties agree to submit to the personal jurisdiction of any State or Federal court situated in Duval County, Florida.

THE REMAINDER OF THE PAGE IS LEFT INTENTIONALLY BLANK

St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. FL2922

BY SIGNING THIS AGREEMENT, I certify that there have been no changes made to the content of this Agreement since its approval by the CSXT Legal Department on **September 20, 2024**.

IN WITNESS WHEREOF, the parties have caused this Agreement to be executed in duplicate, each by its duly authorized officers, as of the date of this Agreement.

APPROVED AS TO FORM
By: Joseph A Morrissey
Office of the County Attorney



PINELLAS COUNTY, FLORIDA BOARD
OF COUNTY COMMISSIONERS

By: Kathleen Peters
Name: Kathleen Peters
Title: Chair

ATTEST: KEN BURKE, CLERK
By: Douglas Lewis

CSX TRANSPORTATION, INC.

By: Tony C. Bellamy
Tony C. Bellamy
Sr. Director - Design & Construction

EXHIBIT A

ALLOCATION OF WORK

Subject to Section 2.1, work to be performed in connection with the Project is allocated as follows:

- A. Agency shall let by contract to its Contractors:
 1. Construction of all components not related to rail or the crossing surface, which includes but is not limited to all items listed under Exhibit A of this Agreement and what is shown in approved plans under Exhibit B of this Agreement.
 2. Perform all asphalt work, milling, overbuild, and resurface operations, up to the proposed tub-platform crossing surface on both sides of the tracks.
 3. Increase roadway profile elevation approaching crossing heading west to achieve a smooth, continuous transition, while maintaining the existing roadway width.
 4. Installation of Florida Department of Transportation Type F concrete curb and gutter with drop curb approaching crossing surface.
 5. Installation of two (2) new six foot (6'-0") wide concrete sidewalks, on both sides of the roadway.
 6. Installation of detectable warning devices.
 7. Placement of all roadway striping work, including implementation of the dynamic envelope.
 8. Placement of erosion control devices.
 9. Design and implement maintenance of traffic, including placement of maintenance of traffic control devices.
 10. Restore the CSXT right of way to a condition acceptable to CSXT, or CSXT Representative.
 11. Removal of all rubbish and debris from project site.
 12. All roadway work is to be done in accordance with Florida Department of Transportation Roadway Standards 2023-2024, with an emphasis of Florida Department of Transportation Standard Index 830-T01.

B. CSXT shall perform or cause to be performed:

1. Preliminary engineering services.
2. Construction and installation of rail, ties, ballast, and other rail-related components to accommodate a successful crossing surface replacement at 46th Avenue North with Department of Transportation Crossing Inventory Number 626693F, Railroad Milepost Number ARE 894.46.
3. Replace existing asphalt and rail seal crossing surface with a tub-platform at 46th Avenue North with Department of Transportation Crossing Inventory Number 626693F, Railroad Milepost Number ARE 894.46.
4. Removal and disposal of waste materials; Clean-up of the work site at the 46th Avenue North crossing.
5. Crossing circuit detection frequency change to accommodate new tub-platform crossing surface.
6. Any other services, equipment, and components deemed necessary to place crossing in-service in a safe and efficient manner.
7. Flagging services and other protective services and devices, as may be necessary.
8. Construction engineering and inspection to protect the interests of CSXT.
9. All work to be accordance with CSXT MWI 901-08 and CSXT MWI 2539.

St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone: ARE 894.46
 CSXT OP No. FL2922

EXHIBIT B


PLANS AND SPECIFICATIONS

Plans, Specifications and Drawings:


As of the date of this Agreement, the following plans, specifications and drawings have been submitted by Agency to CSXT for its review and approval:

SHEET	DESCRIPTION	PREPARER	DATE
N/A	Proposed Crossing Layout	Alfred Benesch & Co.	03/11/24
01	Key Sheet	Hardesty & Hanover, LLC	01/19/24
02	General Notes	Hardesty & Hanover, LLC	Nov 2023
03	Drainage Map	Hardesty & Hanover, LLC	Nov 2023
04	Typical Sections (1)	Hardesty & Hanover, LLC	Nov 2023
05	Typical Sections (2)	Hardesty & Hanover, LLC	Nov 2023
06	Roadway Plan/Profile (1)	Hardesty & Hanover, LLC	Nov 2023
07	Roadway Plan/Profile (2)	Hardesty & Hanover, LLC	Nov 2023
08	Roadway Plan/Profile (3)	Hardesty & Hanover, LLC	Nov 2023
09	Special Detail	Hardesty & Hanover, LLC	Nov 2023
10	Drainage Structures (1)	Hardesty & Hanover, LLC	Nov 2023
11	Drainage Structures (2)	Hardesty & Hanover, LLC	Nov 2023
12	Cross Sections (1)	Hardesty & Hanover, LLC	Nov 2023
13	Cross Sections (2)	Hardesty & Hanover, LLC	Nov 2023
14	Cross Sections (3)	Hardesty & Hanover, LLC	Nov 2023
15	Cross Sections (4)	Hardesty & Hanover, LLC	Nov 2023
16	SWPPP Notes (1)	Hardesty & Hanover, LLC	Nov 2023
17	SWPPP Notes (2)	Hardesty & Hanover, LLC	Nov 2023
18	TTCP General / Phase Notes	Hardesty & Hanover, LLC	Nov 2023
19	Detour	Hardesty & Hanover, LLC	Nov 2023
20	Signing and Pavement Markings (1)	Hardesty & Hanover, LLC	Nov 2023
21	Signing and Pavement Markings (2)	Hardesty & Hanover, LLC	Nov 2023
22	Signing and Pavement Markings (3)	Hardesty & Hanover, LLC	Nov 2023
23	Utility Adjustment (1)	Hardesty & Hanover, LLC	Nov 2023
24	Utility Adjustment (2)	Hardesty & Hanover, LLC	Nov 2023
25	Utility Adjustment (3)	Hardesty & Hanover, LLC	Nov 2023
26	CSXT Tub Detail	Hardesty & Hanover, LLC	Nov 2023

St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone; ARE 894.46
 CSXT OP No. TBD

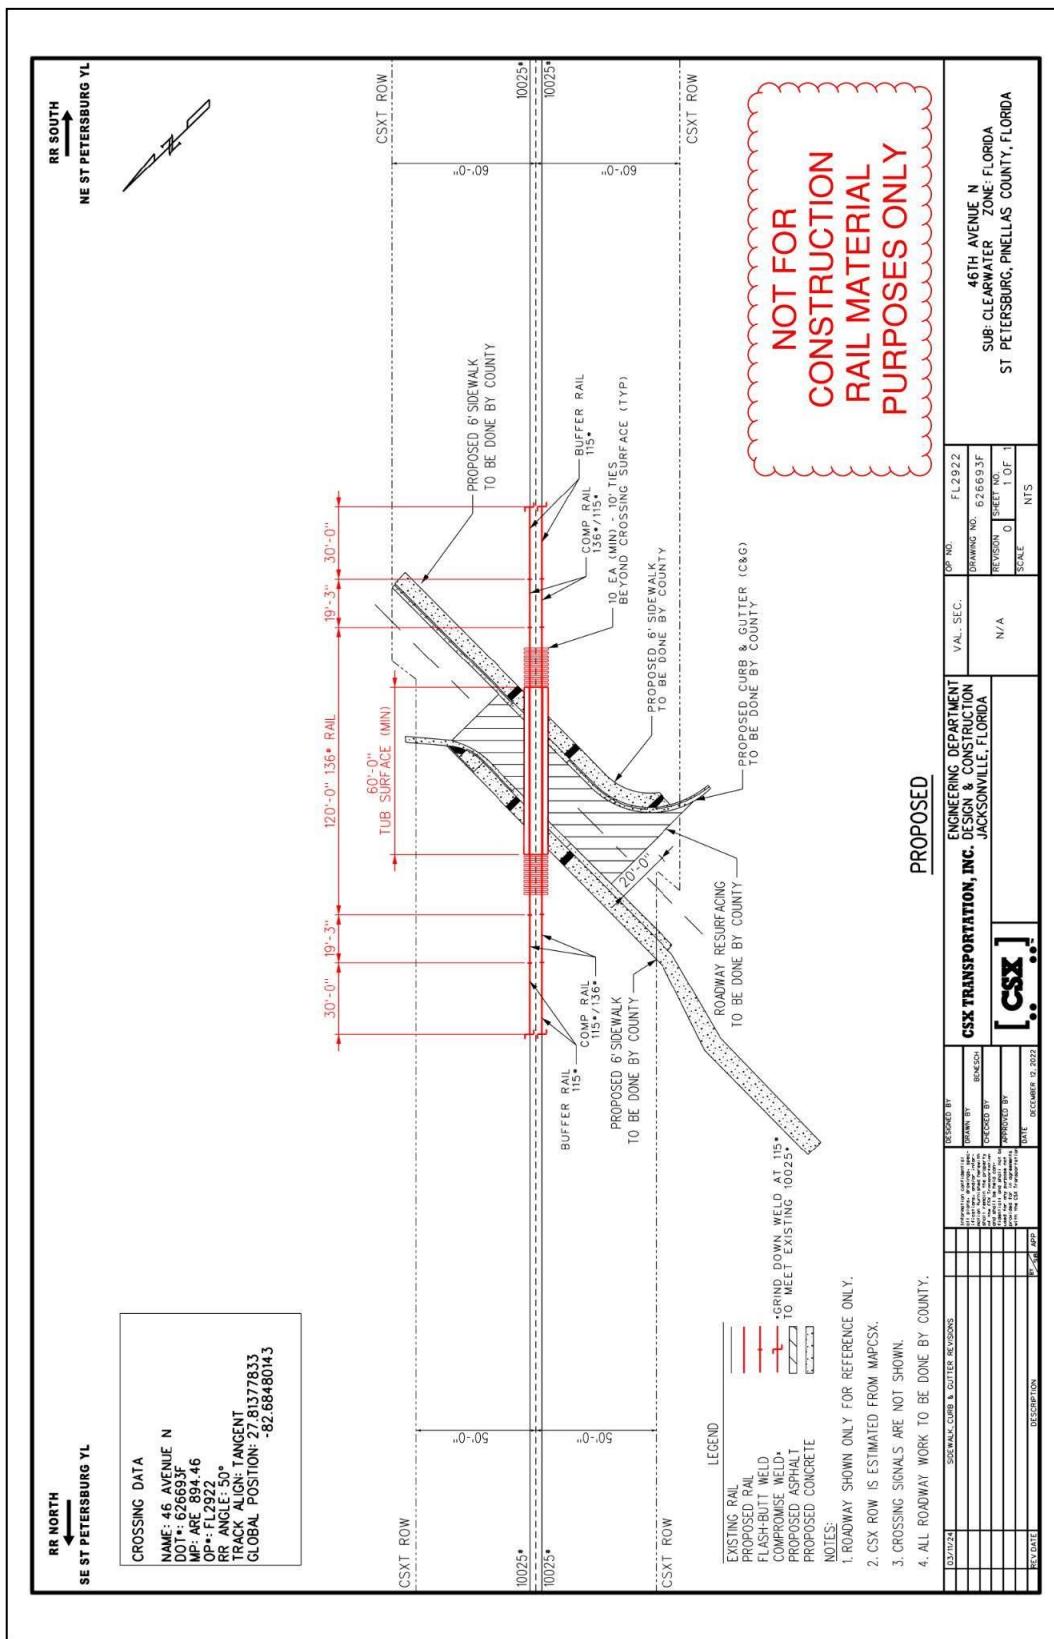


St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone; ARE 894.46
 CSXT OP No. TBD

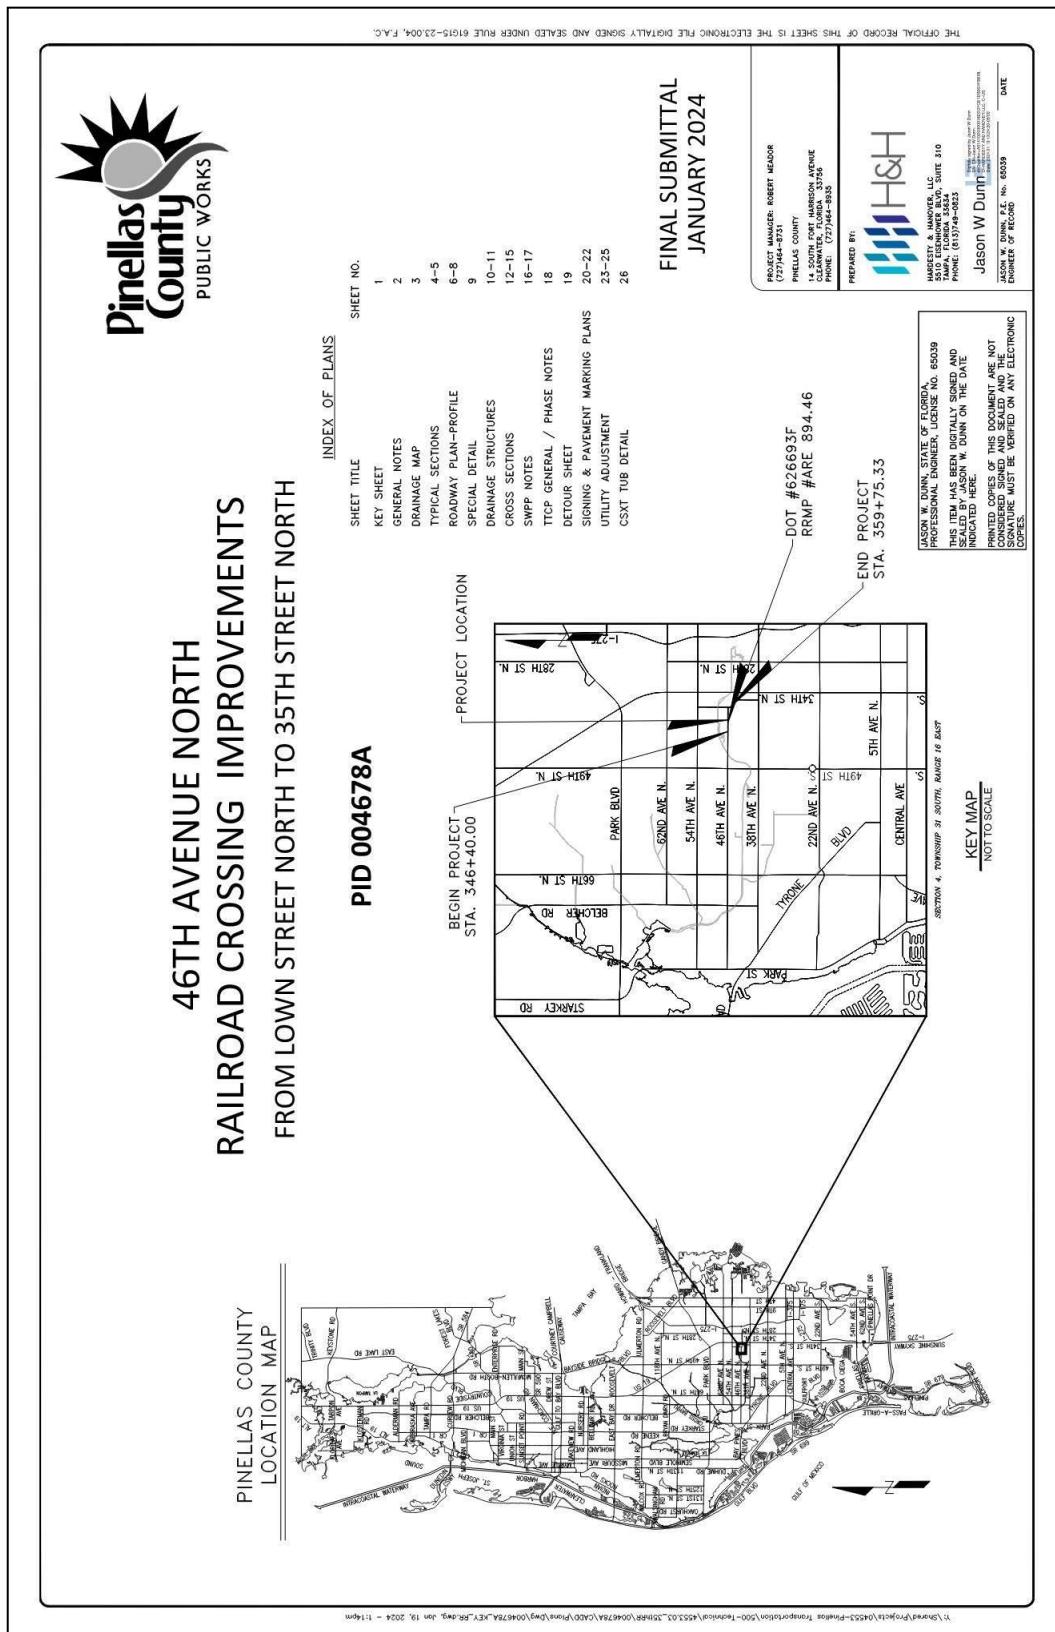


St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone; ARE 894.46
 CSXT OP No. TBD

<small>THE OFFICIAL RECORD OF THIS SHEET IS THE ELECTRONIC FILE DIGITALLY SIGNED AND SEALED UNDER RULE 61G15-23.004, F.A.C.</small>					
1. REMOVE ONLY TREES DESIGNATED FOR REMOVAL IN THE PLAN, OR AS DIRECTED BY AN ENGINEER, OR AS AGREED IN THE MANAGEMENT AGREEMENT. REMOVAL IS INCLUDED IN THE UNIT PRICE BID FOR CLEARING AND GRUBBING, UNLESS SEPARATE PAY TERMS ARE PROVIDED.					
2. ALL MATERIALS NOT CLAIMED BY THE COUNTY MUST BECOME THE PROPERTY OF THE CONTRACTOR AND MUST BE DISPOSED OF BY THE CONTRACTOR IN AREAS PROVIDED BY THE CONTRACTOR, THE COST FOR THIS WORK IS INCLUDED IN THE UNIT PRICE BID FOR CLEARING AND GRUBBING.					
3. ALL STATIONS AND OFFSETS REFER TO CONSTRUCTION BASE LINE, UNLESS OTHERWISE NOTED.					
4. ALL EXISTING PIPES THAT ARE TO REMAIN IN SERVICE WITHIN THE RIGHT-OF-WAY CORRIDOR ARE TO REMAIN IN PLACE, UNLESS OTHERWISE NOTED IN THE PLANS.					
5. STORM DRAIN INLET AND MANHOLE STATION LOCATIONS REFERENCE THE CENTER OF THE SELECTED SHORING LINE BOTTOM.					
6. ALL DISTURBED AREAS, INCLUDING AREAS OUTSIDE THE CONSTRUCTION LIMITS, MUST BE RETURNED TO THEIR PRE-CONSTRUCTION CONDITION AT NO ADDITIONAL EXPENSE TO THE COUNTY, SEDDING MUST NOT BE USED AS A FINAL GRADED SURFACE FINISH, UNLESS OTHERWISE SPECIFICALLY SHOWN IN THE PLANS OR DIRECTED BY THE ENGINEER.					
7. SHEETING, SHORING, AND BRACING MUST BE PROVIDED TO PROTECT ADJACENT STRUCTURES AND UTILITIES, OR TO MINIMIZE TRENCH WIDTH, PROVIDED IN THE UNIT PRICE BID, FOR THE TRENCHES FOR WHICH SHEETING, SHORING, AND BRACING IS REQUIRED, UNLESS OTHERWISE PROVIDED FOR SEPARATELY IN THE BD SUBMITTED SHEETS.					
8. THE ENGINEER MUST RECEIVE PERMISSION FROM THE PROPERTY OWNER THROUGH A RIGHT OF ENTRY AGREEMENT AND/OR A CONSTRUCTION AGREEMENT OR DRAIGNE EASEMENT PRIOR TO ANY GRAVING OR DREDGING BEYOND THE RIGHT-OF-WAY.					
9. ANY AND ALL DESIGN CONDITIONS MUST BE MET, VERIFIED PRIOR TO COMMENCING CONSTRUCTION, THE ENGINEER MUST BE PROMPTLY NOTIFIED OF ANY DISCREPANCIES.					
10. THE LOCATIONS FOR THE UTILITIES SHOWN IN THE PLANS ARE BASED ON THE INFORMATION PROVIDED ON THE PLANS AND SHOULD NOT BE APPROXIMATE ONLY, THE VERIFIED LOCATIONS/ELEVATIONS APPLY ONLY AT THE POINTS SHOWN. INTERPOLATIONS BETWEEN THESE POINTS HAVE NOT BEEN VERIFIED.					
11. SURFACE AND PIPELINE COVERS MUST BE APPLIED TO ANY MANHOLE COVERS, FRAMES, VALVE BOXES, GAS DROPS, ETC.					
12. ALL EXISTING SOILS WITHIN THE PROJECT LIMITS MUST REMAIN UNLESS PROPOSED SIGN LOCATIONS SHOWN ON PLANS ARE APPROPRIATE AND MAY REQUIRE FIELD ADJUSTMENT, AS DIRECTED BY THE ENGINEER.					
13. BLUE, BI-DIRECTIONAL RAMS MUST BE INSTALLED ADJACENT TO ALL FIRE HYDRANTS PLACED PER FOOT TRAFFIC ENGINEERING MANUAL SECTION 4.3 – USE OF BLUE BASED PAVEMENT MARKERS TO IDENTIFY FIRE HYDRANTS.					
14. ABOVE GROUND AND/ OR UNDERGROUND UTILITIES MAY BE IN THE AREA OF THIS PROJECT – PROVIDED WITH CAUTION CALL “SUNSHINE 811” IN ADVANCE OF BEGINNING WORK, IN ACCORDANCE WITH CHAPTER 565, FLORIDA STATUTES, UNDERGROUND FACILITY DAMAGE PREVENTION & SAFETY ACT. ALL UTILITY OWNERS MAY NOT BE A MEMBER, REQUIRING PROTECTION BY THE CONTRACTOR.					
15. THE RESPONSIBLE UTILITY OWNER MUST BE NOTIFIED FOR LOCATION OF METER BOXES FOR PORTABLE AND NON-PORTABLE WATER SERVICE.					
16. ELEVATIONS SHOWN ON THE PLANS ARE BASED ON THE FLORIDA STATE PLANE COORDINATION SYSTEM ZONE 811 (NAD 83) (NAD 27) (NAD 83) (NORTH AMERICAN VERTICAL Datum of 1980 (NAVD 88))					
17. THE CONTRACTOR SHALL NOT STORE EQUIPMENT OR MATERIALS OF ANY KIND ON CSXT RIGHT-OF-WAY (ROW), OR WHERE THEY MAY HAVE THE POTENTIAL TO INFILTRATE INTO CSXT OPERATIONS UNLESS CONTRACTOR ADVISED TO WRITER AUTHORIZATION BY CSXT REPRESENTATIVE.					
18. COORDINATE ALL RAILROAD ACTIVITIES THROUGH PINELAS COUNTY (RAILROAD) ENGINEER, AT 727-464-9751 (PINELAS COUNTY)					
19. BASED ON THE PROJECT SCOPE, CSXT WILL DETERMINE THE LEVEL OF IMPACTS TO CSXT ROW IN TERMEDIATE WILDERNESS ROW WITH PROTECTION TO CSXT ROW IS TERMINATED WITHOUT SIDE ROAD/RW WITH PROTECTION.					
20. UNDER NO CONDITIONS SHALL WORK AFFECT THE SAFE PASSAGE OF CONTRACTOR AND ALL SUBCONTRACTORS (IF APPLICABLE) SHALL PRODUCE AND MAINTAIN RAILROAD PROTECTIVE LIABILITY INSURANCE AND POLICY OF INSURANCE BEFORE ACCESSING CSXT RIGHT-OF-WAY (ROW).					
21. CONTRACTOR SHALL REFER TO THE CSXT PUBLIC PROJECTS MANUAL, MOST RECENT EDITION, OR INSTRUCTION REQUIREMENTS WHILE WITHIN THE CSXT RIGHT-OF-WAY (ROW).					
22. CONTRACTOR SHALL REFER TO THE CSXT PUBLIC PROJECTS MANUAL, MOST RECENT EDITION, OR INSTRUCTION REQUIREMENTS WHILE WITHIN THE CSXT RIGHT-OF-WAY (ROW).					
23. CONTRACTORS MUST HAVE AN EMERGENCY ACTION AND HURRICANE SITE PREPAREDNESS PLAN AND MEET CSXT REQUIREMENTS. CONTRACTORS AND THEIR EMPLOYEES MUST NOT WORK WITHIN CSXT ROW WHILE WORKING WITHIN THE CSXT ROW LIMITS. THESE PLANS MUST BE PROVIDED TO CSXT FOR REVIEW AND ACCEPTANCE PRIOR TO WORK COMMENCING WHICH MAY IMPACT CSXT RIGHT-OF-WAY (ROW).					
24. AGENCY AND CONTRACTOR ARE NOT PERMITTED TO CROSS CSXT PROPERTY OR TRACKS, EXCEPT ON EXISTING PUBLIC ROAD CROSSINGS, WITH VEHICLES, MEN, OR EQUIPMENT OF ANY KIND WITHOUT PRIOR AUTHORIZATION FROM CSXT OR CSXT AUTHORIZED REPRESENTATIVE.					
25. IF ANY ISSUE OR INCIDENT OCCURS WITHIN CSXT RIGHT-OF-WAY (ROW), CONTRACTOR MUST CONTACT THE CSXT PUBLIC SAFETY COORDINATOR, CENTER 800-222-01 AND NOTIFY CSXT PUBLIC SAFETY.					
26. “TONE CALL” SERVICES DO NOT LOCATE BURIED RAILROAD SIGNAL AND COMMANDS LINES. THE CONTRACTOR SHALL CONTACT THE RAILROAD SIGNAL AND COMMANDS LINES, INC. (RCI) TO REQUEST LOCATIONS OF THESE LINES. RCI WILL PROVIDE LOCATIONS OF THESE LINES. CONTRACTOR SHALL NOTIFY RCI OF EXCAVATION PLANS ON HEAVY DUTY, MAIN DAMAGE, RAILROAD UNDERGROUND LINES ON RAILROAD PROPERTY. UPON REQUEST FROM CONTRACTOR OR AGENCY, RAILROAD SIGNALS FORCES WILL LOCATE AND PAINT MARK ON FLAG RAILROAD UNDERGROUND SIGNALS. CONTRACTOR MUST NOTIFY RCI OF EXCAVATION PLANS TO AVOID DISTURBANCE OF THESE LINES WHICH ARE CRITICAL TO CONTRACTOR, THE SAFETY OF THE RAILROAD AND THE PUBLIC. IF DISTURBANCE OR EXCAVATION IS REQUIRED NEAR A BURIED RAILROAD SIGNAL, CONTRACTOR MUST CALL RCI AND EXCAVATION SHALL BE CONDUCTED MANUALLY AND CAREFULLY, AND CONTRACTOR SHALL NOTIFY RCI OF EXCAVATION PLANS. CONTRACTOR SHALL NOT DISTURB OR DAMAGE THE COURSE OF THE RAILROAD SIGNALS. CONTRACTOR SHALL NOT DISTURB UNDER THE SUPERVISION AND DIRECTION OF A RAILROAD SIGNAL REPRESENTATIVE.					
27. ALL SOILS EXCAVATED WITHIN CSXT'S RAILROAD RIGHT-OF-WAY (ROW), SHALL REMAIN ON CSXT'S ROW, TESTING OF SOILS ON CSXT ROW IS PROHIBITED WITHOUT PRIOR WRITTEN CSXT AUTHORIZATION, ANY SOILS EXCAVATED ON CSXT ROW CAN BE REUSED ON THE ROW PROVIDED					
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.
REV. NO./DATE	DESCRIPTION	GENERAL NOTES	PROJECT #	ENGINEER OF RECORD	DATE
KEY	REV.	NAME	PHONE NUMBER	TITLE	PROJECT NO.


St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone; ARE 894.46
 CSXT OP No. TBD

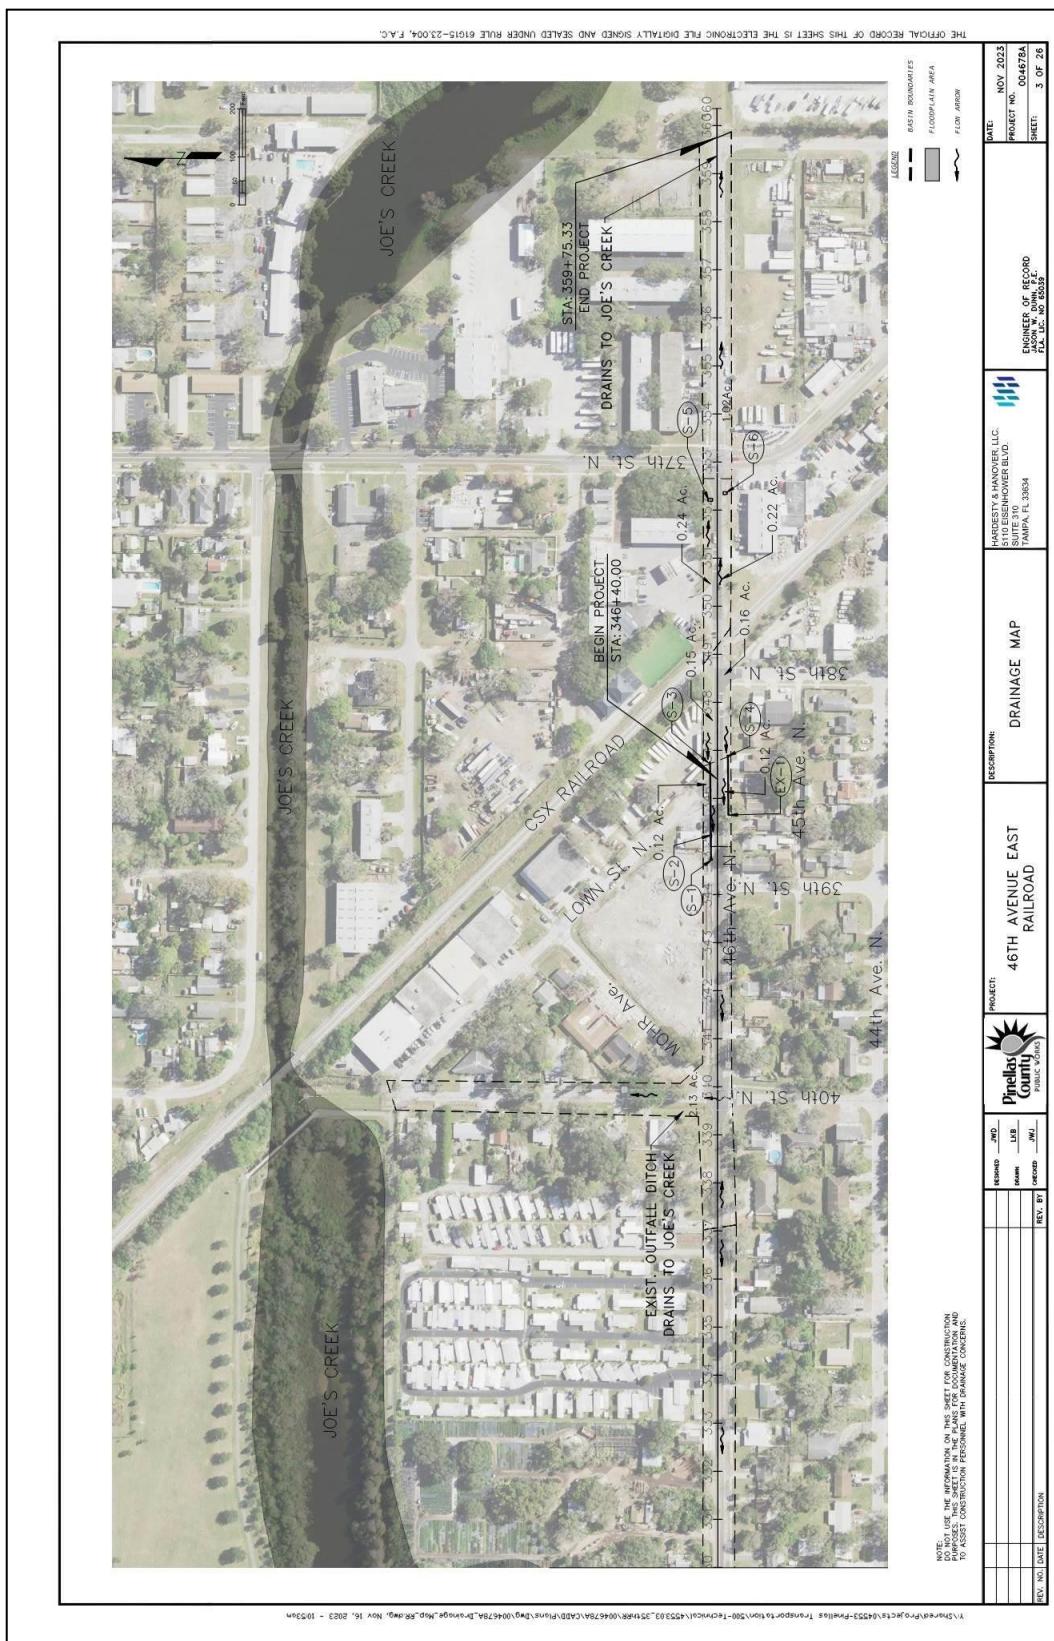


St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. TBD

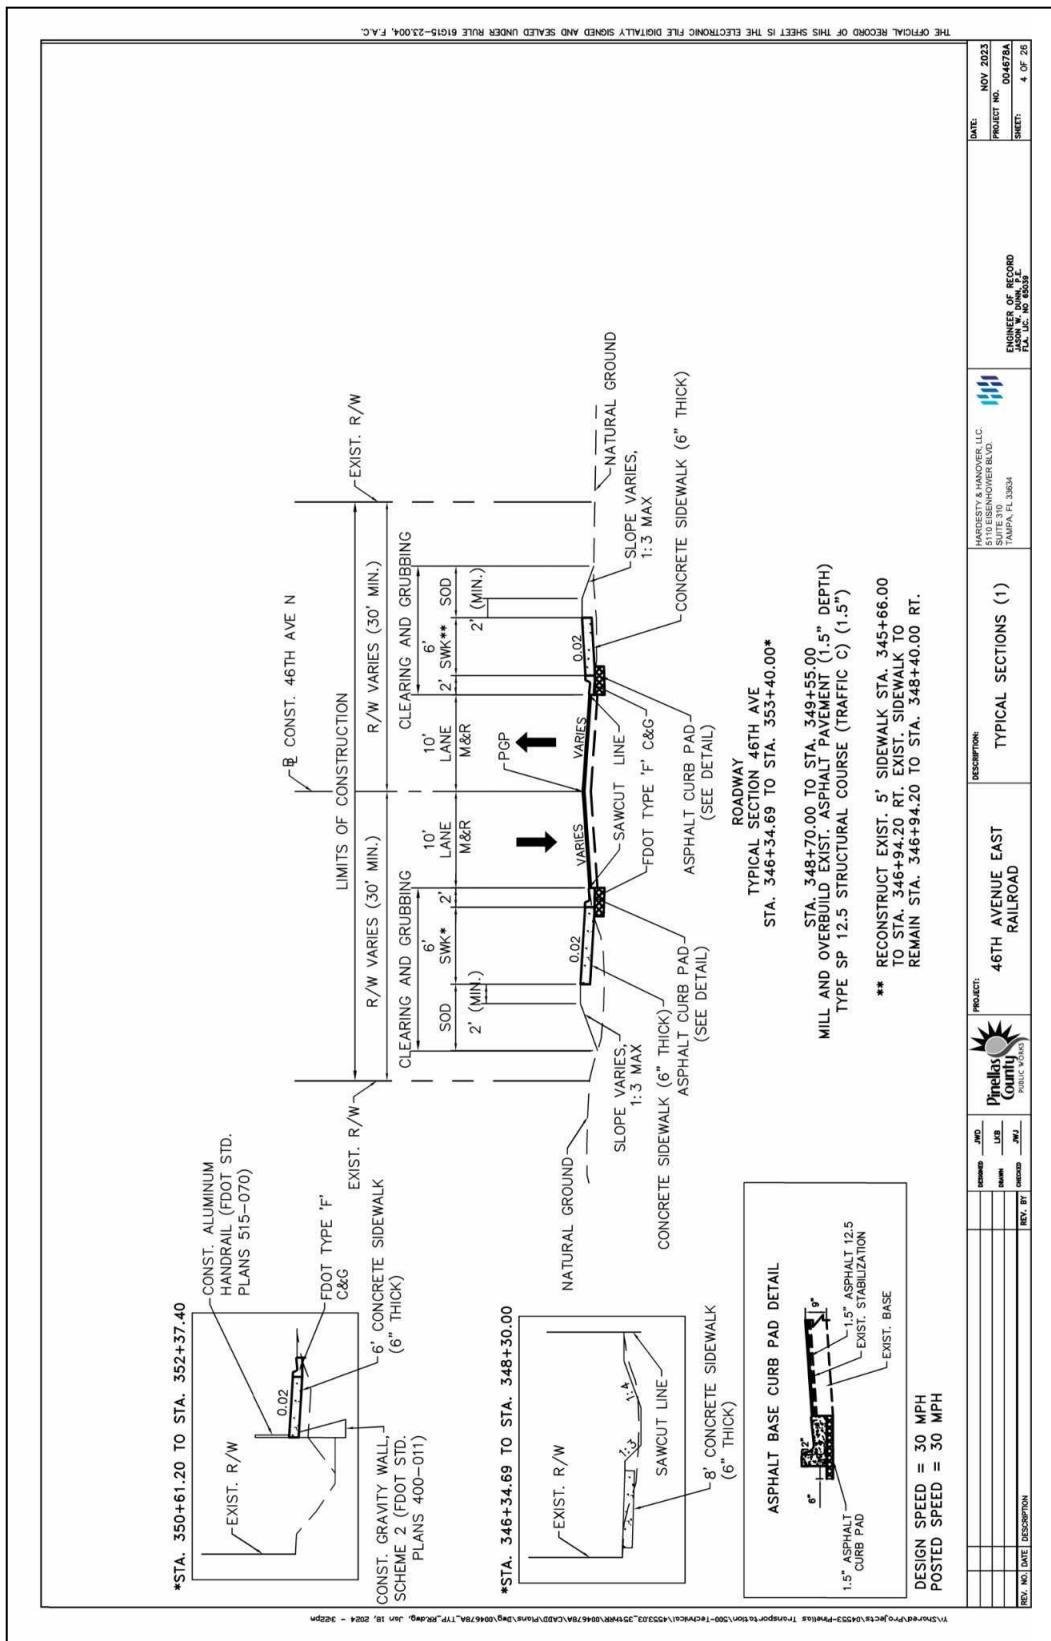


St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone; ARE 894.46
 CSXT OP No. TBD

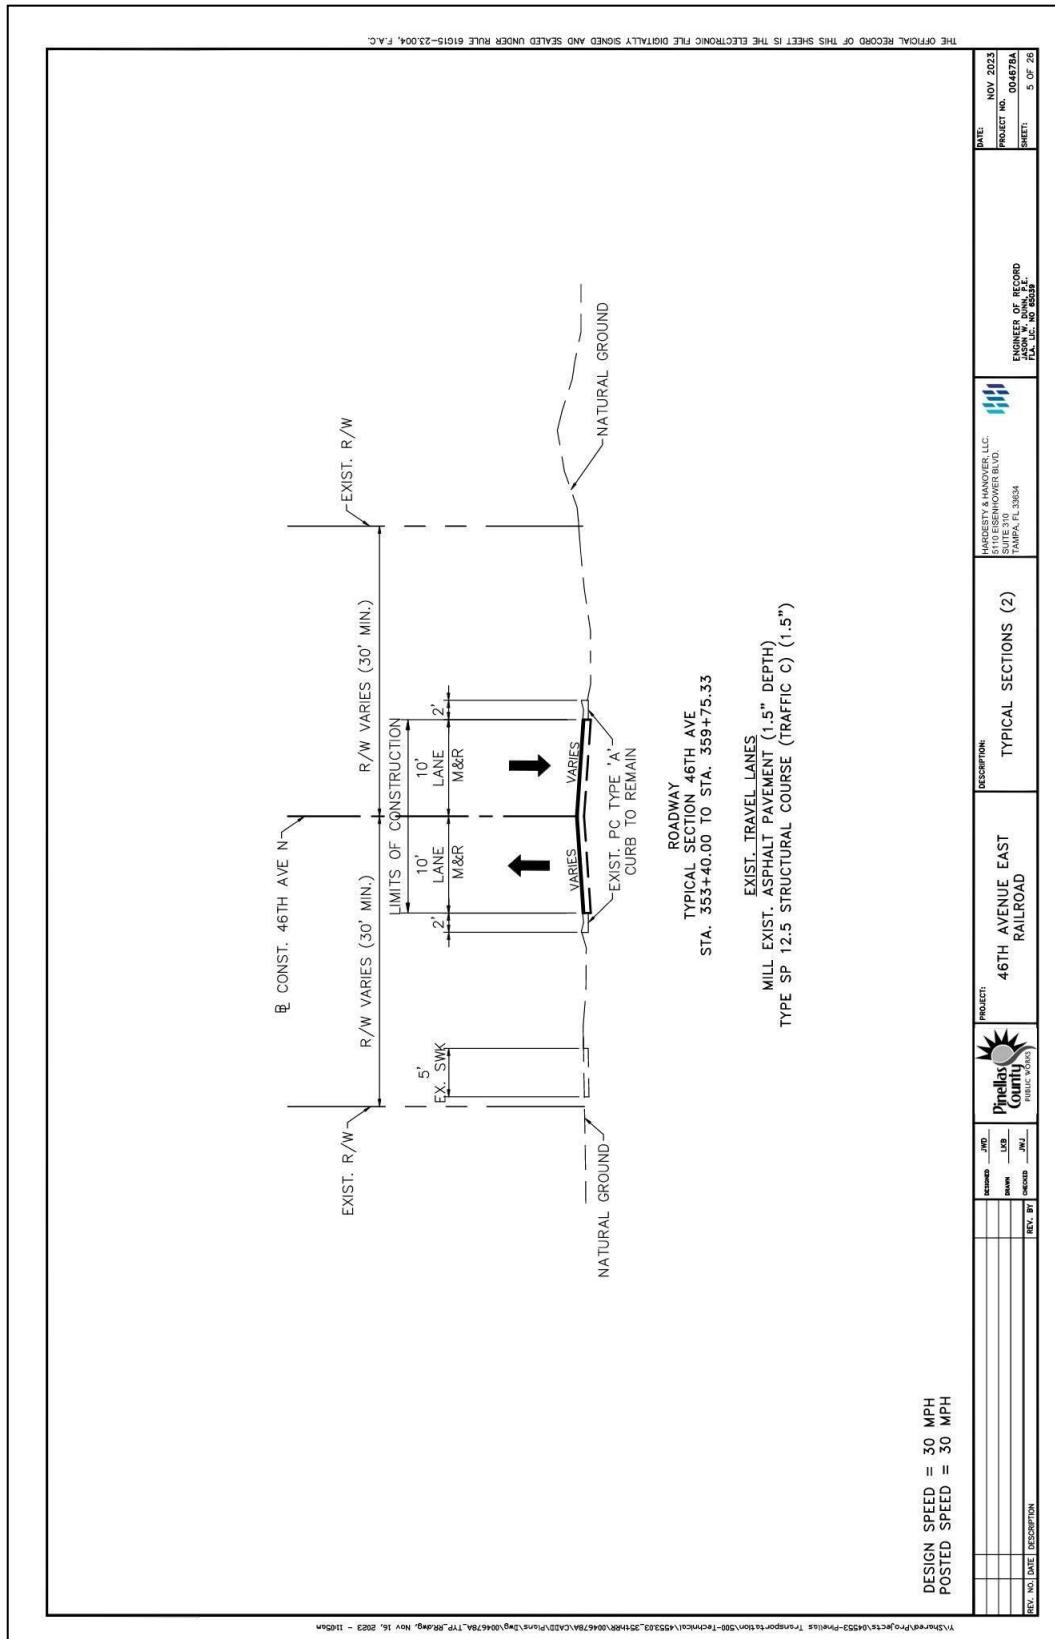


St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. TBD

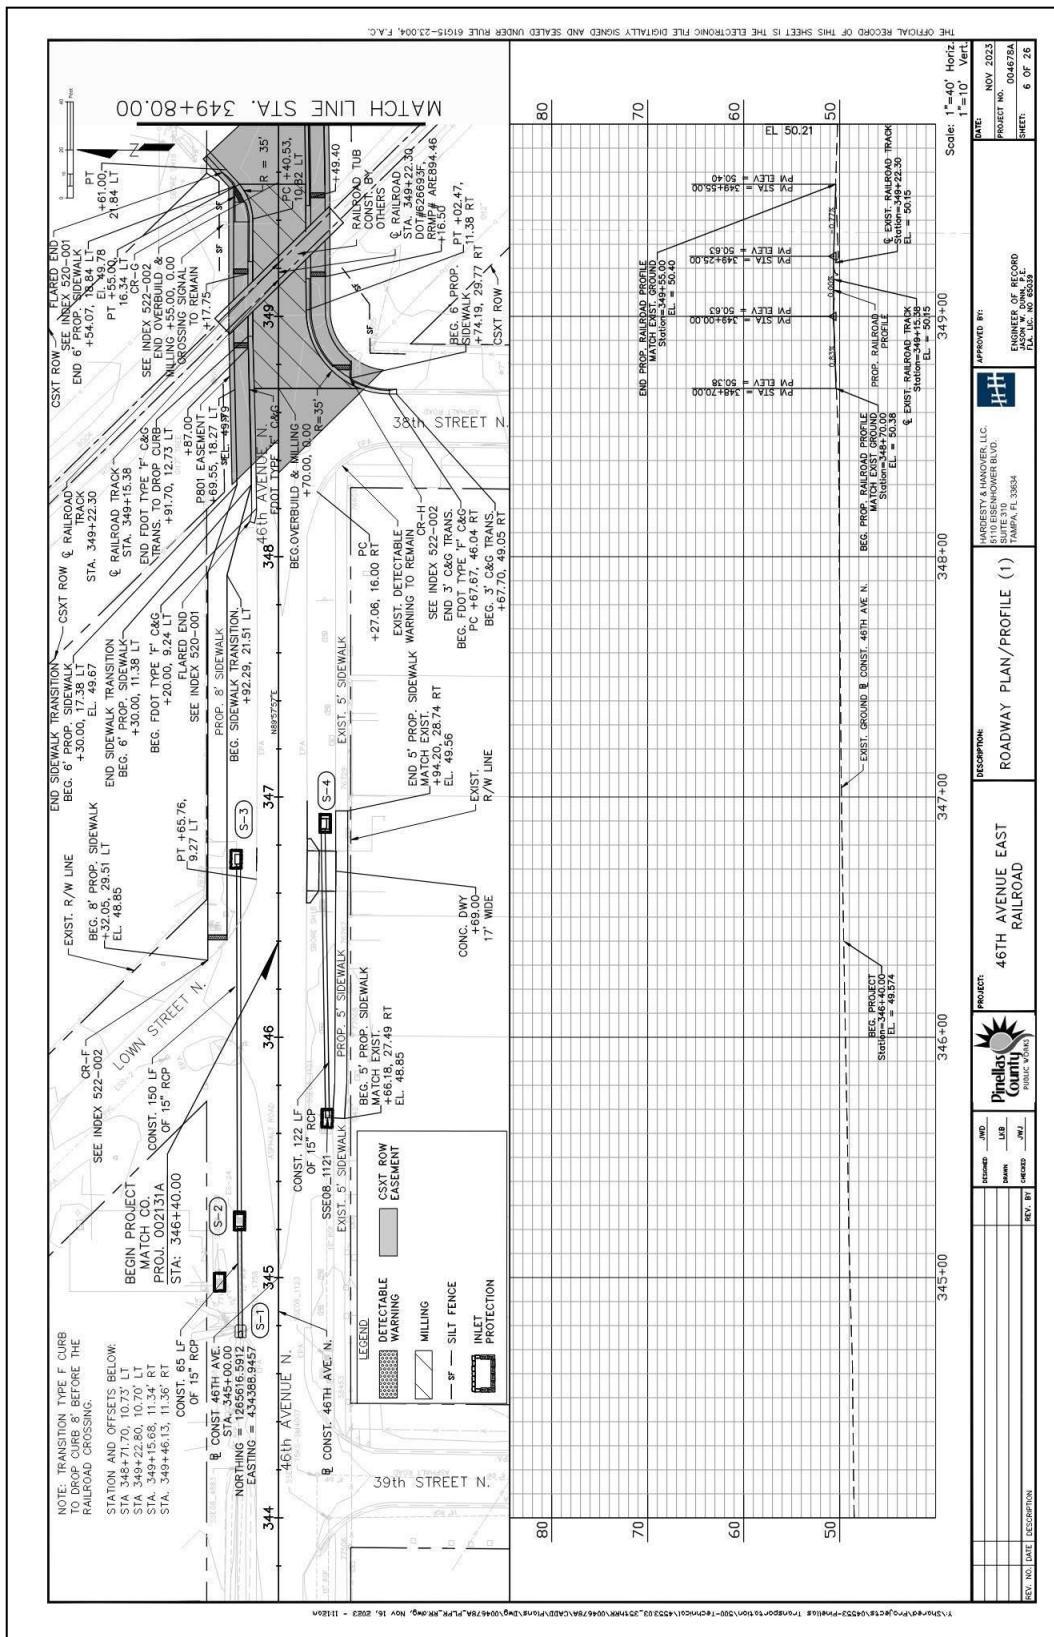


St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. TBD

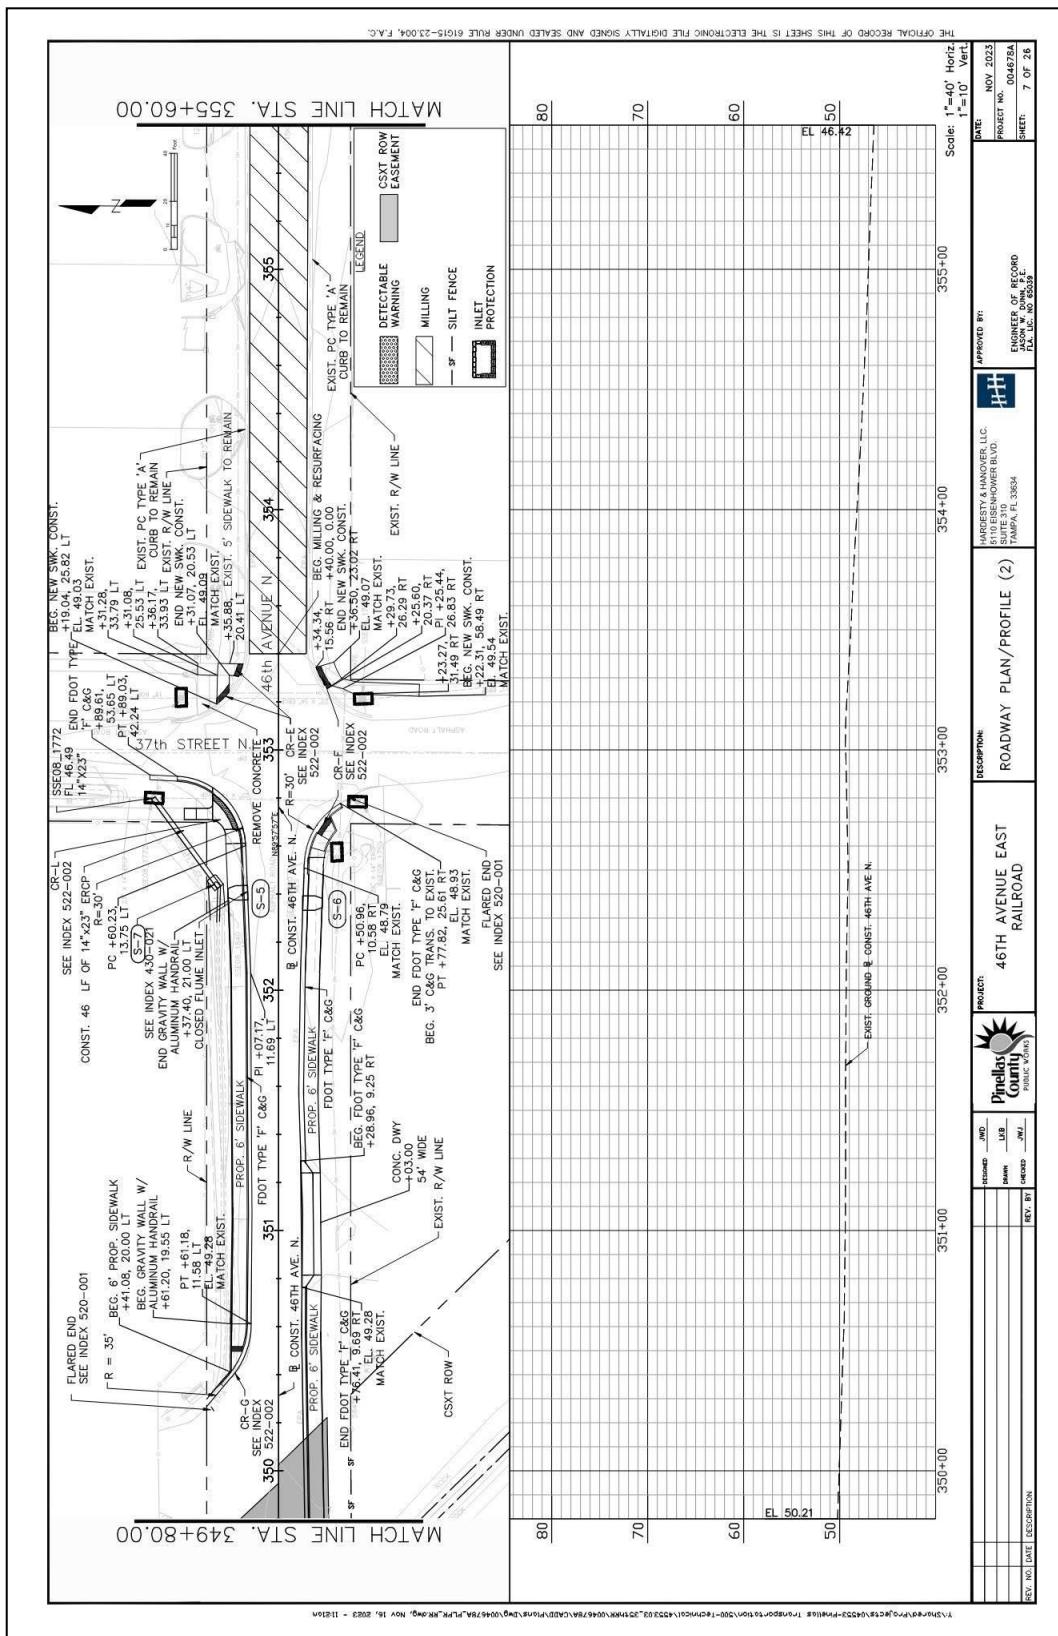


St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone; ARE 894.46
 CSXT OP No. TBD

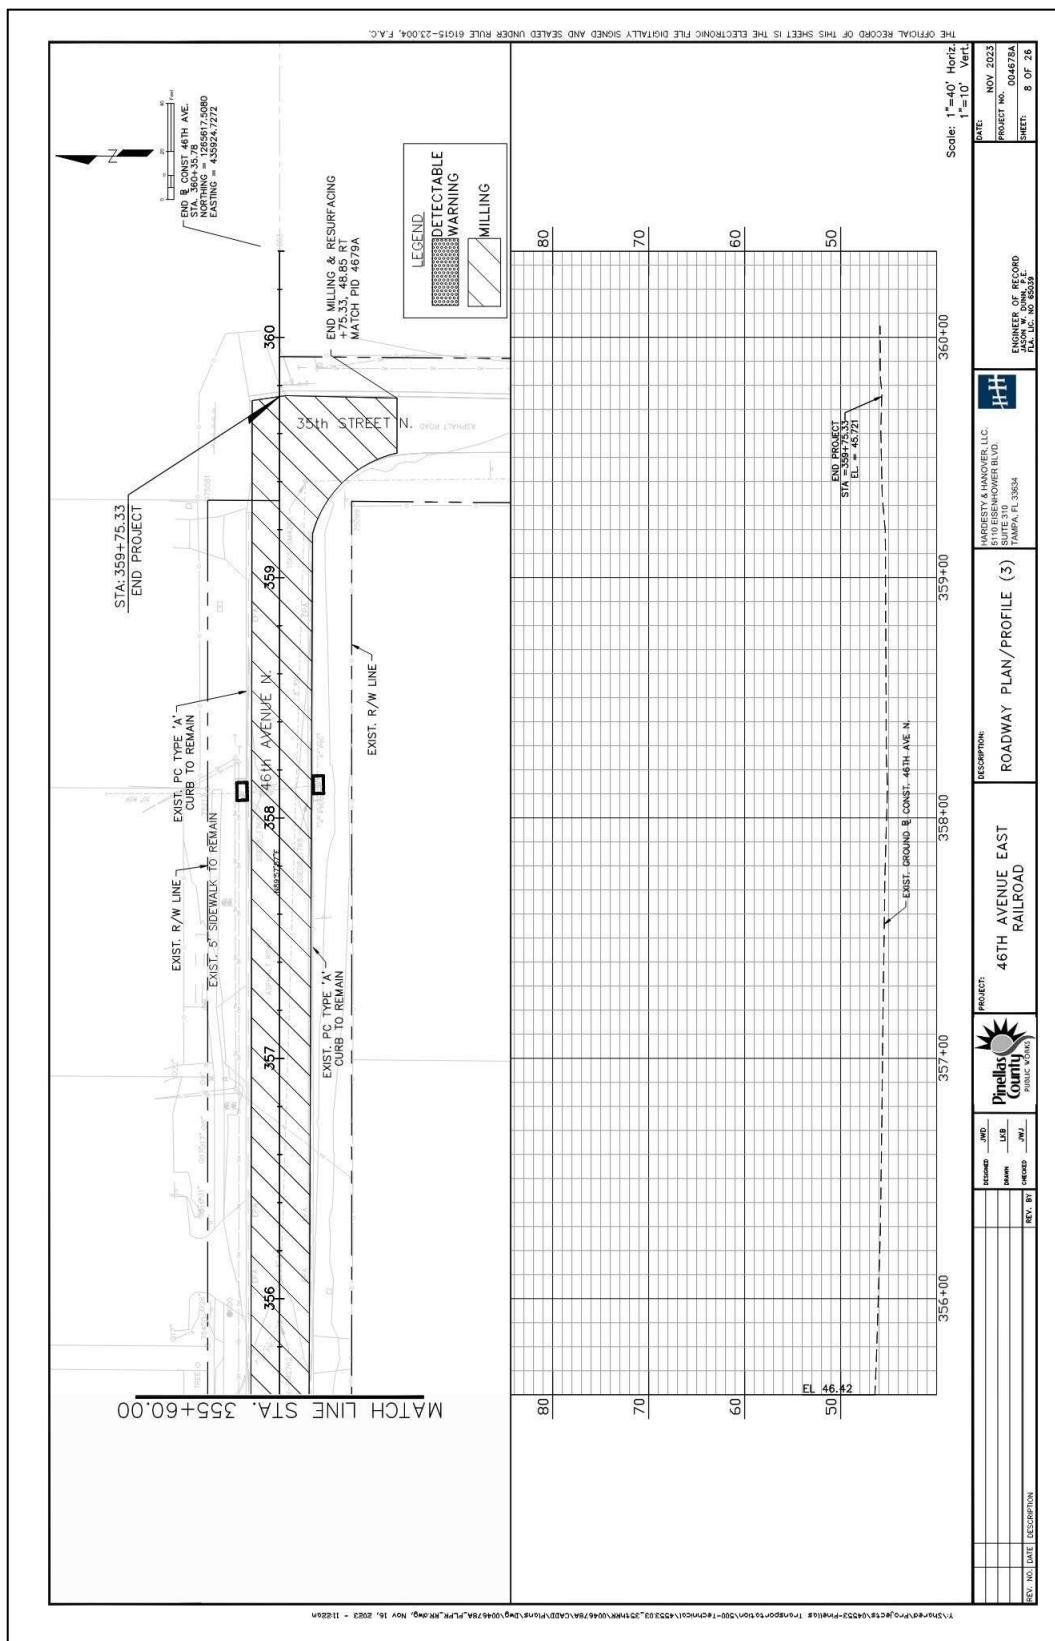


St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. TBD

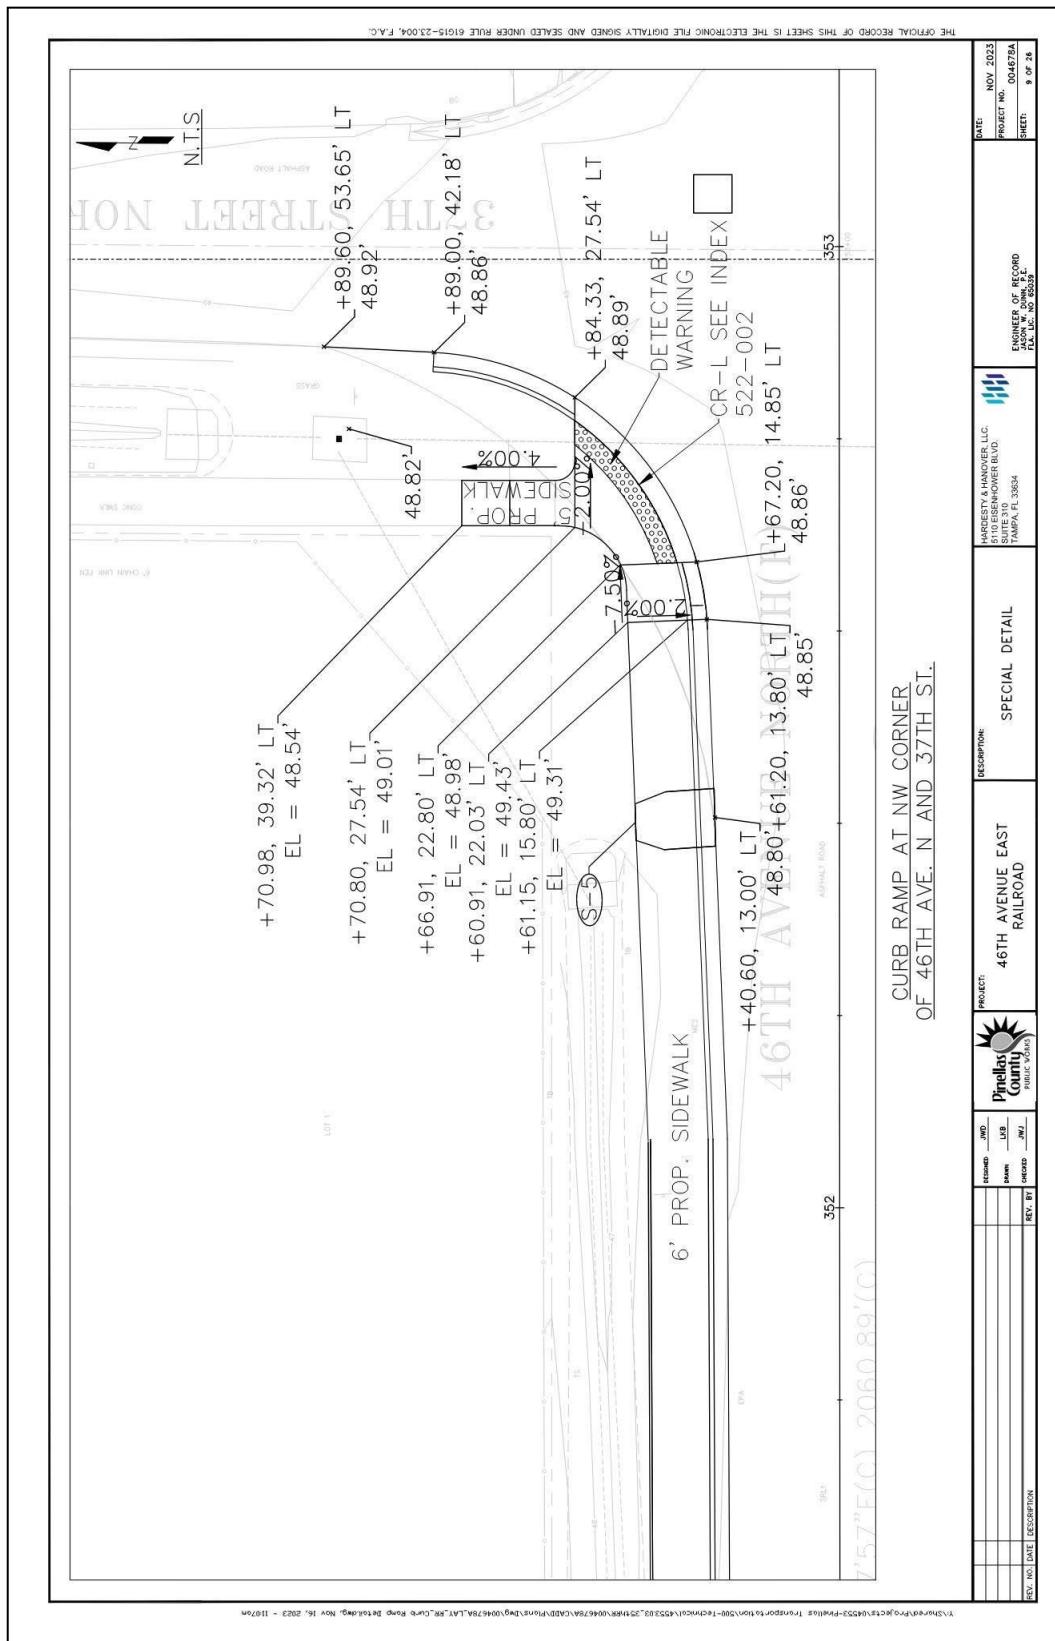


St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. TBD

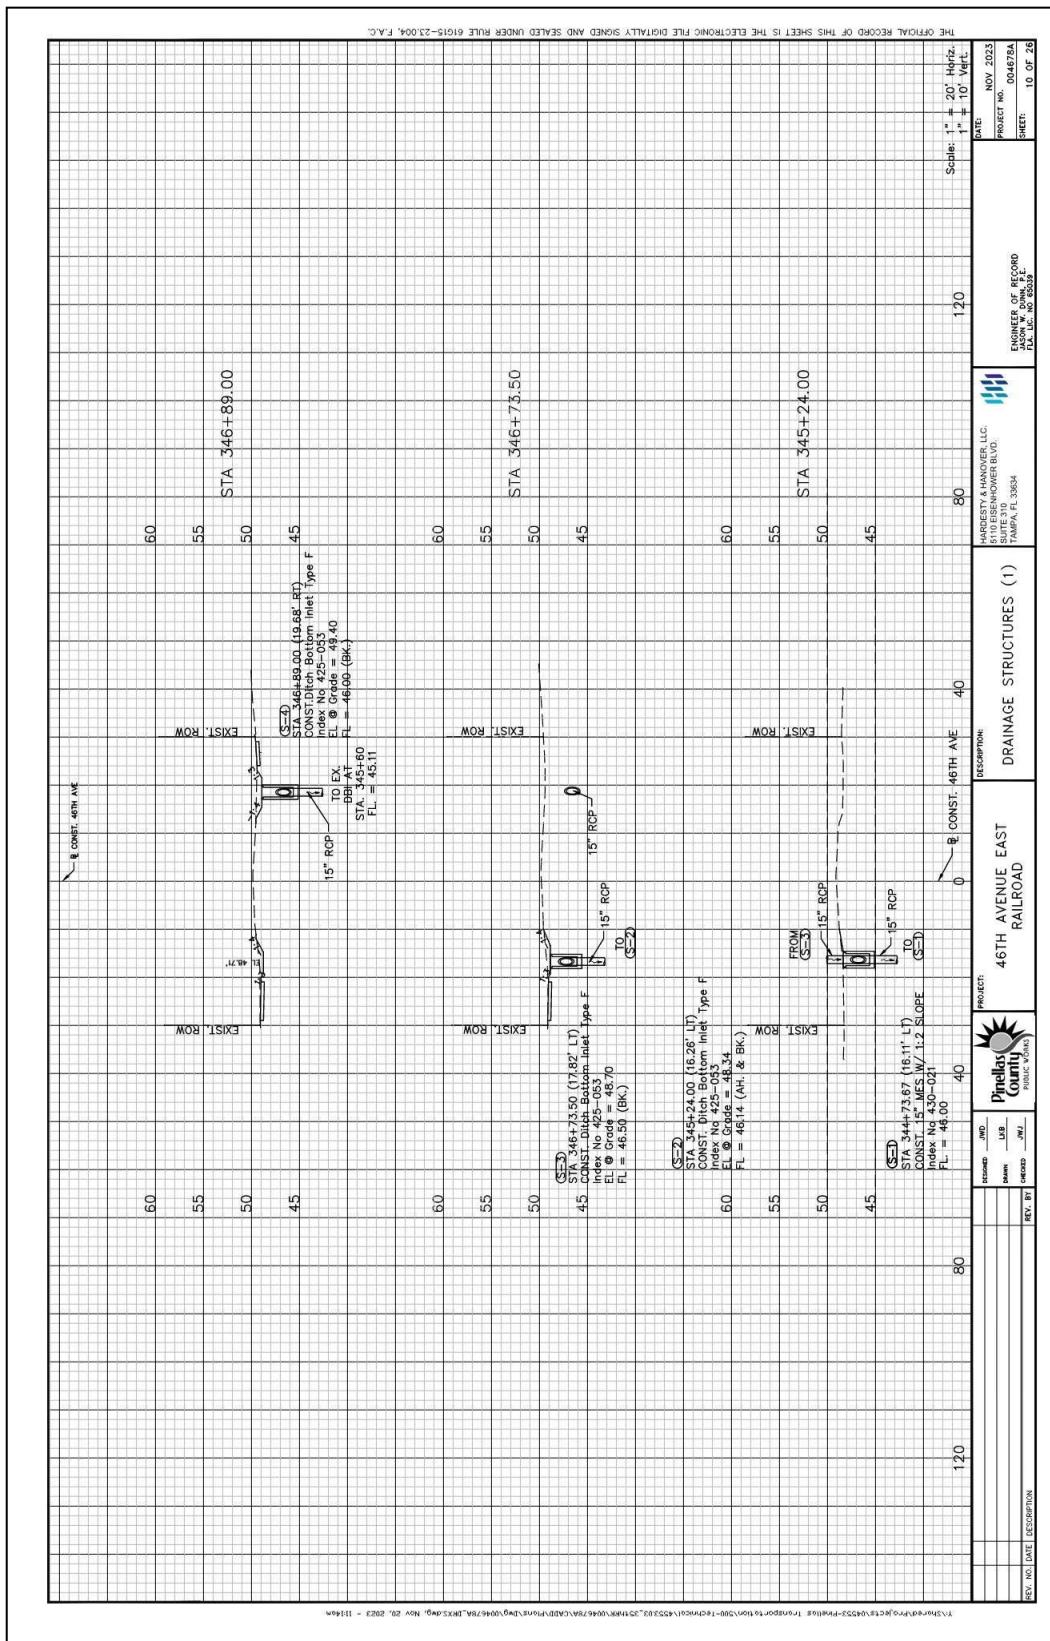


St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone; ARE 894.46
 CSXT OP No. TBD

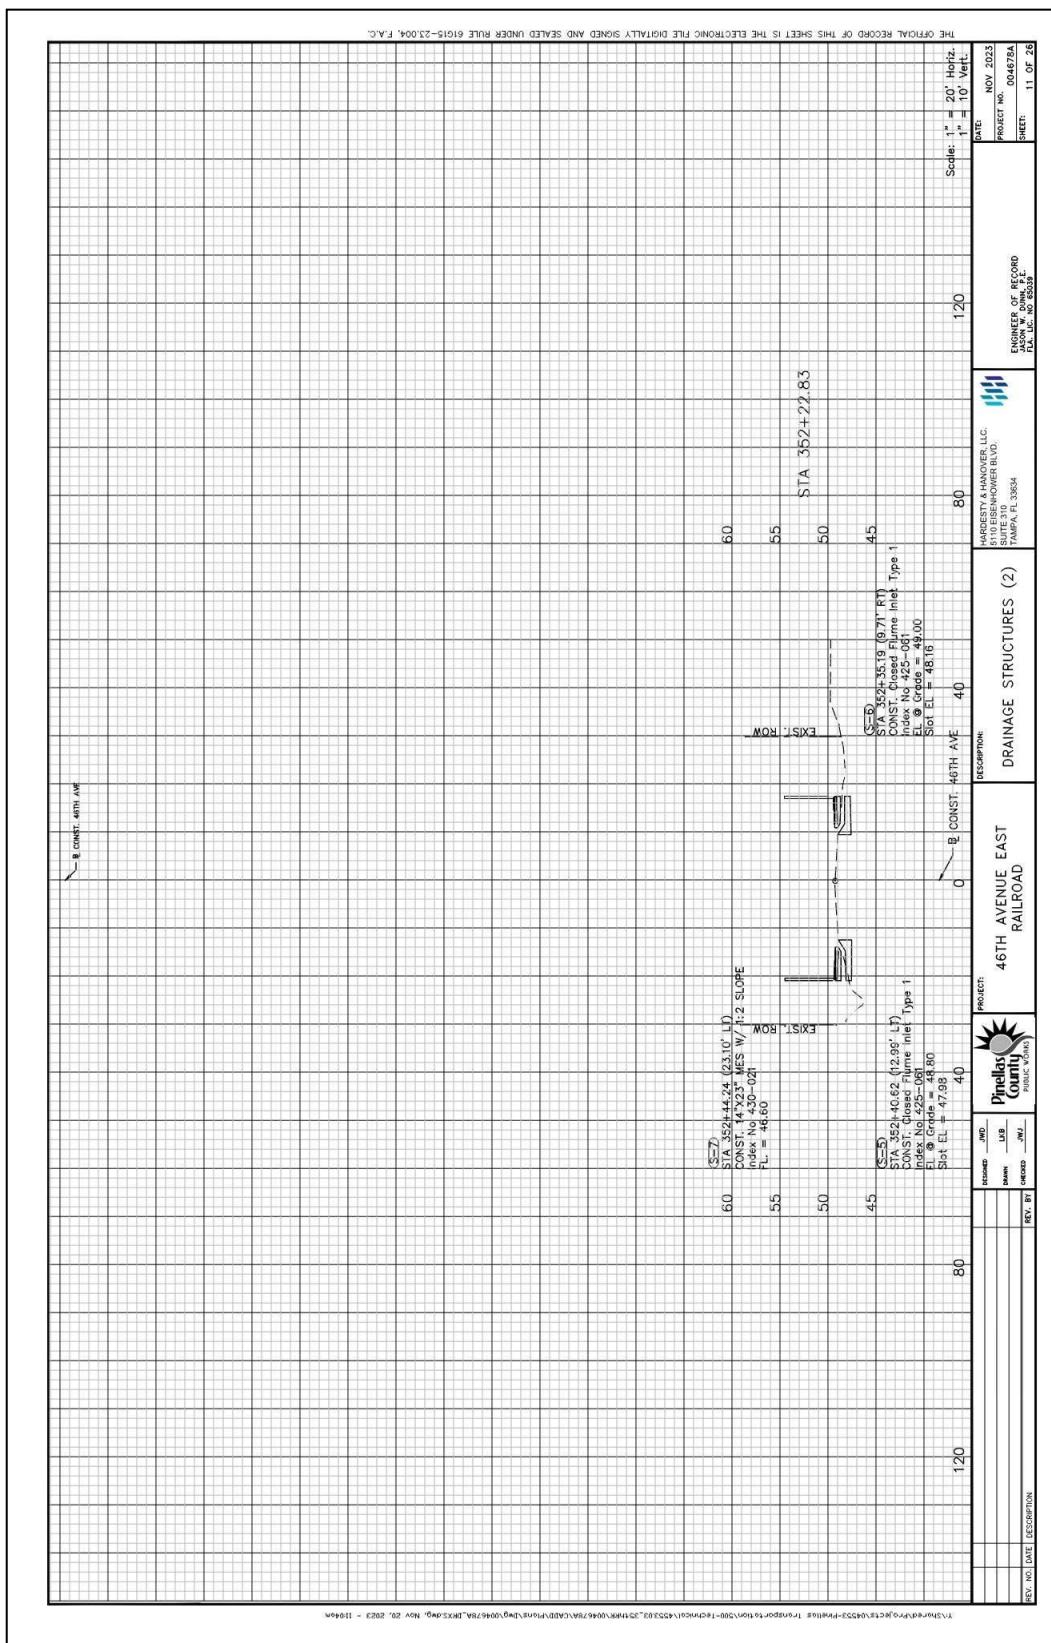


St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. TBD

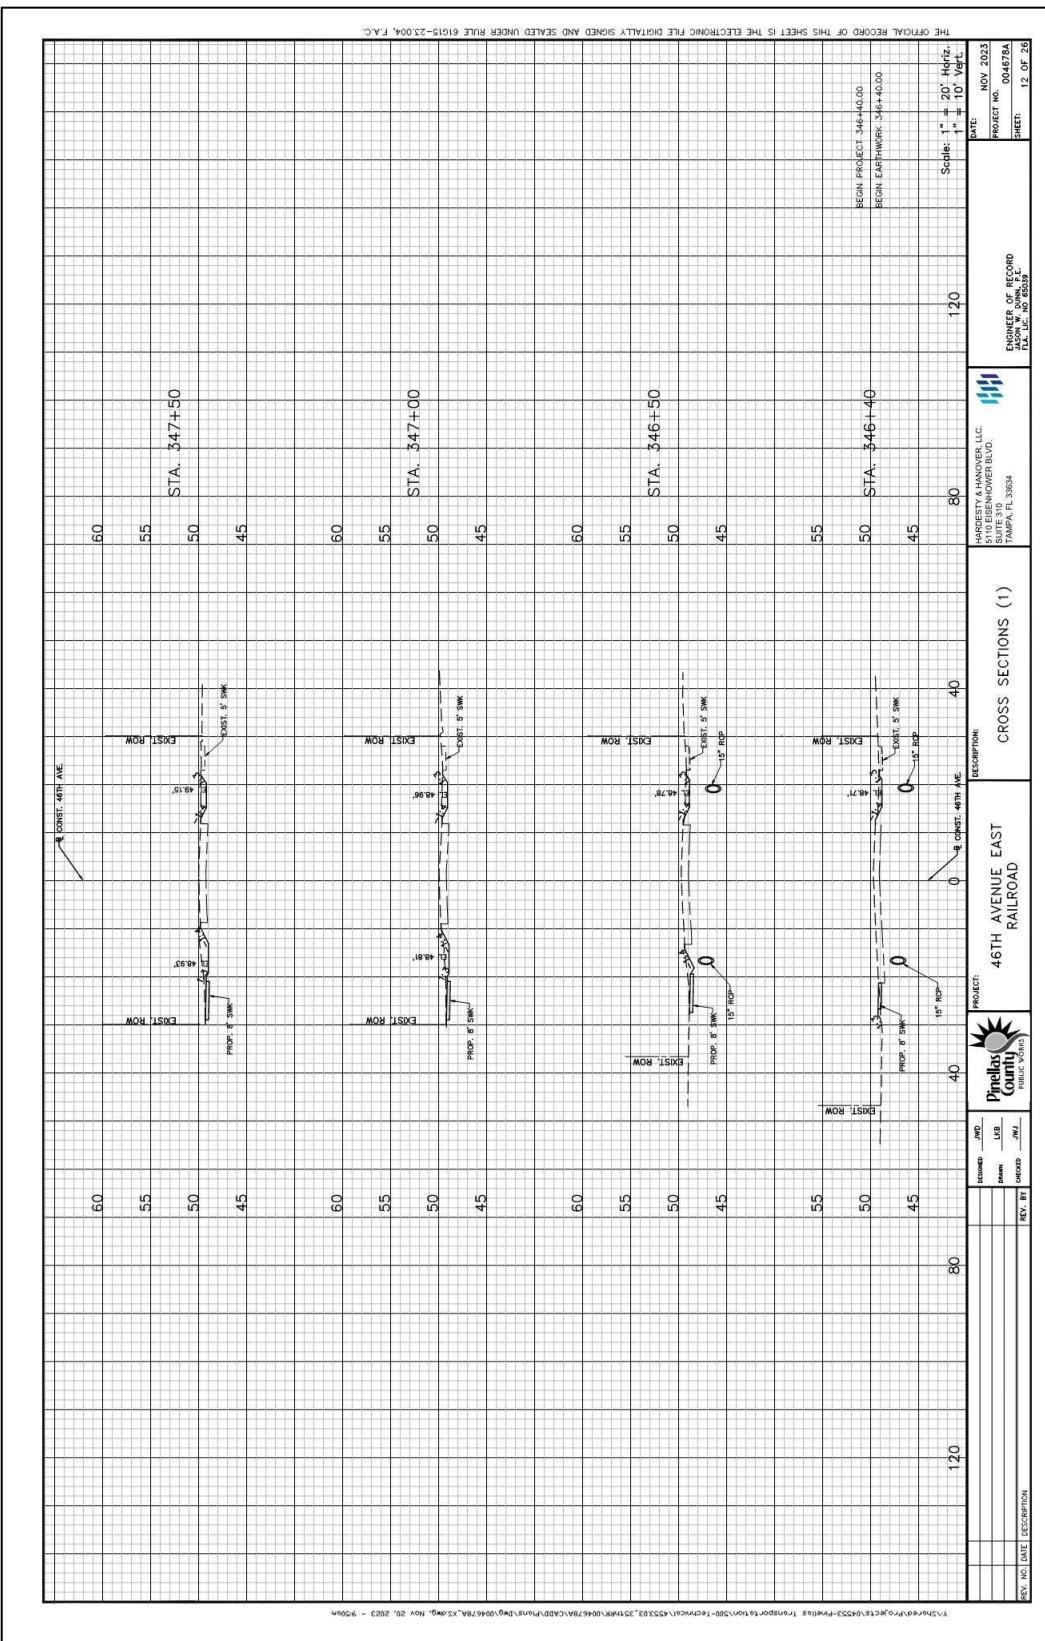


St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone; ARE 894.46
 CSXT OP No. TBD

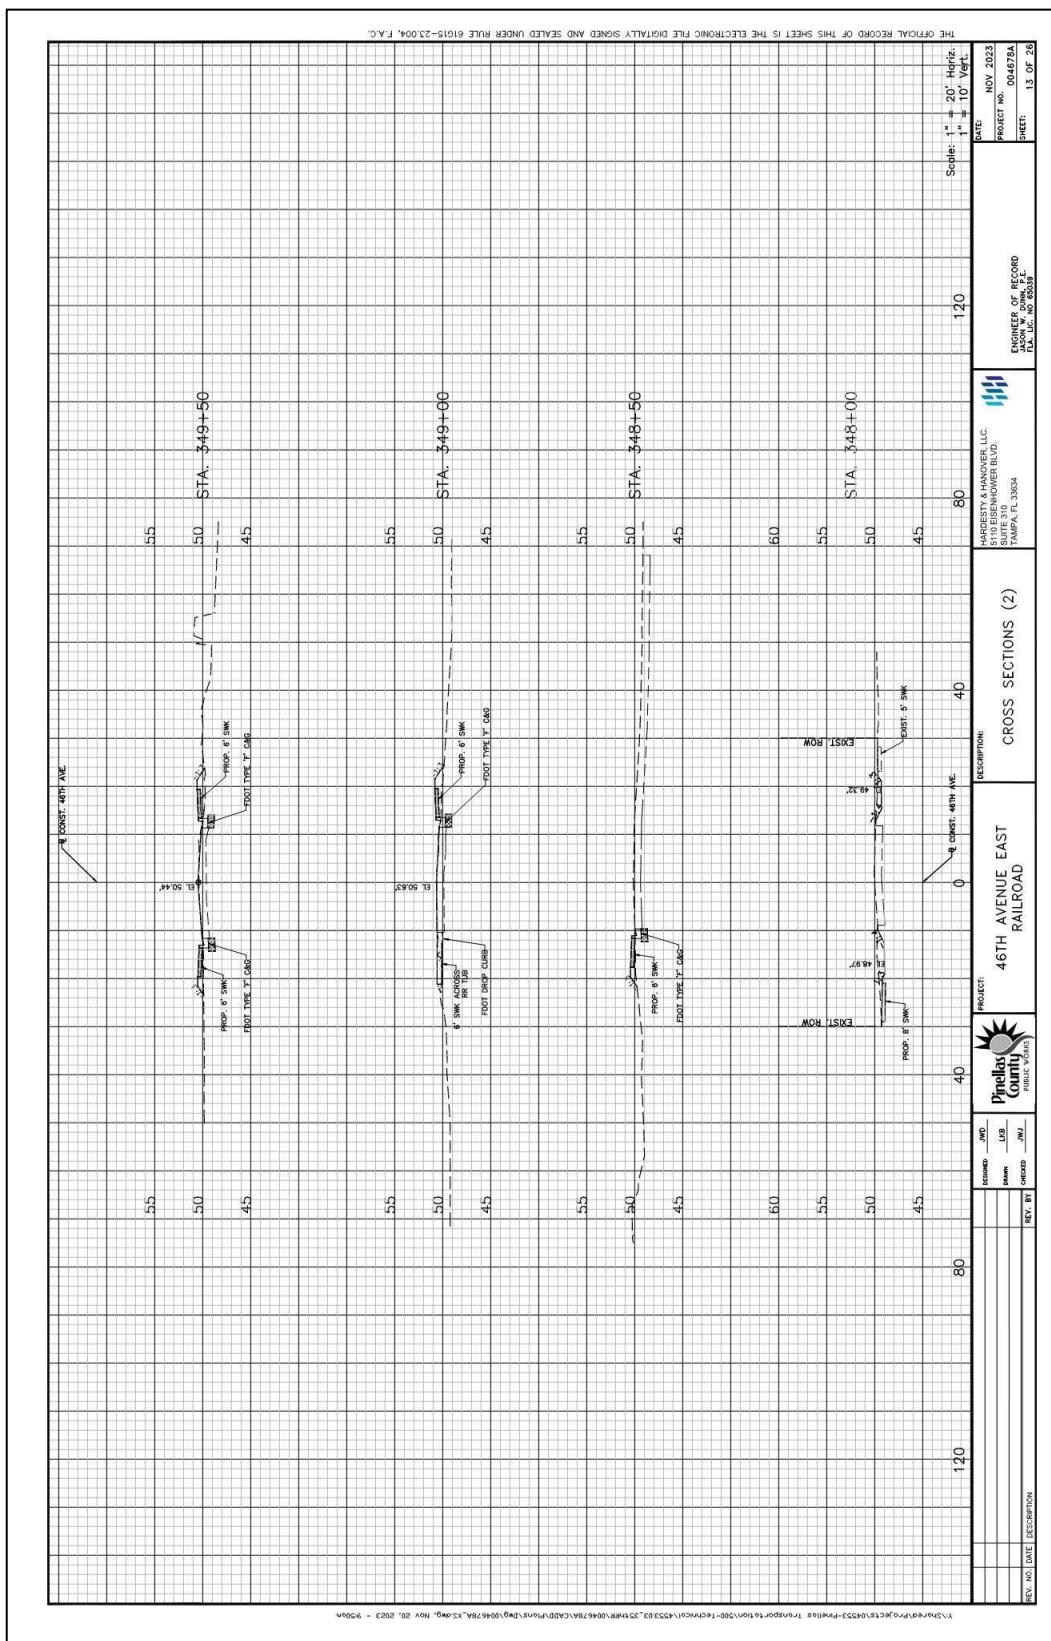

St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. TBD

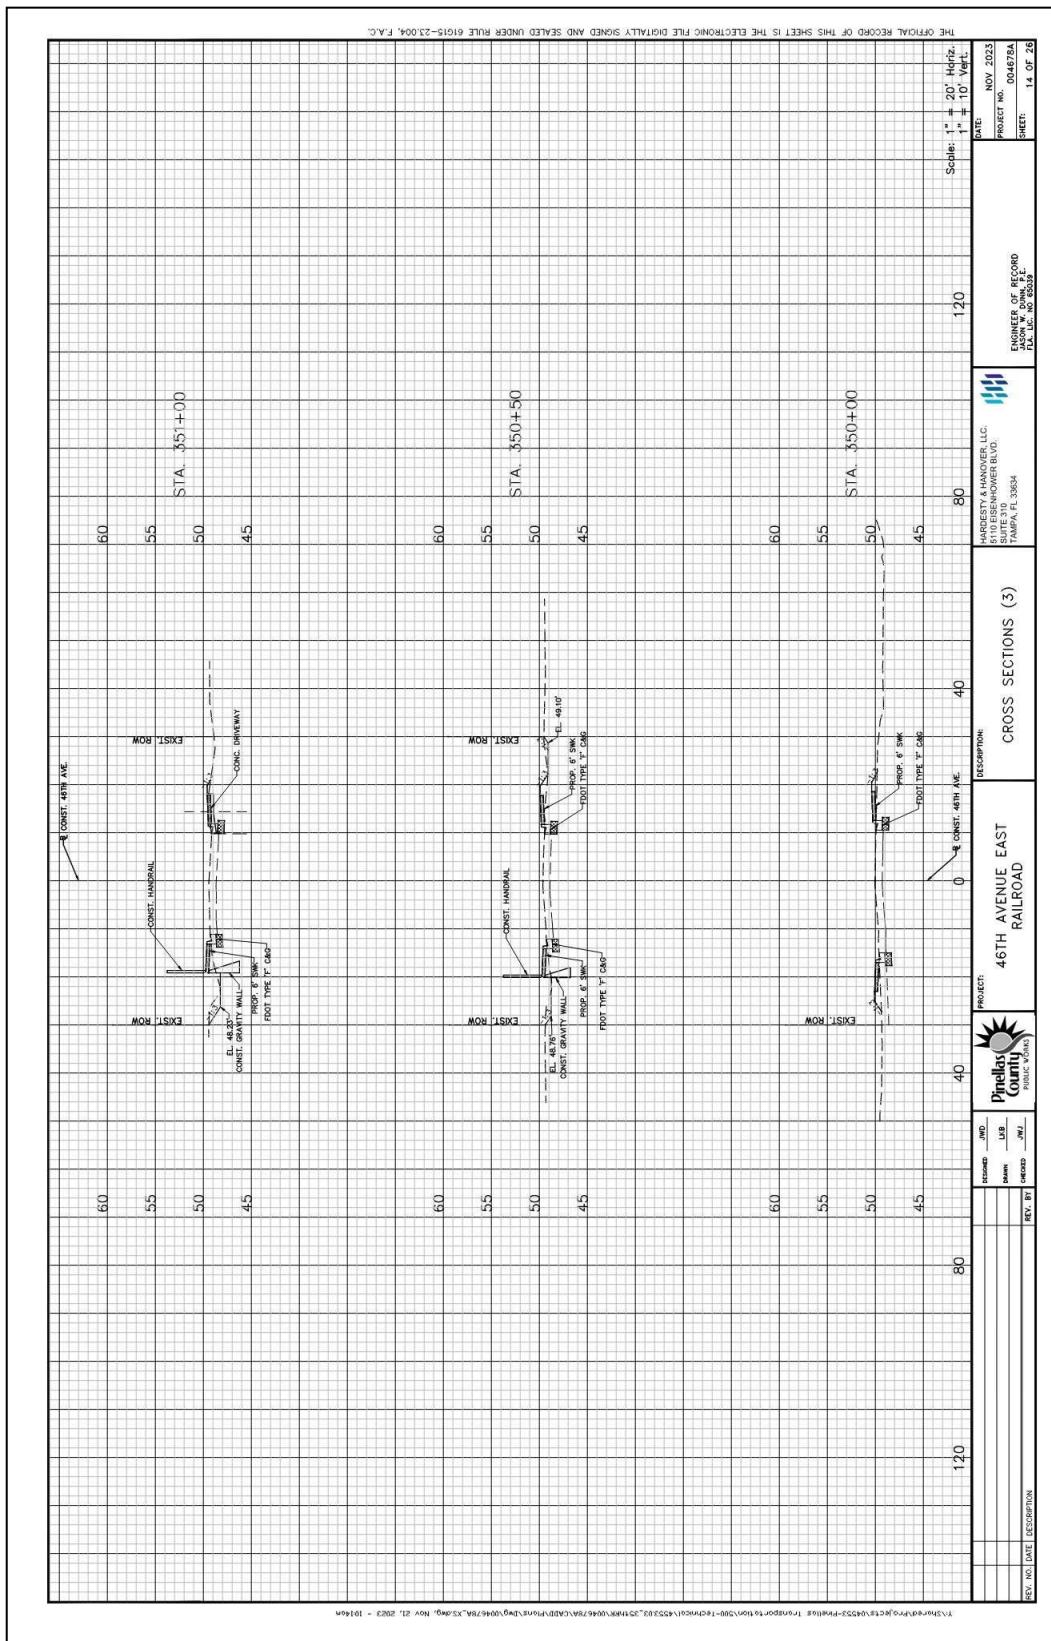

St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone; ARE 894.46
 CSXT OP No. TBD

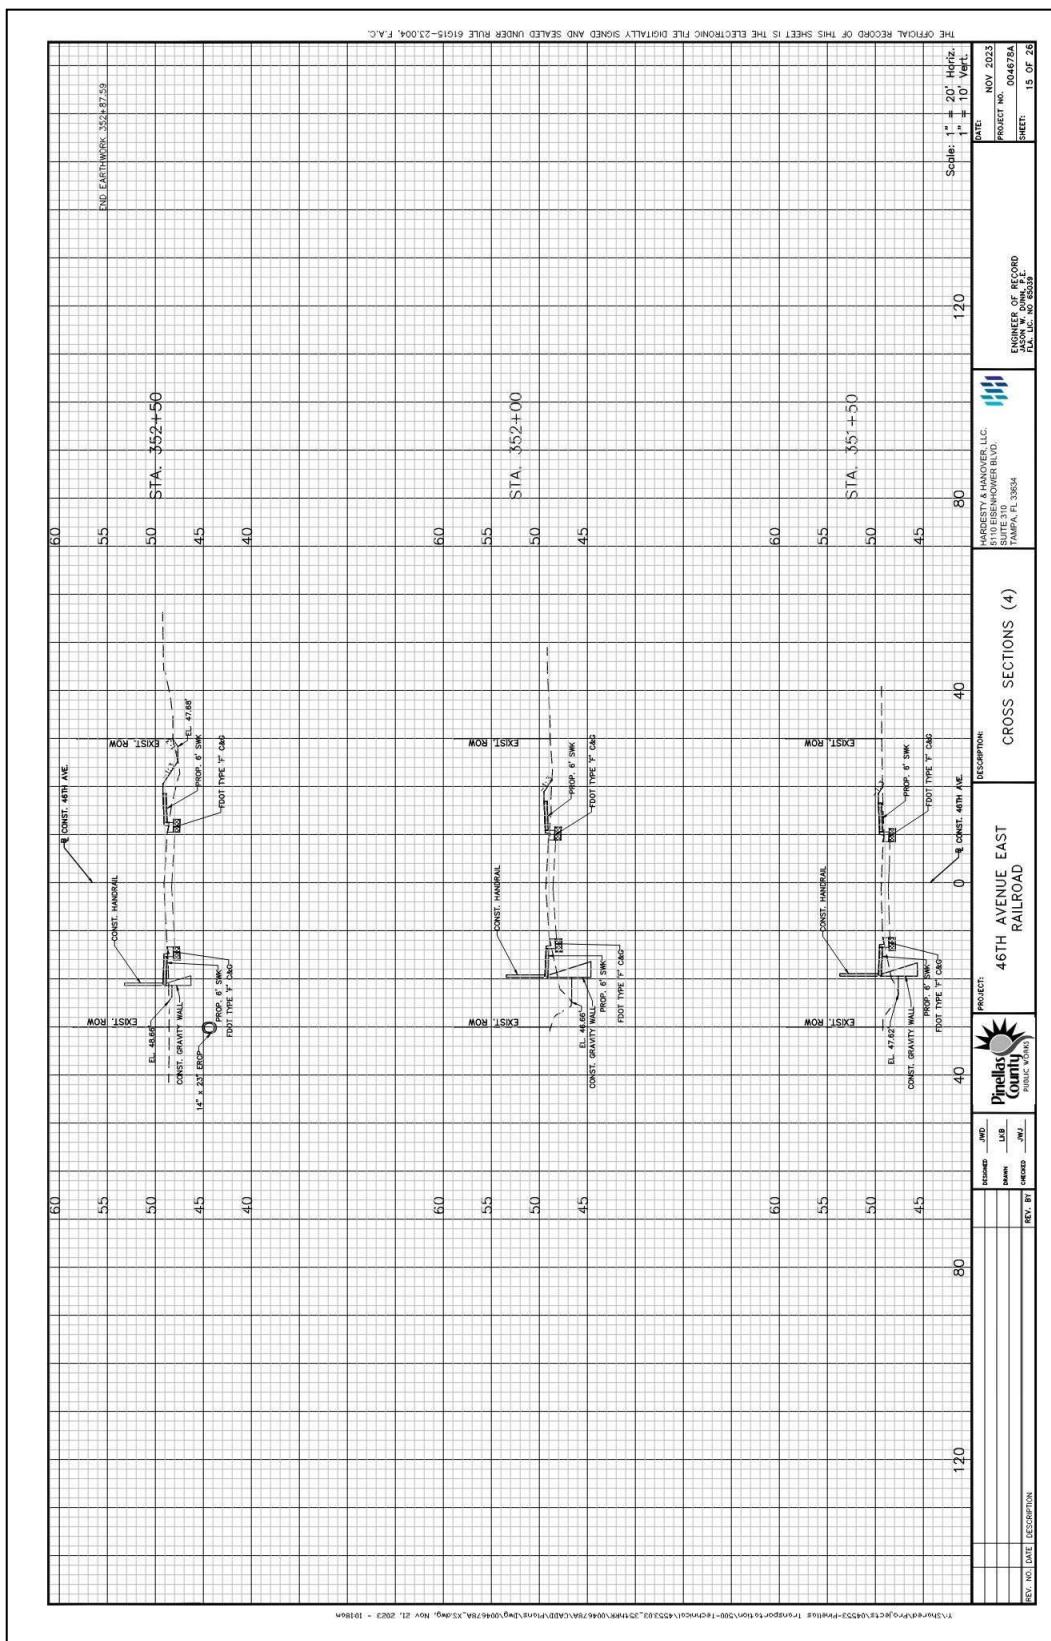


St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone; ARE 894.46
 CSXT OP No. TBD

I. SITE DESCRIPTION			
A. CONSTRUCTION ACTIVITY			
1. CONSTRUCTION OF A NEW RAILROAD CROSSING AND ROADWAY APPROACHES			
2. CONSTRUCTION OF CURB AND GUTTER AND SIDEWALKS			
3. ROADWAY RESURFACING			
B. PROJECT LIMITS			
PROJECT LIMITS ALONG 46TH AVENUE NORTH FROM LOW STREET TO 35TH STREET NORTH.			
C. PROJECT DESCRIPTION			
THE PROJECT CONSISTS OF CONSTRUCTION OF A NEW RAILROAD CROSSING, ADA COMPLIANT SIDEWALKS ON BOTH SIDES OF THE ROAD Curb AND Gutter IN THE RAILROAD CROSSING APPROACHES AND INCIDENTAL DRAINAGE WORK ALONG THE 46TH AVENUE NORTH.			
D. MAJOR SOIL DISTURBING ACTIVITIES			
MINOR CLEANING AND GRUBBING AND GRADING TO CONSTRUCT SIDEWALKS AND CURB AND GUTTER			
ALONG 46TH AVENUE NORTH.			
E. TOTAL PROJECT AREA: .183 ACRES			
TOTAL AREA TO BE DISTURBED: 1.24 ACRES			
F. RUNOFF DATA			
BEFORE CONSTRUCTION RUNOFF COEFFICIENT: 0.70			
AFTER CONSTRUCTION RUNOFF COEFFICIENT: 0.70-0.78			
G. SOIL DATA			
SOIL TYPE HYDROLOGIC SOIL GROUP			
MANGA LURAN LAND ID 1.5			
BRIAN LAND N/A			
H. DRAINAGE AREA (ATTACH DRAINAGE MAP OR PROVIDE DRAINAGE AREA IN ACRES)			
REFEE TO DRAINAGE MAP			
I. RECEIVING WATERS			
ROADSIDE DITCHES THAT DRAIN TOWARD JOE'S CREEK			
J. WETLANDS AREAS			
NONE WITHIN PROJECT LIMITS.			
K. ALL CONTROLS SHALL BE CONSISTENT WITH PERFORMANCE STANDARDS FOR EROSION AND SEDIMENT CONTROL AND STREAMWATER TREATMENT SET FORTH IN 6.6-4042 F.A.C. THE APPLICABLE STREAMWATER OR AND WATER MANAGEMENT (DEP, 1992) AND ANY SUBSEQUENT AMENDMENTS.			
L. SEQUENCE OF MAJOR ACTIVITIES			
A. 1. INSTALL STREAM BARRIERS AND INLET PROTECTION, CLEARING AND GRUBBING, GRADING			
2. INSTALL NEW RAILROAD CROSSING TUB			
3. CONSTRUCT CURB AND GUTTER AND SIDEWALK			
4. CONSTRUCT ROADWAY OVERBUILD AND PERFORM PAVEMENT RESURFACING			
WHEN CONSTRUCTION ACTIVITY IS COMPLETE AND THE SITE IS STABILIZED REMOVE EROSION PROTECTION DEVICES AND CONSTRUCTION ENTRANCE IS REQUIRED.			
B. EROSION AND SEDIMENT CONTROL CONSTRUCTION ACTIVITIES			
THE CONTRACTOR IS REQUIRED TO REVIEW THE SITE SPECIFIC EROSION CONTROL PLAN, THE CONTRACTOR AND THE ENGINEER SHALL CONFIRM THAT THE SITE SPECIFIC EROSION CONTROL PLAN MEETS THE REQUIREMENTS OF THE EROSION CONTROL PLAN AND THAT THE CONTRACTOR COMPLY WITH THE PLAN. ANY MODIFICATIONS TO THIS PLAN MAY BE CONDUCTED BY THE CONTRACTOR AS LONG AS THE CONTRACTOR SUBMITS THE MODIFIED PLAN FOR APPROVAL BEFORE COMMENCING ANY APPLICABLE OPERATION WITHIN CSXT CONSTRUCTION AREAS.			
C. SANITARY WASTE			
D. STABILIZED SITE, GLOVED AND DRESSED CONSTRUCTION REGIONS, TO SANITARY PROVISIONS, THE CONTRACTOR SHALL BE PROVIDED TO HELP REDUCE VEHICLE TRADING OF SEDIMENT AND INSPECTED DAILY. THE PAVED STREETS WILL BE CLEANED AS DIRECTED BY THE CONSTRUCTION INSPECTOR AND ENGINEER TO REMOVE ANY EXCESS MUD, DIRT OR ROCK TRACKED FROM THE SITE. DUMP TRUCKS HAULING MATERIAL TO OR FROM THE SITE WILL BE COVERED WITH A TARPULIN AT HAZARDOUS WASTE.			
E. TEMPORARY SODDING OR SEEDING			
PRESERVATION OF NATURAL RESOURCES			
BUFFER ZONES			
F. SYNTHETIC SODDINGS			
ARTIFICIAL COVERINGS/ROLLED EROSION CONTROL PRODUCTS (SY)			
INLET PROTECTION SYSTEM (IA)			
LETTER REMOVAL AND DISPOSAL (AC)			
MOVING (AC)			
SLOPE DRAINS, TEMPORARY RUNOFF CONTROL STRUCTURES (IF)			
SOIL TRACKING PREVENTION DEVICE (EA)			
SEDIMENT BASIN/CONTAINMENT SYSTEM (EA)			
SEDIMENT BASIN/CONTAINMENT SYSTEM/CLEANOUT (EA)			
FLOATING TURBIDITY BARBET (IF)			
STAKED SALT FENCE (IF)			
CHEMICAL TREATMENT, POWERED (SY)			
CHEMICAL TREATMENT (FLOC/LCLS, DRUMS OF PRODUCT) (EA)			
OTHER			
G. CONTRACTOR CERTIFICATION			
I CERTIFY UNDER PENALTY OF PERIOD OF LAW THAT THIS DOCUMENT AND ALL ATTACHMENTS WERE PREPARED UNDER MY DIRECTION OR SUPERVISION IN ACCORDANCE WITH THE SYSTEM DESIGNED TO ASSURE THAT ONLY EXPERT PERSONNEL OR PERSONS WHO MANAGE THE SYSTEM ON THESE PERSONS DIRECTLY RESPONSIBLE FOR OBTAINING THE INFORMATION SUBMITTED IS, TO THE BEST OF MY KNOWLEDGE AND BELIEF, TRUE, ACCURATE AND COMPLETENESS. I AM AUTHORIZED TO SIGN THIS DOCUMENT AND SUBMITTING THIS PAGE INFORMATION, INCLUDING POSSIBILITY OF FINE AND IMPRISONMENT FOR KNOWINGLY FALSE STATEMENTS.			
H. PERMITTEE CERTIFICATION			
I CERTIFY UNDER PENALTY OF PERIOD OF LAW THAT I UNDERSTAND AND SHALL COMPLY WITH THE TERMS AND CONDITIONS OF THE STATE OF FLORIDA GENERAL PERMIT FOR STORMWATER DISCHARGE FROM LARGE AND SMALL CONSTRUCTION ACTIVITIES AND THIS STORMWATER POLLUTION PREVENTION PLAN PREPARED THEREUNDER.			
I. COMPANY NAME			
HARDESTY & HAWKER, LLC.			
SUITE 110, HAWKER BLV.			
TAMPA, FL 33634			
J. COMPANY STREET ADDRESS			
K. CITY, STATE, ZIP CODE			
L. GENERAL CONTRACTOR NAME & TITLE			
NONA R. GABRIEL, P.E., COM. CAPITAL IMPROVEMENTS DIVISION DIRECTOR			
PINELLAS COUNTY PUBLIC WORKS, APP-LAW AUTHORIZED AGENT FOR THE COUNTY COMMISSIONERS			
M. DATE			
N. CONTRACTOR CERTIFICATION			
I CERTIFY UNDER PENALTY OF PERIOD OF LAW THAT THE DESIGN AND CONSTRUCTION ACTIVITIES AND MATERIALS USED IN THE PROJECT ARE IN ACCORDANCE WITH THE TERMS AND CONDITIONS OF THE STATE OF FLORIDA GENERAL PERMIT FOR STORMWATER DISCHARGE FROM LARGE AND SMALL CONSTRUCTION ACTIVITIES AND THIS STORMWATER POLLUTION PREVENTION PLAN PREPARED THEREUNDER.			
O. COMPANY NAME			
HARDESTY & HAWKER, LLC.			
SUITE 110, HAWKER BLV.			
TAMPA, FL 33634			
P. COMPANY STREET ADDRESS			
K. CITY, STATE, ZIP CODE			
Q. DATE			
R. ENGINEER OF RECORD			
HARDESTY & HAWKER, LLC.			
SUITE 110, HAWKER BLV.			
TAMPA, FL 33634			
S. DATE			
NOV 2023			
PROJECT NO.			
004873A			
SHEET: 16 OF 26			
THE OFFICIAL RECORD OF THIS SHEET IS THE ELECTRONICALLY DIGITAL COPY MADE AND SEALED UNDER RULE 6105-23.004, F.A.C.			


St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone; ARE 894.46
 CSXT OP No. TBD

		<small>THE OFFICIAL RECORD OF THIS SHEET IS THE ELECTRONIC FILE DIGITALLY SIGNED AND SEALED UNDER RULE 61G15-23.004, F.A.C.</small>					
TEMPORARY TRAFFIC CONTROL GENERAL NOTES							
<p>1. MANTAIN LOCAL TRAFFIC AND PEDESTRIAN TRAFFIC TO RESIDENTIAL PROPERTIES AT ALL TIMES.</p> <p>2. DETOUR ALL NON-LOCAL TRAFFIC DURING THE RECONSTRUCTION OF THE ROADWAY.</p> <p>3. USE PORTABLE CHANGEABLE MESSAGE SIGNS (PCMS) TO INFORM PUBLIC 2 WEEKS IN ADVANCE OF CONSTRUCTION COMMENCING WHEN CONSTRUCTION BEGINS. ADJUST PCMS MESSAGE DISPLAY AS SHOWN BELOW.</p>							
2 WEEKS PRIOR:	DISPLAY 1 46TH AVE CLOSED AT RR	DISPLAY 2 MANADO TO MANADO	DISPLAY 1 46TH AVE CLOSED AT RR	DISPLAY 2 MANADO TO MANADO			
<p>DURING CONSTRUCTION:</p> <p>PLACE PANS AS SHOWN ON THE TEMPORARY TRAFFIC CONTROL PLAN DETOUR (1).</p> <p>1. COORDINATE DRIVEWAY / PROPERTY ACCESS WITH AFFECTED PROPERTY OWNERS TWO MONTHS PRIOR TO ANY WORK ADJACENT TO PROPERTY IMPACTED BY RECONSTRUCTION OF THE ROADWAY OR PROPERTY.</p> <p>2. PRIOR TO AN ELEVATED RR OVERBUILDS, THE ROADWAY AND OVERBUILDS WILL BE OPEN TO LOCAL TRAFFIC ONLY. LOCAL TRAFFIC CAN TURN ONTO THE RR OVERBUILD AND TRAVEL SAFELY AND ACROSS THEIR PROPERTY. REFER TO FOOT STANDARD PLANS 102-400.</p> <p>3. DESIGN SPEED OF 46TH AVE. = 30 MPH.</p> <p>4. ROADWAY LADERS MUST BE PRESENT ON EACH SIDE OF THE RR OVERBUILD CROSSING, ANY TIME TRAFFIC IS DIRECTED INTO EXPOSING TRAFFIC LANES AT THE RR OVERBUILD CROSSING.</p> <p>5. CHANNELIZATION DEVICES SHALL BE PLACED A MINIMUM OF 15 FEET FROM CENTER LINE OF RR OVERBUILD CROSSING.</p>							
TEMPORARY TRAFFIC CONTROL PHASE NOTES							
<p>PHASE 1.</p> <p>THIS PHASE WILL CONSTRUCT THE RR TRACK CROSSING ALONG WITH THE PROPOSED SIDEWALK, CURB AND GUTTER AND OVERBUILD OF THE ROADWAY FOR THE NORTH AND SOUTH APPROACHES TO THE RR TRACK.</p> <p>1. INSTALL DETOUR SIGNS PER DETOUR SHEET.</p> <p>2. INSTALL DETOUR.</p> <p>3. CLOSE ROADWAY TO THROUGH TRAFFIC, CONSTRUCT PROPOSED TRACK CROSSING ALONG THE RR OVERBUILD WHILE MAINTAINING LOCAL TRAFFIC LANE OF THE PROPOSED RR OVERBUILD.</p> <p>4. CONSTRUCT PROPOSED SIDEWALK AND CURB AND GUTTER.</p> <p>5. CONSTRUCT ROADWAY OVERBUILD TO MATCH THE PROFILE OF THE CONSTRUCTED RR TRACK CROSSING.</p> <p>6. REMOVE DETOUR AND OPEN ROADWAY TO TRAFFIC.</p>							
<p>PHASE 2.</p> <p>THIS PHASE WILL RESURFACE 46TH AVENUE NORTH FROM 37TH STREET NORTH TO 35TH STREET NORTH.</p> <p>1. MILL AND RESURFACE THE ROADWAY AS SHOWN IN THE CONSTRUCTION PLANS USING FOOT STANDARD PLANS 102-600.</p>							
<small>REV. NO. DATE / DESCRIPTION</small>	<small>RECD/ED - JWD SHW - LRB COKED - JMS</small>	<small>RECD/ED - JWD SHW - LRB COKED - JMS</small>	<small>PROJECT: 46TH AVENUE EAST RR</small>	<small>DESCRIPTION: TTCP GENERAL / PHASE NOTES</small>	<small>HANDEBRY & HANOVER, LLC. SUITE 110 TAMPA, FL 33634</small>	<small>ENGINEER OF RECORD: FLA. INC. #00809</small>	<small>DATE: NOV. 2023 PROJECT NO.: 004678A SHEET: 18 OF 26</small>


St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone; ARE 894.46
 CSXT OP No. TBD

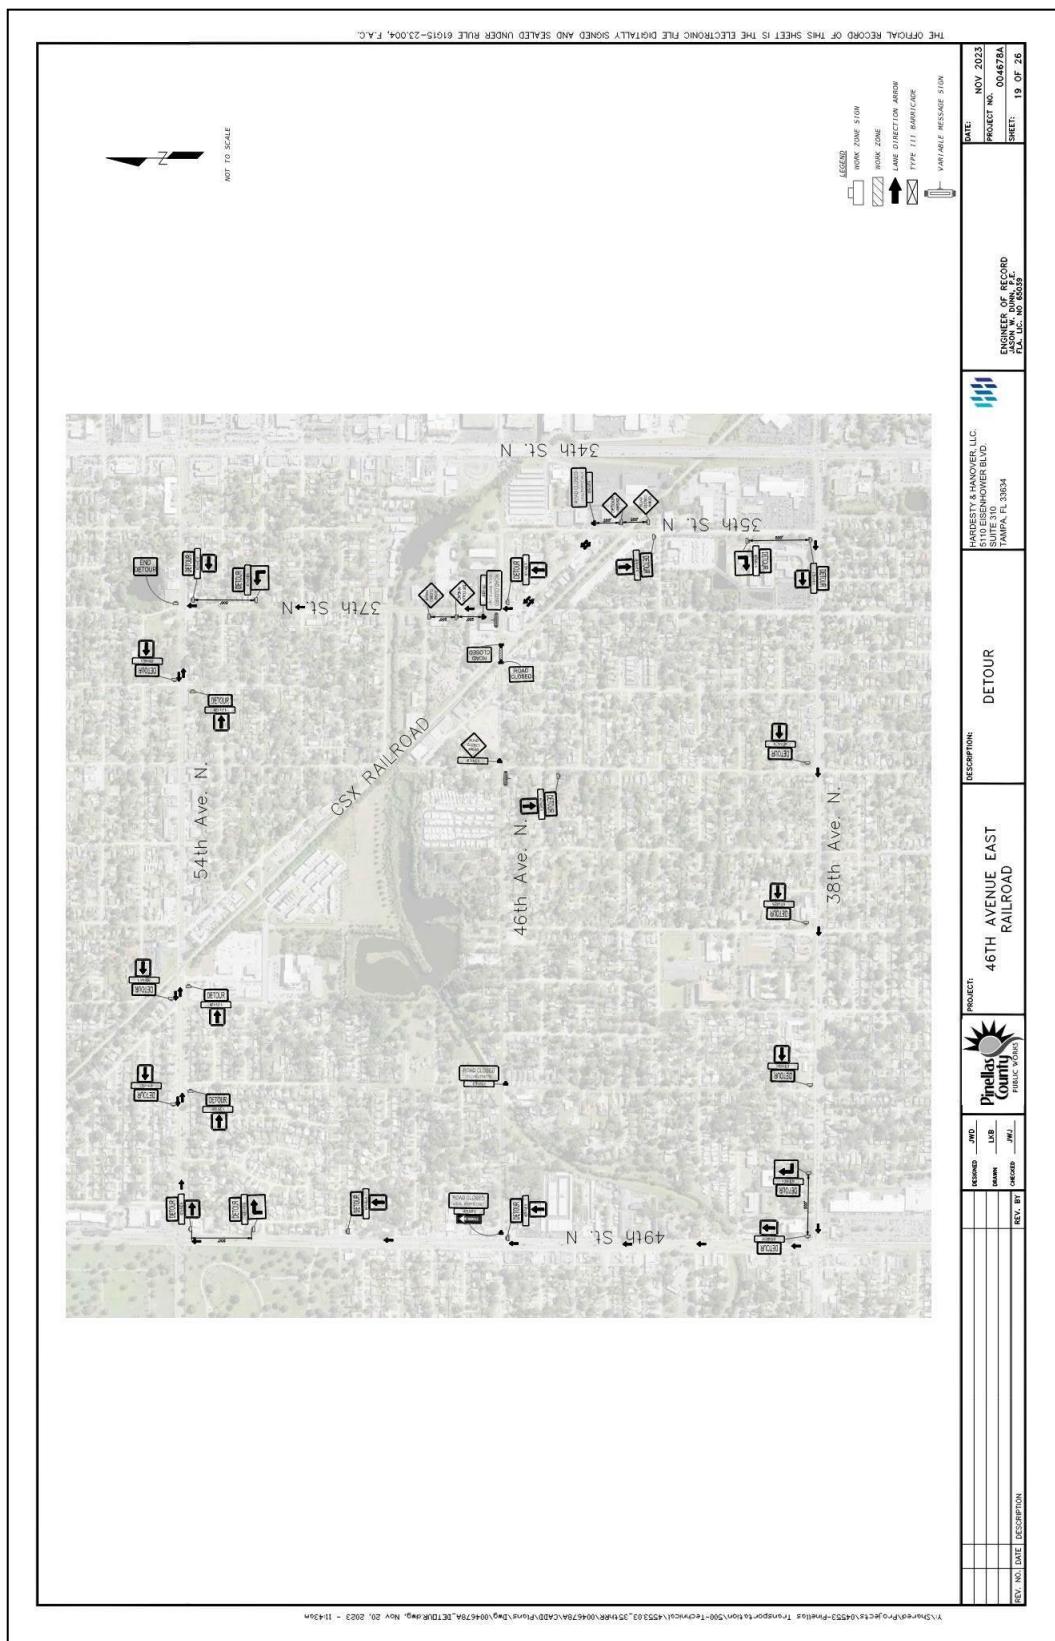


St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. TBD

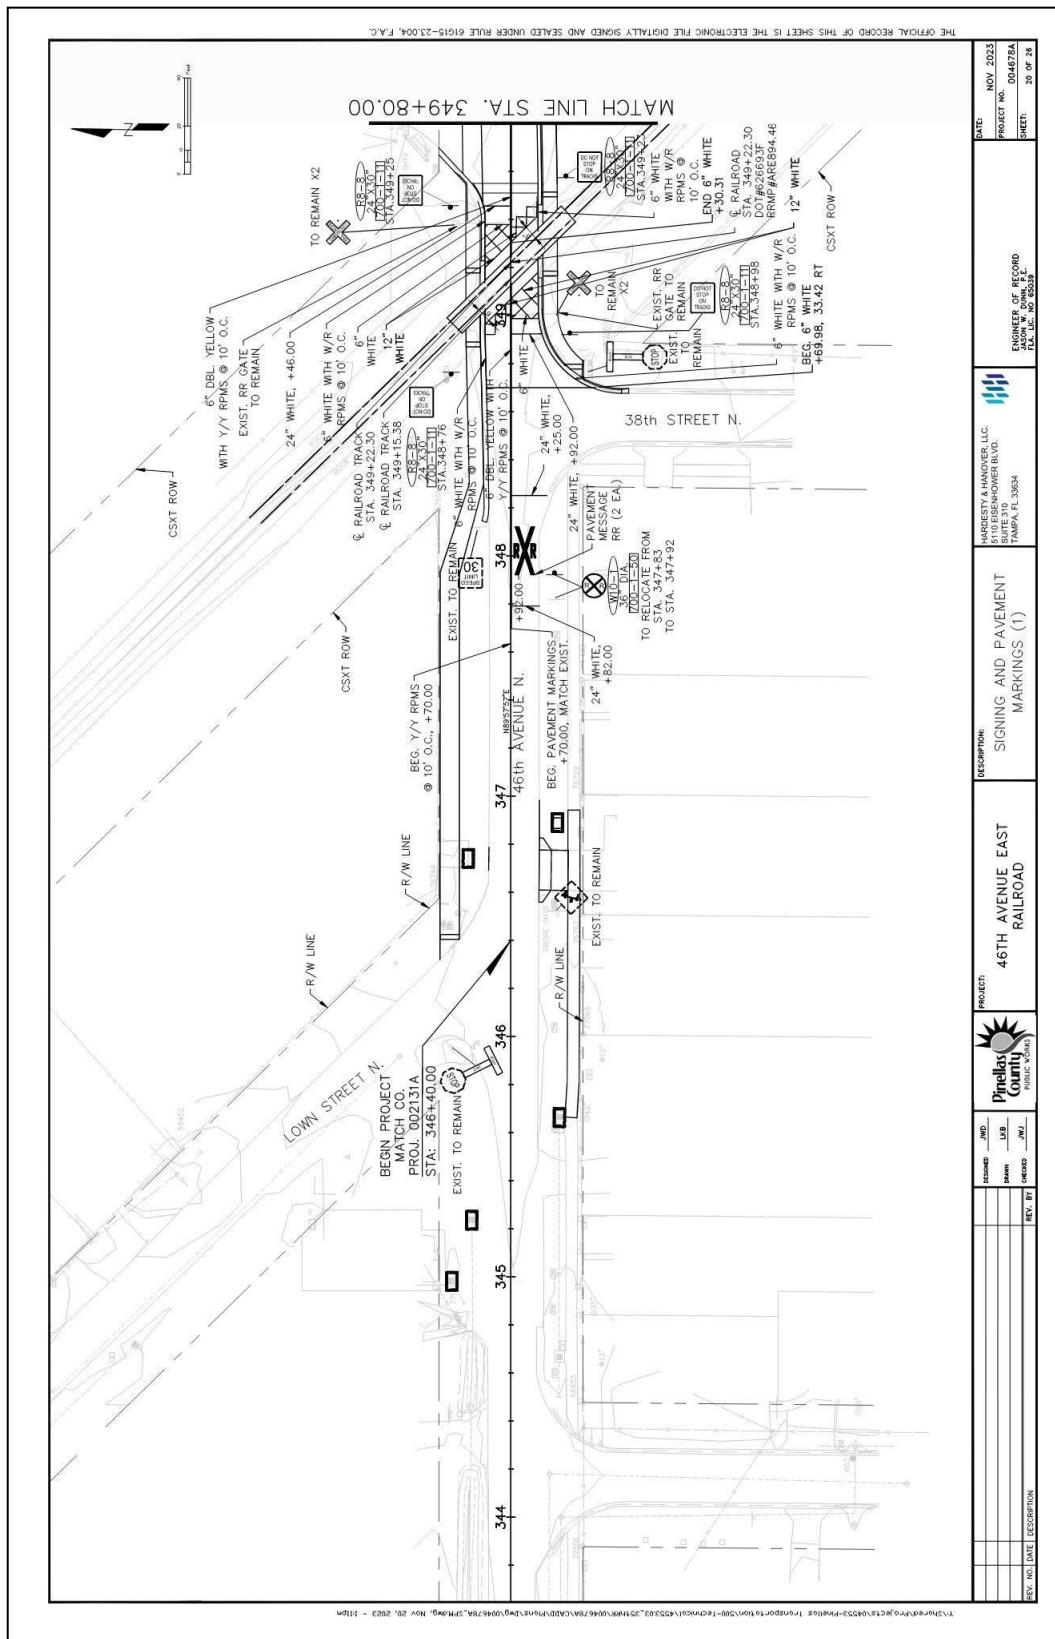


St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. TBD

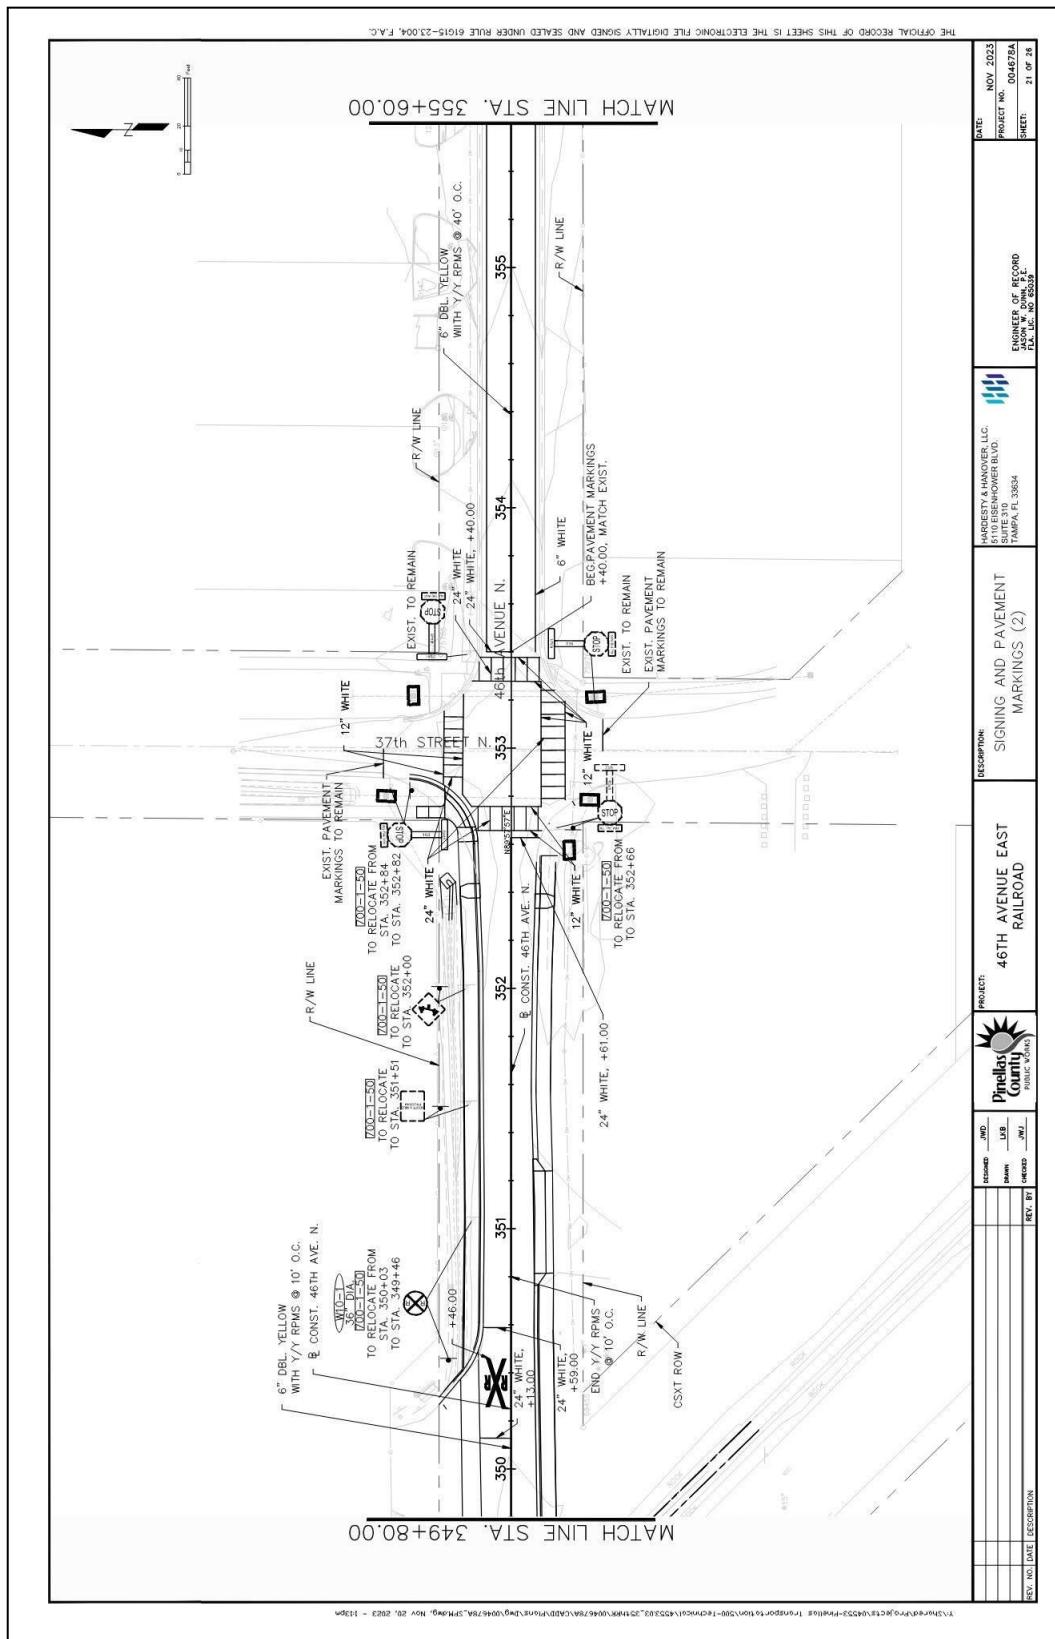


St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. TBD

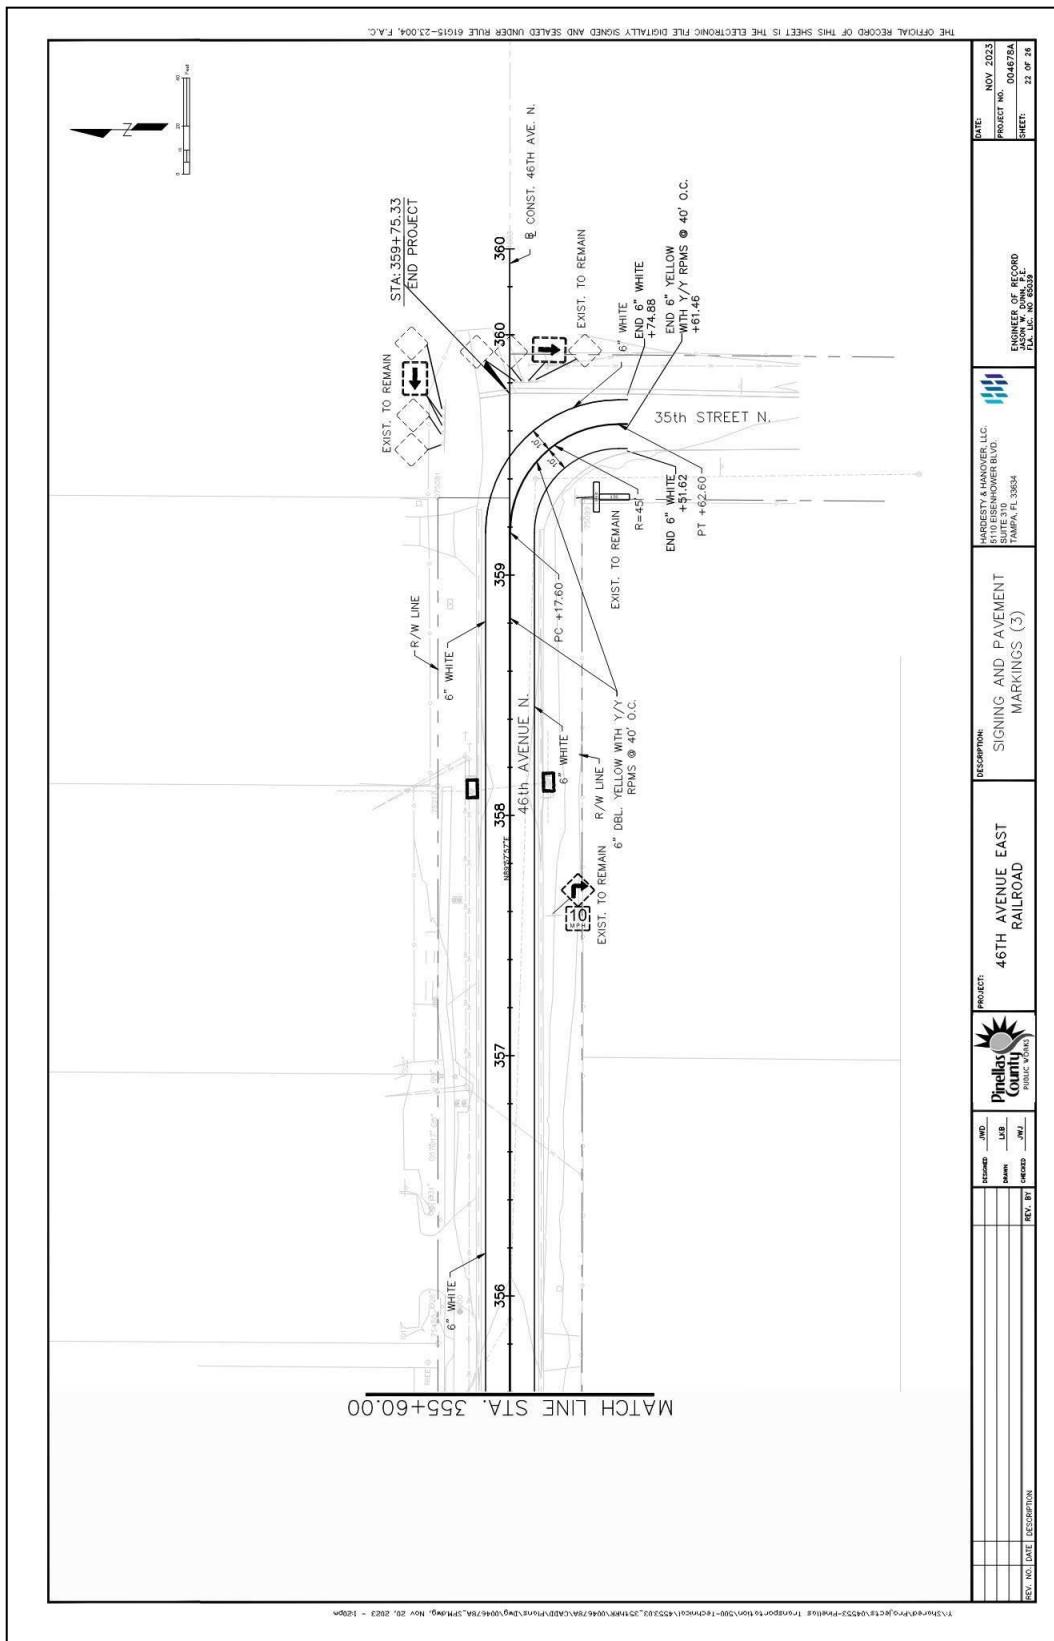


St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. TBD

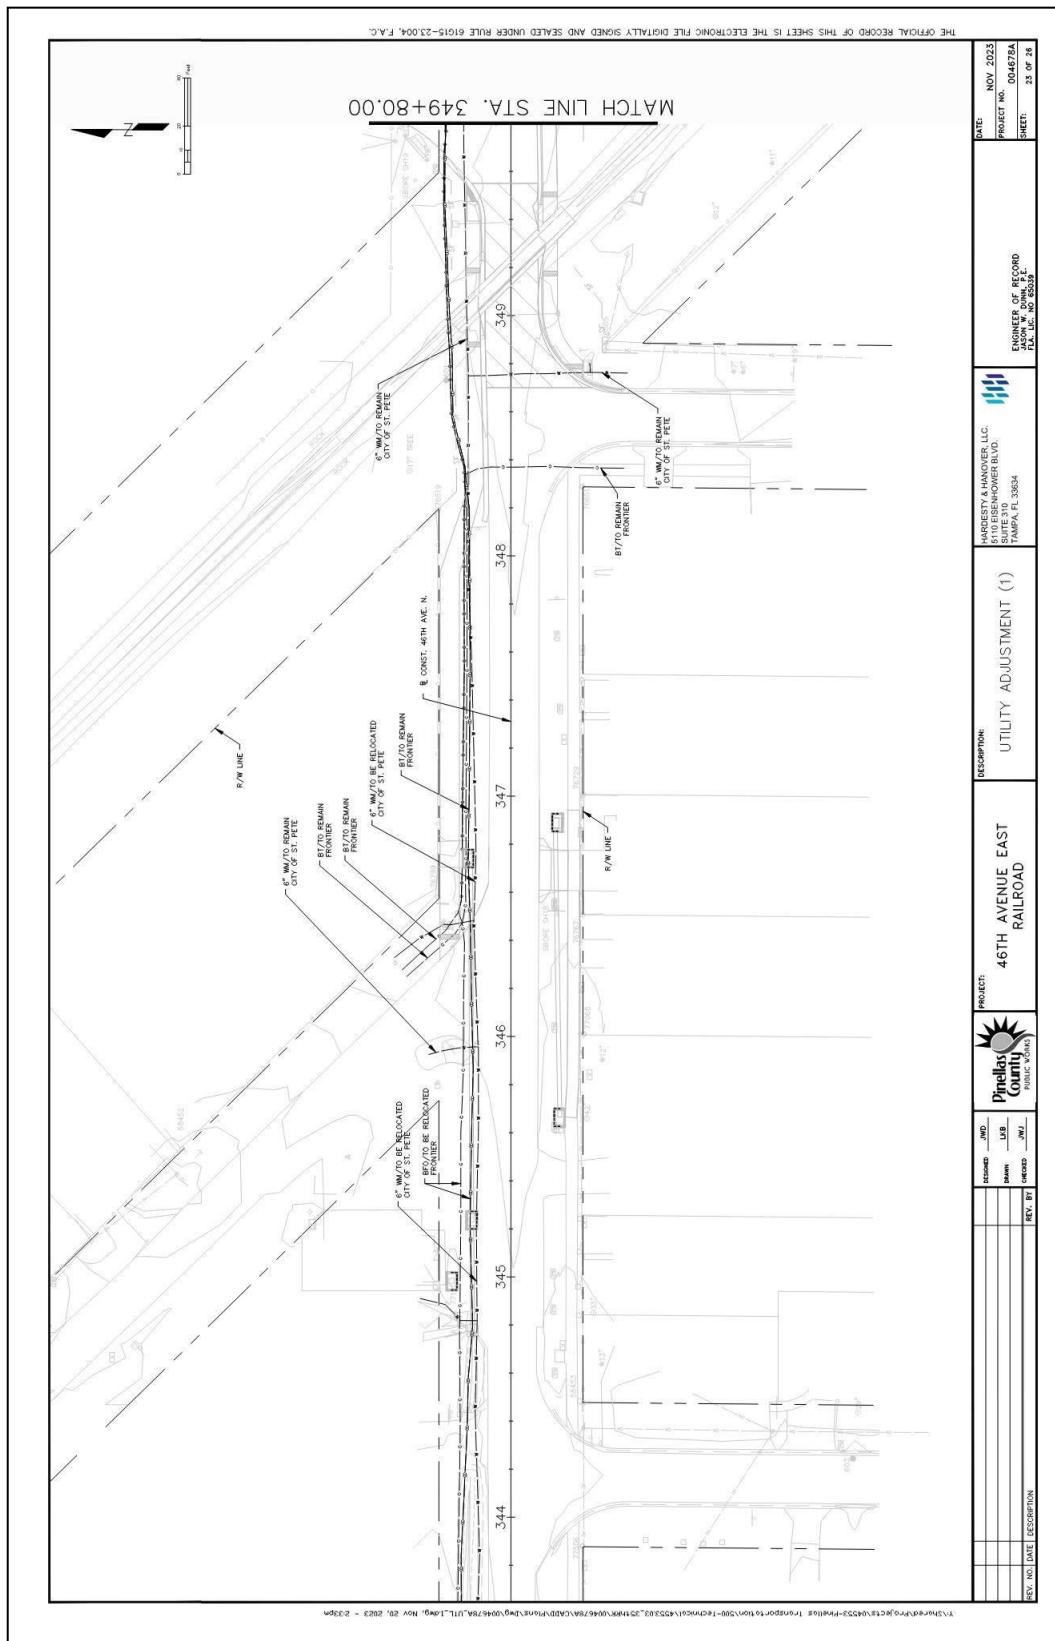

St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. TBD

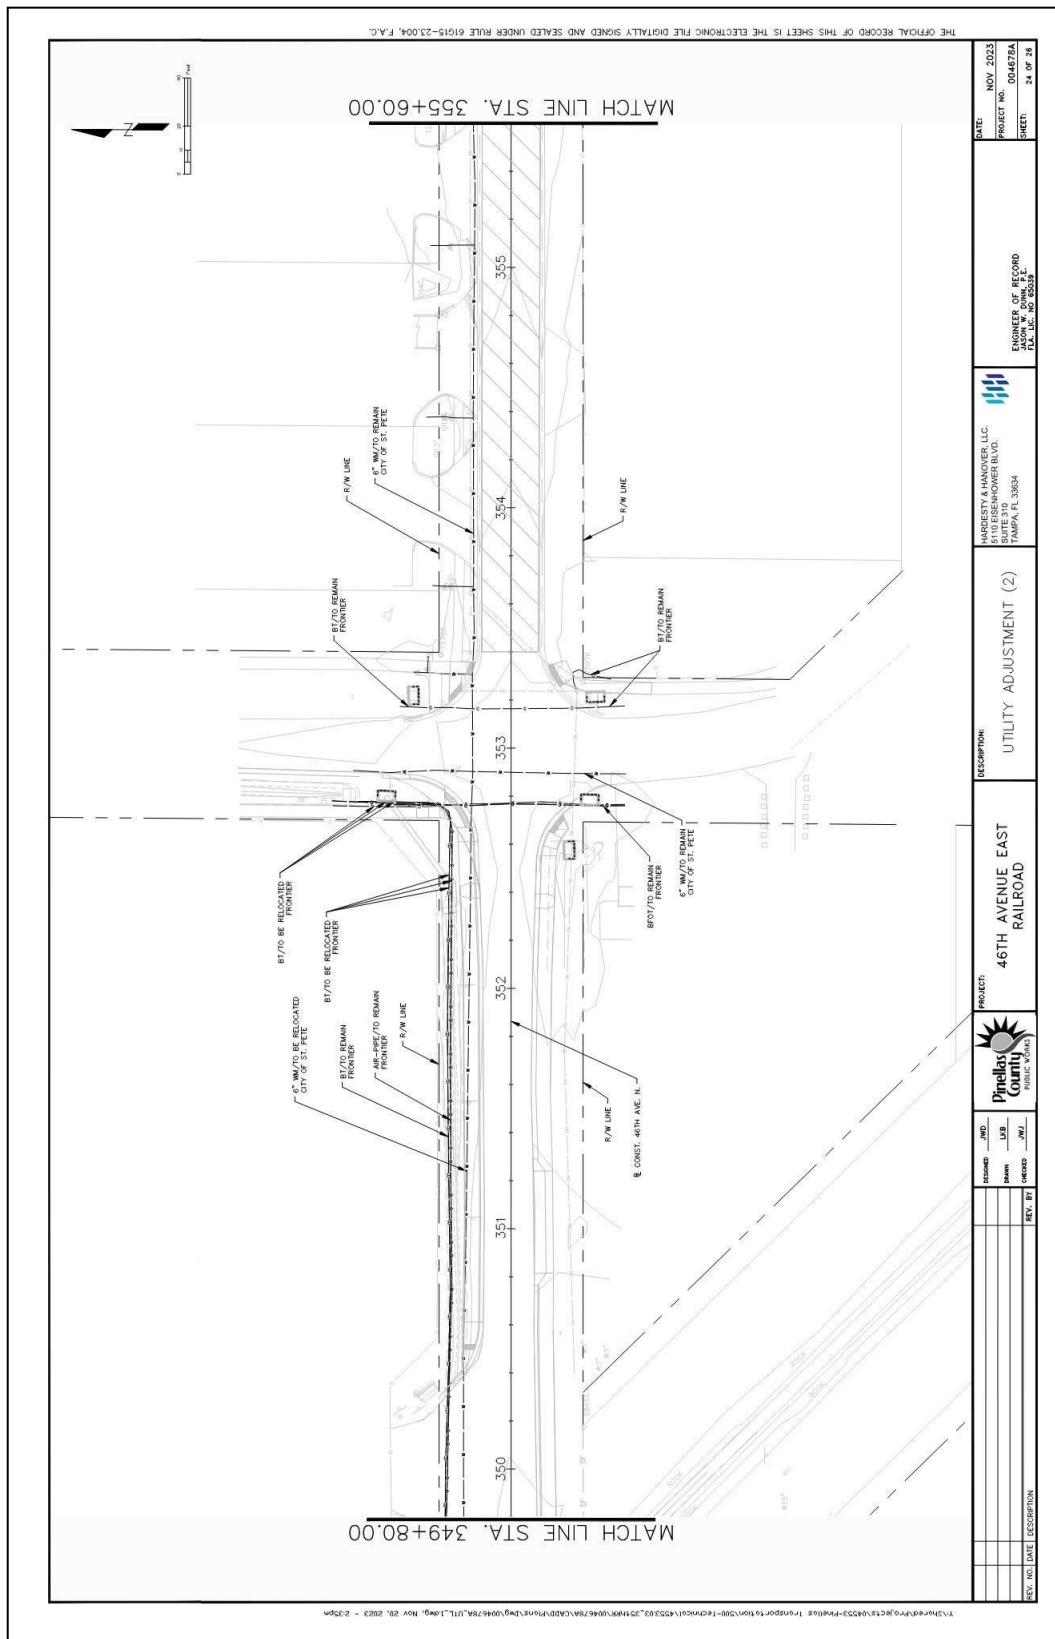

St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. TBD

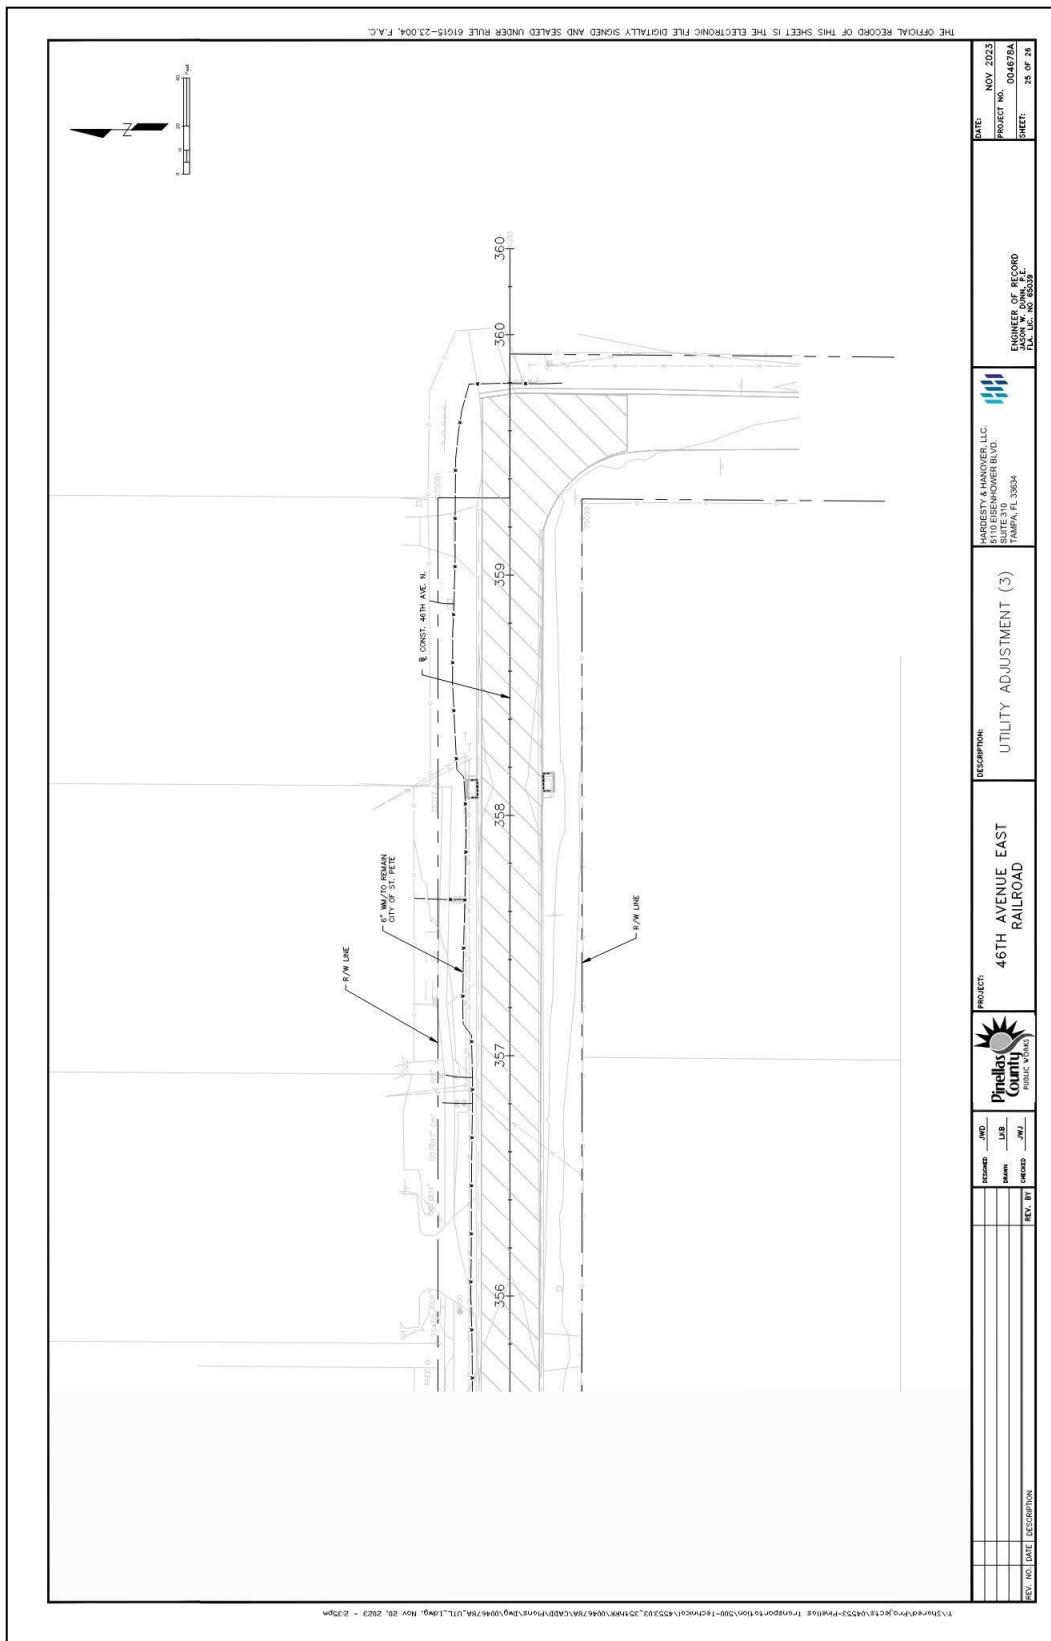

St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone; ARE 894.46
 CSXT OP No. TBD

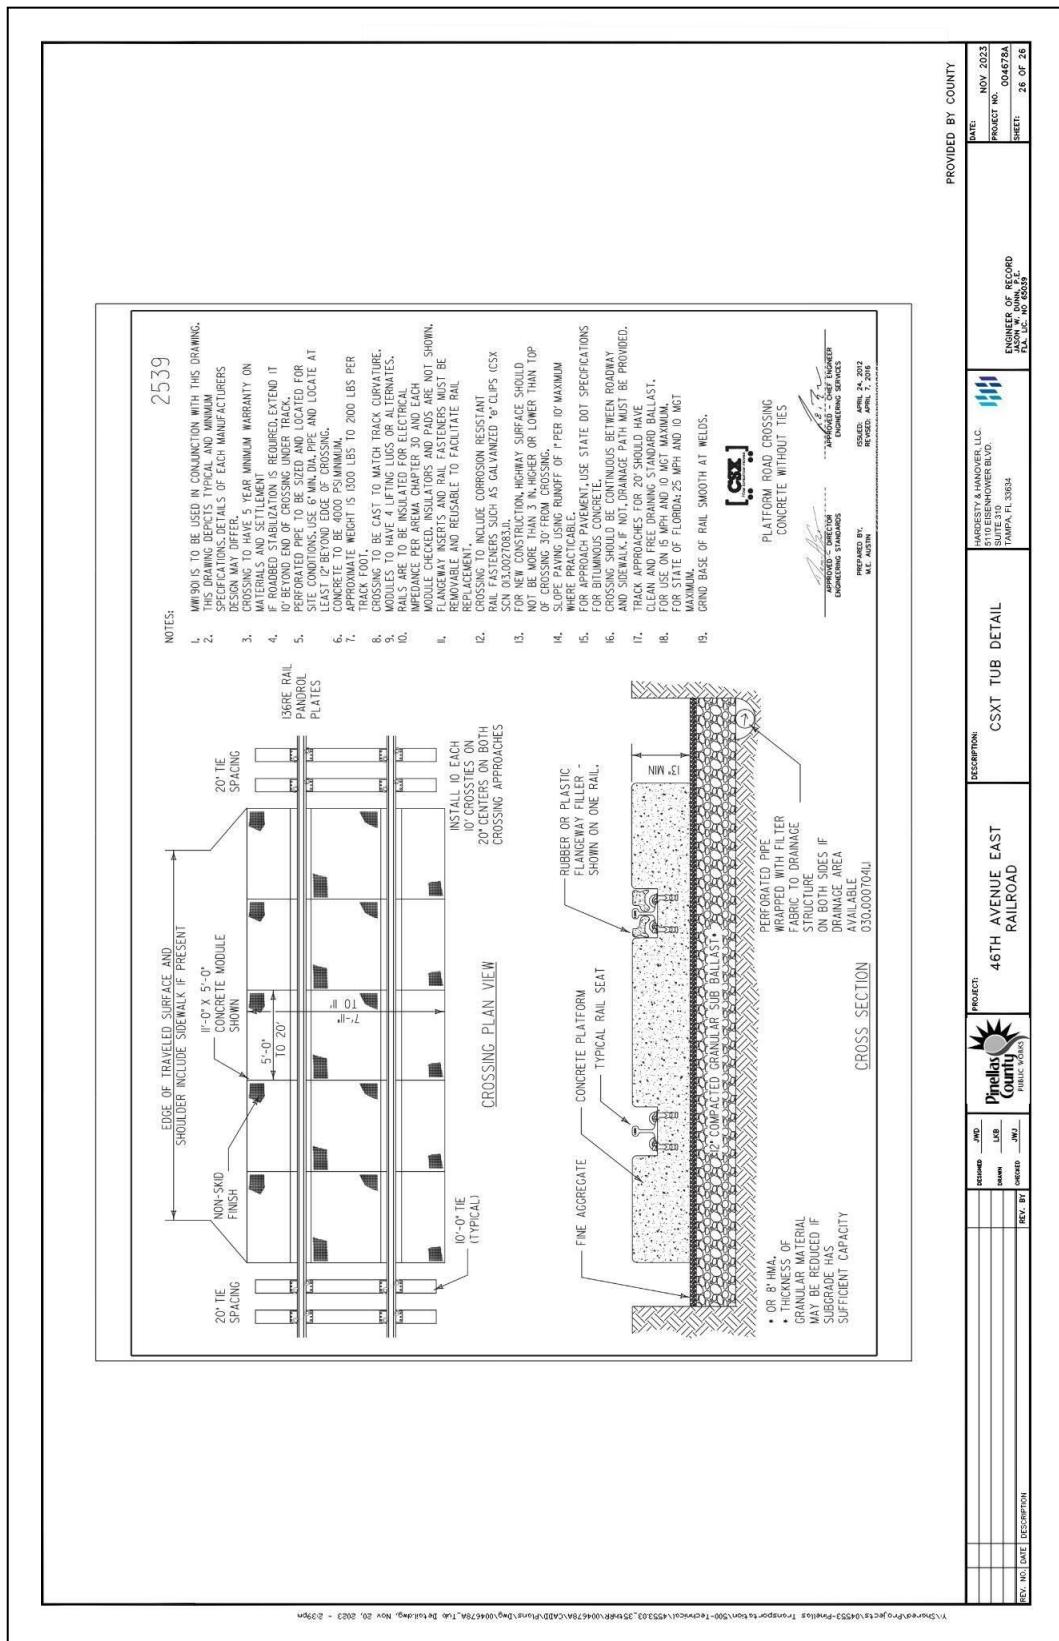


EXHIBIT C

CSXT SPECIAL PROVISIONS

DEFINITIONS:

As used in these Special Provisions, all capitalized terms shall have the meanings ascribed to them by the Agreement, and the following terms shall have the meanings ascribed to them below:

“CSXT” shall mean CSX Transportation, Inc., its successors and assigns.

“CSXT Representative” shall mean the authorized representative of CSX Transportation, Inc.

“Agreement” shall mean the Agreement between CSXT and Agency dated as of June 4, 2025, as amended from time to time.

“Agency” shall mean the **Pinellas County, Florida Board of County Commissioners**.

“Agency Representative” shall mean the authorized representative of **Pinellas County, Florida Board of County Commissioners**.

“Contractor” shall have the meaning ascribed to such term by the Agreement.

“Work” shall mean the Project as described in the Agreement.

I. AUTHORITY OF CSXT ENGINEER

The CSXT Representative shall have final authority in all matters affecting the safe maintenance of CSXT operations and CSXT property, and his or her approval shall be obtained by the Agency or its Contractor for methods of construction to avoid interference with CSXT operations and CSXT property and all other matters contemplated by the Agreement and these Special Provisions.

II. INTERFERENCE WITH CSXT OPERATIONS

- A. Agency or its Contractor shall arrange and conduct its work so that there will be no interference with CSXT operations, including train, signal, telephone and telegraphic services, or damage to CSXT’s property, or to poles, wires, and other facilities of tenants on CSXT’s Property or right-of-way. Agency or its Contractor shall store materials so as to prevent trespassers from causing damage to trains, or CSXT Property. Whenever Work is likely to affect the operations or safety of trains, the method of doing such Work shall first be submitted to the CSXT Representative for approval, but such approval shall not relieve Agency or

its Contractor from liability in connection with such Work.

- B. If conditions arising from or in connection with the Project require that immediate and unusual provisions be made to protect train operation or CSXT's property, Agency or its Contractor shall make such provision. If the CSXT Representative determines that such provision is insufficient, CSXT may, at the expense of Agency or its Contractor, require or provide such provision as may be deemed necessary, or cause the Work to cease immediately.

III. NOTICE OF STARTING WORK. Agency or its Contractor shall not commence any work on CSXT Property or rights-of-way until it has complied with the following conditions:

- A. Notify CSXT in writing of the date that it intends to commence Work on the Project. Such notice must be received by CSXT at least ten business days in advance of the date Agency or its Contractor proposes to begin Work on CSXT property. The notice must refer to this Agreement by date. If flagging service is required, such notice shall be submitted at least thirty (30) business days in advance of the date scheduled to commence the Work.
- B. Obtain authorization from the CSXT Representative to begin Work on CSXT property, such authorization to include an outline of specific conditions with which it must comply.
- C. Obtain from CSXT the names, addresses and telephone numbers of CSXT's personnel who must receive notice under provisions in the Agreement. Where more than one individual is designated, the area of responsibility of each shall be specified.

IV. WORK FOR THE BENEFIT OF THE CONTRACTOR

- A. No temporary or permanent changes to wire lines or other facilities (other than third party fiber optic cable transmission systems) on CSXT property that are considered necessary to the Work are anticipated or shown on the Plans. If any such changes are, or become, necessary in the opinion of CSXT or Agency, such changes will be covered by appropriate revisions to the Plans and by preparation of a force account estimate. Such force account estimate may be initiated by either CSXT or Agency, but must be approved by both CSXT and Agency. Agency or Contractor shall be responsible for arranging for the relocation of the third party fiber optic cable transmission systems, at no cost or expense to CSXT.

- B. Should Agency or Contractor desire any changes in addition to the above, then it shall make separate arrangements with CSXT for such changes to be accomplished at the Agency or Contractor's expense.

V. HAUL ACROSS RAILROAD

- A. If Agency or Contractor desires access across CSXT property or tracks at other than an existing and open public road crossing in or incident to construction of the Project, the Agency or Contractor must first obtain the permission of CSXT and shall execute a license agreement or right of entry satisfactory to CSXT, wherein Agency or Contractor agrees to bear all costs and liabilities related to such access.
- B. Agency and Contractor shall not cross CSXT's property and tracks with vehicles or equipment of any kind or character, except at such crossing or crossings as may be permitted pursuant to this section.

VI. COOPERATION AND DELAYS

- A. Agency or Contractor shall arrange a schedule with CSXT for accomplishing stage construction involving work by CSXT. In arranging its schedule, Agency or Contractor shall ascertain, from CSXT, the lead time required for assembling crews and materials and shall make due allowance therefore.
- B. Agency or Contractor may not charge any costs or submit any claims against CSXT for hindrance or delay caused by railroad traffic; work done by CSXT or other delay incident to or necessary for safe maintenance of railroad traffic; or for any delays due to compliance with these Special Provisions.
- C. Agency and Contractor shall cooperate with others participating in the construction of the Project to the end that all work may be carried on to the best advantage.
- D. Agency and Contractor understand and agree that CSXT does not assume any responsibility for work performed by others in connection the Project. Agency and Contractor further understand and agree that they shall have no claim whatsoever against CSXT for any inconvenience, delay or additional cost incurred by Agency or Contractor on account of operations by others.

VII. STORAGE OF MATERIALS AND EQUIPMENT

Agency and Contractor shall not store their materials or equipment on CSXT's property or where they may potentially interfere with CSXT's operations, unless Agency or Contractor has received CSXT Representative's prior written permission. Agency and Contractor understand and agree that CSXT will not be liable for any damage to such

materials and equipment from any cause and that CSXT may move, or require Agency or Contractor to move, such material and equipment at Agency's or Contractor's sole expense. To minimize the possibility of damage to the railroad tracks resulting from the unauthorized use of equipment, all grading or other construction equipment that is left parked near the tracks unattended by watchmen shall be immobilized to the extent feasible so that it cannot be moved by unauthorized persons.

VIII. CONSTRUCTION PROCEDURES

A. General

1. Construction work on CSXT property shall be subject to CSXT's inspection and approval.
2. Construction work on CSXT property shall be in accord with CSXT's written outline of specific conditions and with these Special Provisions.
3. Contractor shall observe the terms and rules of the CSXT Safe Way manual, which Agency and Contractor shall be required to obtain from CSXT, and in accord with any other instructions furnished by CSXT or CSXT's Representative.

B. Blasting

1. Agency or Contractor shall obtain CSXT Representative's and Agency Representative's prior written approval for use of explosives on or adjacent to CSXT property. If permission for use of explosives is granted, Agency or Contractor must comply with the following:
 - a. Blasting shall be done with light charges under the direct supervision of a responsible officer or employee of Agency or Contractor.
 - b. Electric detonating fuses shall not be used because of the possibility of premature explosions resulting from operation of two-way train radios.
 - c. No blasting shall be done without the presence of an authorized representative of CSXT. At least 10 days' advance notice to CSXT Representative is required to arrange for the presence of an authorized CSXT representative and any flagging that CSXT may require.
 - d. Agency or Contractor must have at the Project site adequate equipment, labor and materials, and allow sufficient time, to (i) clean up (at Agency's expense) debris resulting from the blasting

without any delay to trains; and (ii) correct (at Agency's expense) any track misalignment or other damage to CSXT's property resulting from the blasting, as directed by CSXT Representative, without delay to trains. If Agency's or Contractor's actions result in delay of any trains, including Amtrak passenger trains, Agency shall bear the entire cost thereof.

- e. Agency and Contractor shall not store explosives on CSXT property.
2. CSXT Representative will:
 - a. Determine the approximate location of trains and advise Agency or Contractor of the approximate amount of time available for the blasting operation and clean-up.
 - b. Have the authority to order discontinuance of blasting if, in his or her opinion, blasting is too hazardous or is not in accord with these Special Provisions.

IX. MAINTENANCE OF DITCHES ADJACENT TO CSXT TRACKS

Agency or Contractor shall maintain all ditches and drainage structures free of silt or other obstructions that may result from their operations. Agency or Contractor shall provide erosion control measures during construction and use methods that accord with applicable state standard specifications for road and bridge construction, including either (1) silt fence; (2) hay or straw barrier; (3) berm or temporary ditches; (4) sediment basin; (5) aggregate checks; and (6) channel lining. All such maintenance and repair of damages due to Agency's or Contractor's operations shall be performed at Agency's expense.

X. FLAGGING / INSPECTION SERVICE

- A. CSXT has sole authority to determine the need for flagging required to protect its operations and property. In general, flagging protection will be required whenever Agency or Contractor or their equipment are, or are likely to be, working within fifty (50) feet of live track or other track clearances specified by CSXT, or over tracks.
- B. Agency shall reimburse CSXT directly for all costs of flagging that is required on account of construction within CSXT property shown in the Plans, or that is covered by an approved plan revision, supplemental agreement or change order.

- C. Agency or Contractor shall give a minimum of 10 days' advance notice to CSXT Representative for anticipated need for flagging service. No work shall be undertaken until the flag person(s) is/are at the job site. If it is necessary for CSXT to advertise a flagging job for bid, it may take up to 90-days to obtain this service, and CSXT shall not be liable for the cost of delays attributable to obtaining such service.
- D. CSXT shall have the right to assign an individual to the site of the Project to perform inspection service whenever, in the opinion of CSXT Representative, such inspection may be necessary. Agency shall reimburse CSXT for the costs incurred by CSXT for such inspection service. Inspection service shall not relieve Agency or Contractor from liability for its Work.
- E. CSXT shall render invoices for, and Agency shall pay for, the actual pay rate of the flagpersons and inspectors used, plus standard additives, whether that amount is above or below the rate provided in the Estimate. If the rate of pay that is to be used for inspector or flagging service is changed before the work is started or during the progress of the work, whether by law or agreement between CSXT and its employees, or if the tax rates on labor are changed, bills will be rendered by CSXT and paid by Agency using the new rates. Agency and Contractor shall perform their operations that require flagging protection or inspection service in such a manner and sequence that the cost of such will be as economical as possible.

XI. UTILITY FACILITIES ON CSXT PROPERTY

Agency shall arrange, upon approval from CSXT, to have any utility facilities on or over CSXT Property changed as may be necessary to provide clearances for the proposed trackage.

XII. CLEAN-UP

Agency or Contractor, upon completion of the Project, shall remove from CSXT's Property any temporary grade crossings, any temporary erosion control measures used to control drainage, all machinery, equipment, surplus materials, falsework, rubbish, or temporary buildings belonging to Agency or Contractor. Agency or Contractor, upon completion of the Project, shall leave CSXT Property in neat condition, satisfactory to CSXT Representative.

XIII. FAILURE TO COMPLY

If Agency or Contractor violate or fail to comply with any of the requirements of these Special Provisions, (a) CSXT may require Agency and/or Contractor to vacate CSXT Property; and (b) CSXT may withhold monies due Agency and/or Contractor; (c) CSXT

St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. FL2922

may require Agency to withhold monies due Contractor; and (d) CSXT may cure such failure and the Agency shall reimburse CSXT for the cost of curing such failure.

St. Petersburg, Pinellas County, FL
 Tub-Platform Crossing Surface 46th Avenue N.
 626693F; Florida Zone
 Clearwater Zone; ARE 894.46
 CSXT OP No. FL2922

EXHIBIT D

FORCE ACCOUNT ESTIMATE

ACCT. CODE : 709 - TBD		Form Revision 4/21/2023
ESTIMATE SUBJECT TO REVISION AFTER: 3/11/2025		
CITY: St. Petersburg COUNTY: Pinellas		
DESCRIPTION: 46th Avenue North: Tub-Platform crossing surface upgrade and construction engineering & inspection and flagging services to cover proposed roadway resurfacing.		
ZONE: Florida SUB-DIV: Clearwater		MILE POST: ARE 894.46
AGENCY PROJECT NUMBER: Pinellas County BOCC		
PRELIMINARY ENGINEERING:		
212	Contracted & Administrative Engineering Services	\$ -
	Subtotal	\$ -
CONSTRUCTION ENGINEERING/INSPECTION:		
212	Contracted & Administrative Engineering Services	\$ 30,000
	Subtotal	\$ 30,000
FLAGGING SERVICE: (Contract Labor)		
70	Labor (Conductor-Flagman)	\$ -
50	Labor (Foreman/Inspector) 45 Days @ \$ 504.00	\$ 22,680
70	Additive (Transportation Department)	\$ -
50	Additive 160.00% (Engineering Department)	\$ 36,288
	Subtotal	\$ 58,968
SIGNAL & COMMUNICATIONS WORK: \$ 7,120		
TRACK WORK: \$ 279,637		
PROJECT SUBTOTAL: \$ 375,725		
900	CONTINGENCIES: 10.00%	\$ 37,572
PROJECT TOTAL: **** \$ 413,297		
CURRENT AUTHORIZED BUDGET: **** \$ -		
TOTAL SUPPLEMENT REQUESTED: **** \$ 413,297		
DIVISION OF COST:		
	Agency 100.00%	\$ 413,297
	Railroad 0.00%	\$ -
NOTE: Estimate is based on FULL CROSSING CLOSURE during work by Railroad Forces.		
This estimate has been prepared based on site conditions, anticipated work duration periods, material prices, labor rates, manpower and resource availability, and other factors known as of the date prepared. The actual cost for CSXT work may differ based upon the agency's requirements, their contractor's work procedures, and/or other conditions that become apparent once construction commences or during the progress of the work.		
Office of Chief Engineer Public Projects-Jacksonville, Florida		
Estimated prepared by: Benesch - CDS DATE: 03/11/24		Approved by: KSW CSXT Public Project Group DATE: 03/22/24

St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. FL2922

EXHIBIT E

PAYMENT SCHEDULE

Advance Payment in Full

Upon execution and delivery of notice to proceed with the Project, Agency will deposit with CSXT a sum equal to the Reimbursable Expenses, as shown by the Estimate. If CSXT anticipates that it may incur Reimbursable Expenses in excess of the deposited amount, CSXT will request an additional deposit equal to the then remaining Reimbursable Expenses which CSXT estimates that it will incur. CSXT shall request such additional deposit by delivery of invoices to Agency. Agency shall make such additional deposit within 30 days following delivery of such invoice to Agency.

EXHIBIT F

INSURANCE REQUIREMENTS

I. Insurance Policies:

Agency and Contractor, if and to the extent that either is performing work on or about CSXT's property, shall procure and maintain the following insurance policies:

1. Commercial General Liability coverage at their sole cost and expense with limits of not less than \$5,000,000 in combined single limits for bodily injury and/or property damage per occurrence, and such policies shall name CSXT as an additional named insured. The policy shall include endorsement ISO CG 24 17 evidencing that coverage is provided for work within 50 feet of a railroad. If such endorsement is not included, railroad protective liability insurance must be provided as described in item 4 below.
2. Statutory Worker's Compensation and Employers Liability Insurance with limits of not less than \$1,000,000, which insurance must contain a waiver of subrogation against CSXT and its affiliates (if permitted by state law).
3. Commercial automobile liability insurance with limits of not less than \$1,000,000 combined single limit for bodily injury and/or property damage per occurrence, and such policies shall name CSXT as an additional named insured. The policy shall include endorsement ISO CA 20 70 evidencing that coverage is provided for work within 50 feet of a railroad. If such endorsement is not included, railroad protective liability insurance must be provided as described in item 4 below.
4. Railroad protective liability insurance with limits of not less than \$5,000,000 combined single limit for bodily injury and/or property damage per occurrence and an aggregate annual limit of \$10,000,000, which insurance shall satisfy the following additional requirements:
 - a. The Railroad Protective Insurance Policy must be on the ISO/RIMA Form of Railroad Protective Insurance - Insurance Services Office (ISO) Form CG 00 35.
 - b. CSX Transportation must be the named insured on the Railroad Protective Insurance Policy.
 - c. Name and Address of Contractor and Agency must appear on the Declarations page.

St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone; ARE 894.46
CSXT OP No. FL2922

- d. Description of operations must appear on the Declarations page and must match the Project description.
 - e. Authorized endorsements must include the Pollution Exclusion Amendment - CG 28 31, unless using form CG 00 35 version 96 and later.
 - f. Authorized endorsements may include:
 - (i) Broad Form Nuclear Exclusion - IL 00 21
 - (ii) 30-day Advance Notice of Non-renewal or cancellation
 - (iii) Required State Cancellation Endorsement
 - (iv) Quick Reference or Index - CL/IL 240
 - g. Authorized endorsements may not include:
 - (i) A Pollution Exclusion Endorsement except CG 28 31
 - (ii) A Punitive or Exemplary Damages Exclusion
 - (iii) A "Common Policy Conditions" Endorsement
 - (iv) Any endorsement that is not named in Section 4 (e) or (f) above.
 - (v) Policies that contain any type of deductible
5. All insurance companies must be A. M. Best rated A- and Class VII or better.
 6. The CSX OP number or CSX contract number, as applicable, must appear on each Declarations page and/or certificates of insurance.
 7. Such additional or different insurance as CSXT may require.

II. Additional Terms

1. Contractor must submit the original Railroad Protective Liability policy, Certificates of Insurance and all notices and correspondence regarding the insurance policies to:

Insurance Department
CSX Transportation, Inc.
500 Water Street, C-907
Jacksonville, FL 32202

OR

insurancedocuments@csx.com

2. Neither Agency nor Contractor may begin work on the Project until it has received CSXT's written approval of the required insurance.

St. Petersburg, Pinellas County, FL
Tub-Platform Crossing Surface 46th Avenue N.
626693F; Florida Zone
Clearwater Zone: ARE 894.46
CSXT OP No. FL2922

SCHEDULE I

CONTRACTOR'S ACCEPTANCE

To and for the benefit of CSX Transportation, Inc. ("CSXT") and to induce CSXT to permit Contractor on or about CSXT's property for the purposes of performing work in accordance with the Agreement dated June 4, 2025, between PINELLAS COUNTY, FLORIDA BOARD OF COUNTY COMMISSIONERS and CSXT, Contractor hereby agrees to abide by and perform all applicable terms of the Agreement, including, but not limited to Exhibits C and F to the Agreement, and Sections 3, 9 and 11 of the Agreement.

Contractor: _____

By: _____
Name: _____
Title: _____
Date: _____

\COR\130459.7
