

## **CONSTRUCTION CHANGE ORDER NUMBER 01**

**PROJECT:** St Pete-Clearwater International Airport  
Airport Landside and Parking Lot Improvements - Rebid  
(PID Number: 001546A)

**CONTRACT NO:** 167-0509-CP(PF)

**AGREEMENT DATE:** September 26, 2017

**COMMENCEMENT DATE:** December 26, 2017 (NTP Date)

**AGREEMENT TERM:** 540 consecutive calendar days

**OWNER:** Pinellas County

**CONTRACTOR:** Pepper Contracting Services, Inc.

### **DESCRIPTION:**

This Change Order is for various items related to revisions to the plans and associated time extensions.

### **REASON FOR CHANGE**

The need for this change order is for the following:

1. Convert the cost of the nine (9) bid allowance items, totaling \$965,000.00, to Unspecified Work.
2. Convert the cost of Owners Contingency totaling \$600,000.00 to Unspecified Work.
3. All field Additional Work Authorizations (i.e. Field Directives) executed to date will be applied and paid against the new Unspecified Work line item;
4. Scope of Work revisions due to re-phasing of the project;
5. Addition of new pay items; and quantity adjustment to existing pay items due to required Scope of Work revisions and re-phasing.
6. Revisions to schedule milestones and liquidated damages;
7. Reduction of retainage from ten percent (10%) to five percent (5%);

## **CHANGES TO THE AGREEMENT**

### **1. Conversion of Allowances and Owners Contingency to Unspecified Work**

The following contract items will be converted to Unspecified Work:

|                 |                                            |    |              |
|-----------------|--------------------------------------------|----|--------------|
| Allowance No. 1 | Trash Compactor enclosure (15'x30')        | LS | \$30,000.00  |
| Allowance No. 2 | Permanent Area Lighting – Remote #2        | LS | \$35,000.00  |
| Allowance No. 3 | Relocate Existing Airport Monument Signs   | LS | \$60,000.00  |
| Allowance No. 4 | Portable Changeable Message Sign           | LS | \$15,000.00  |
| Allowance No. 5 | Two 12'x12' DMS signs and sign structure   | LS | \$200,000.00 |
| Allowance No. 6 | Eight portable light banks, (120 days)     | LS | \$50,000.00  |
| Allowance No. 7 | Covered Pedestrian Walkway                 | LS | \$450,000.00 |
| Allowance No. 8 | Parking Lot Directional Signage            | LS | \$50,000.00  |
| Allowance No. 9 | On-site Electrical/Communications Services | LS | \$75,000.00  |

|                    |    |                       |
|--------------------|----|-----------------------|
| Owners Contingency | LS | <u>\$600,000.00</u>   |
| <b>TOTAL</b>       |    | <b>\$1,565,000.00</b> |

Therefore, the new total amount of Unspecified Work will now be \$1,565,000.00.

### **2. New Pay Items and Quantity Adjustments to Existing Pay Items**

Due to unforeseen field conditions, and a need to re-phase the project sequencing, it is necessary to add new pay items with associated unit costs to the project, as well as, quantity adjustments to existing pay items.

Attachment "B" denotes these additions and revisions. The additional costs of these items is \$492,555.62. This amount will be paid from the Unspecified Work amount, set forth above in Section 1.

**Therefore, the balance of the Unspecified Work item will be as follows:**

- Conversion of Allowances/Owners Contingency to Unspecified Work \$1,565,000.00
- Deduction in Unspecified Work due to Additional Costs related to New Pay Items and Quantity Adjustment to Existing Pay Items (\$492,555.62)

|                                    |                       |
|------------------------------------|-----------------------|
| <b>Balance of Unspecified Work</b> | <b>\$1,072,444.38</b> |
|------------------------------------|-----------------------|

### **3. Adjustments to Previous Allowance Items**

The (previous) Allowance items No. 02, No. 05 and No. 07 will no longer be implemented as part of this project. The remaining (previous) Allowance items will be paid from the Balance of Unspecified Work, shown above, set forth in Section 2.

#### 4. Work Authorizations

All Additional Work Authorizations (AWA) executed to date (and previously applied to Owners Contingency and Allowances) will be now be paid from the Balance of the Unspecified Work, set forth in Section 2.

#### 5. Payment for Unspecified Work

Payment for Unspecified Work shall be made according to *Pinellas County Standard Technical Specifications for Roadway and Related Construction (January 2018)* Specification 999-0000 Unspecified Work.

#### 6. Scope of Work Revisions due to alteration of plans

The Owner and the Contractor have mutually agreed that a re-phasing of the project is acceptable to reduce operational impacts to the Airport. (Attachment "A" contains the most recent Maintenance of Traffic (MOT) plans showing the re-phasing of this project). The County and the Contractor have negotiated and mutually agreed to a lump sum cost of three hundred and nineteen thousand three hundred dollars and zero cents (\$319,300.00) to be made in partial payments on a prorated basis as work is completed under a new line item Maintenance of Traffic – Re-Phasing.

An additional one hundred and forty nine (149) calendar days will be also be added to the duration of the project for the Contractor to reach Final Completion.

#### 7. Revisions to schedule milestones and liquidated damages

Contract Section B *Special Conditions* subsection 20(B) *Liquidated Damages* shall be replaced with:

*B. The County shall be entitled to assess, as liquidated damages, but not as a penalty, for each Calendar day after the time specified for Substantial completion and Final completion:*

| <u>Phase</u>           | <u>Calendar days after Notice to Proceed<br/>(NTP December 26, 2017)</u> | <u>Liquidated Damages<br/>per Day</u> |
|------------------------|--------------------------------------------------------------------------|---------------------------------------|
| Substantial Completion | 624 calendar days<br>(September 11, 2019)                                | \$1500.00                             |
| Final Completion       | 689 calendar days<br>(November 15, 2019)                                 | \$1000.00                             |

*The Project shall be deemed to be completed on the date the Work is deemed complete to the satisfaction of the Design Professional/Engineer/Project Manager. The Contractor hereby expressly waives and relinquishes any right which it may have to seek to characterize the above-noted liquidated damages as a penalty. The parties agree that the liquidated damages sum represents a fair and reasonable estimate of the County's actual damages at the time of contracting if the Contractor fails to complete the Work in a timely manner.*

## 8. Reduction of Retainage

Contract Section B *Special Conditions* subsection 25(G) *Payment to Contractor (Retainage)* shall be replaced with:

*G. Retainage: If progress satisfactory to the County is being made by the Contractor, the Contractor will receive partial payments on this Agreement as the Work progresses, based upon estimates of the amount of Work done less payments previously made. In each case 5% of the Agreement Amount earned shall be retained until satisfactory completion and final acceptance of the Project, and final compliance by the Contractor with all terms and conditions of the Contract Documents. Neither progress payment nor partial or entire use or occupancy of the Project by the County shall constitute an acceptance of Work not in accordance with the Contract Documents. The County, prior to making of any payment, may require the Contractor to furnish a certificate or other evidence showing the amount of Work done or completed at that time.*

### **CHANGE IN AGREEMENT PRICE:**

|                                        |                        |
|----------------------------------------|------------------------|
| Original Agreement Amount:             | \$13,238,899.88        |
| Change Order No. 01:                   | \$319,300.00           |
| <b>Final Revised Agreement Amount:</b> | <b>\$13,558,199.88</b> |

Your acceptance of this Change order shall constitute a modification to our Agreement and will be performed subject to all of the same terms and conditions as contained in our Agreement indicated above, as fully as if the same were repeated in this acceptance. Acceptance by Contractor of this adjustment to the agreement shall constitute a full and final settlement and release by Contractor of any and all claims, whether known or unknown, against the Owner arising out of or related to the substance of or the circumstances giving rise to the change or changes set forth herein, including claims for impact and delay costs.

PINELLAS COUNTY,  
FLORIDA  
by and through its Board of  
County Commissioners

ATTEST:

By:

Ken Burke

Clerk of the Court

By:

Chairman  
Board of County  
Commissioners

Date:

APPROVED AS TO FORM

ATTEST:

By:

Terry Ann McNeil  
Project Management Assistant  
Type/Print Name and Title  
(Seal)

By:

By: [Signature]  
Office of the County Attorney

CONTRACTOR:

By:


Doug J. Ebbers  
Executive Vice President

Type/Print Name and Title

**ATTACHMENT “A”**

**Maintenance of Traffic Plans**


V:\SI - Pkg Character (REV)15-27 (Landscape and Parking Improvements)\2. DESIGN (Parking Lot Drawings) - Parking Lot\2018 - REVISED - (PH-101) dwg, Jul 12, 2018 - 8:55am

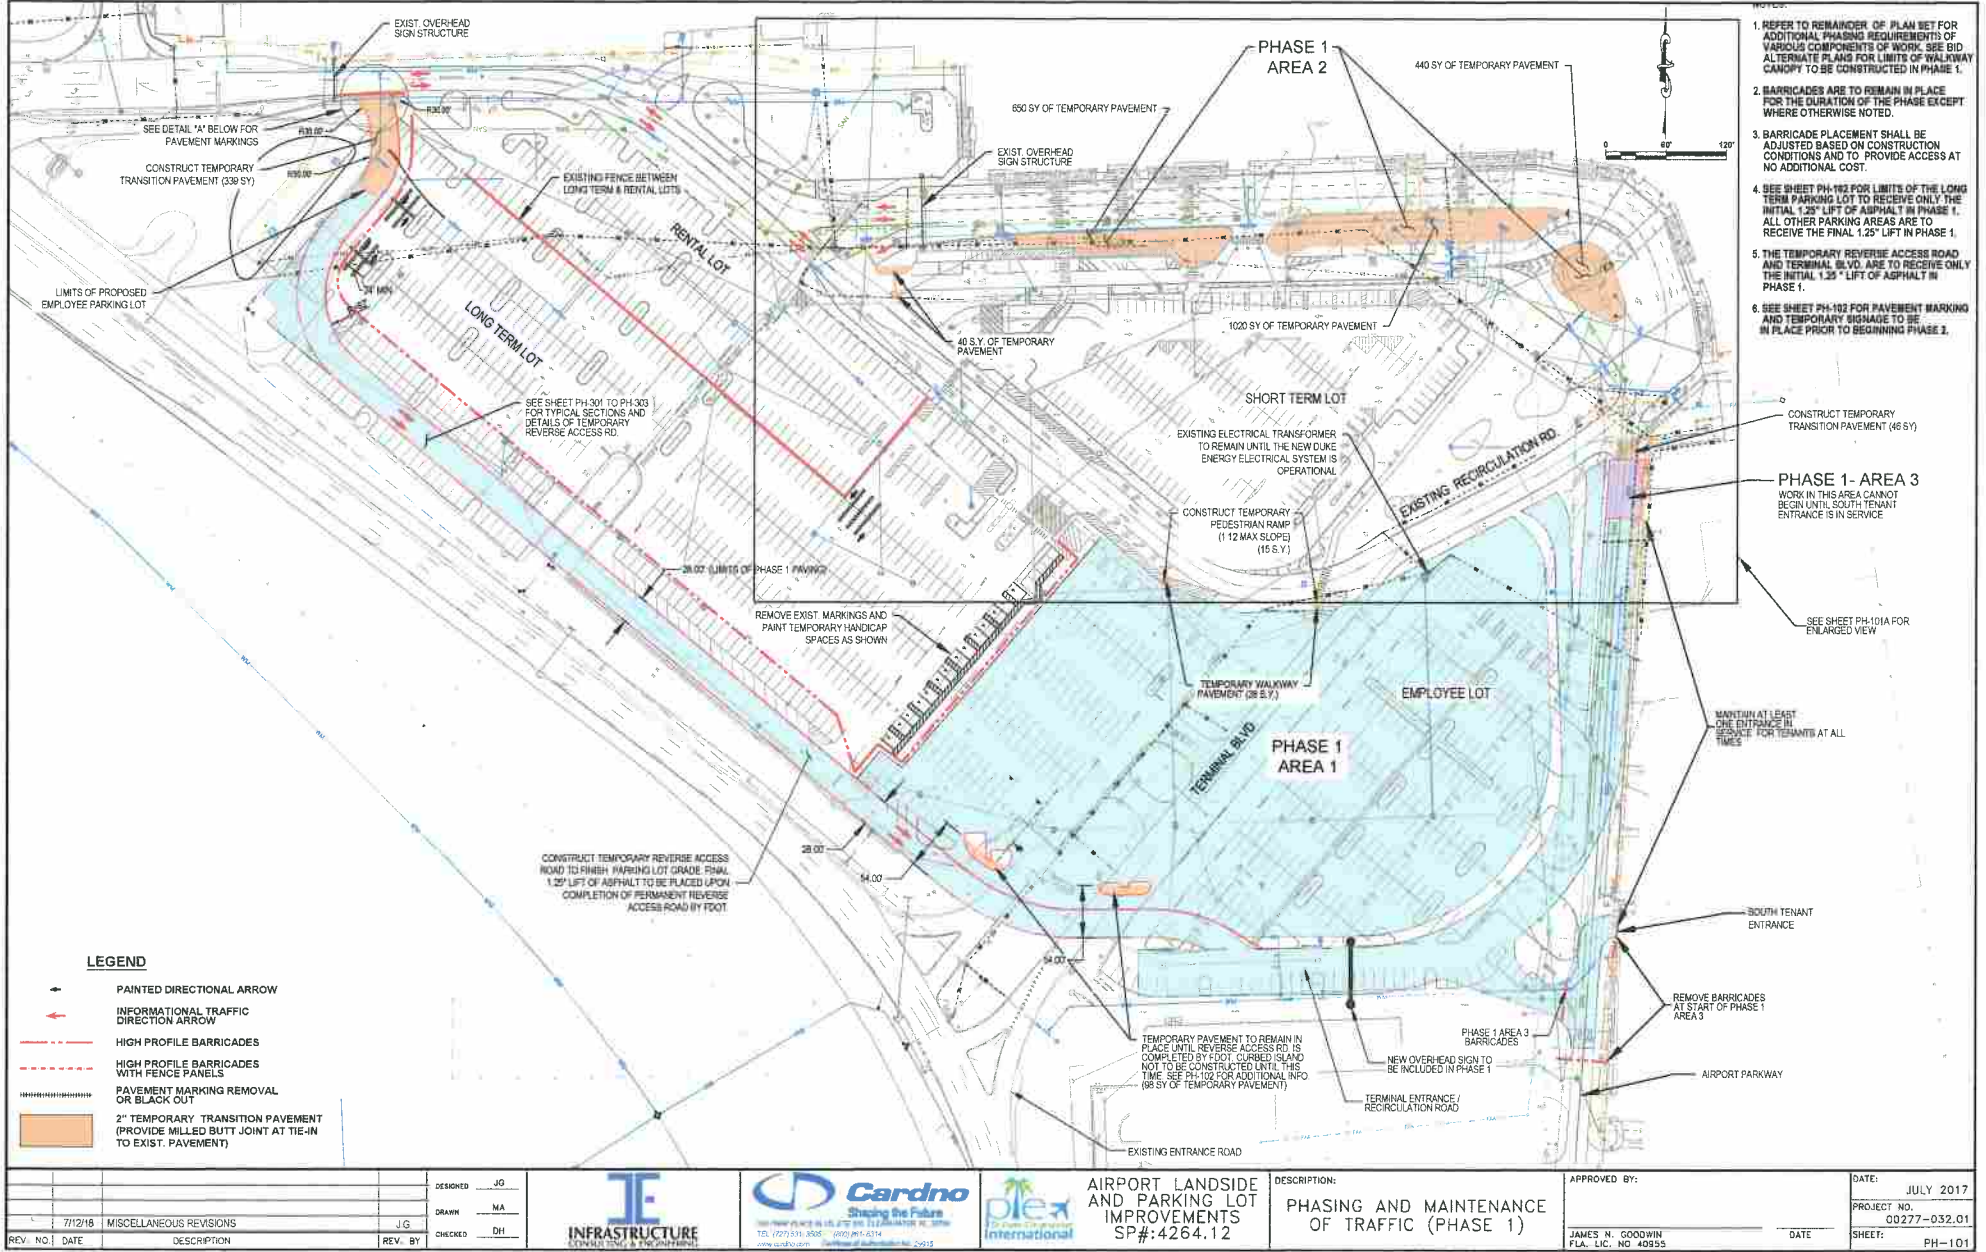



1.151 - Plan Character (P) (V) 15-27 (Construction and Parking Improvements) (2) DESIGN (working L) (Drawings - Parking Lot) (2020) 15-27 PHASING & MAINT OF TRAFFIC PHASE 2 (PH-102-102A) JUL 12, 2018 - 6:25pm


Remove Sign

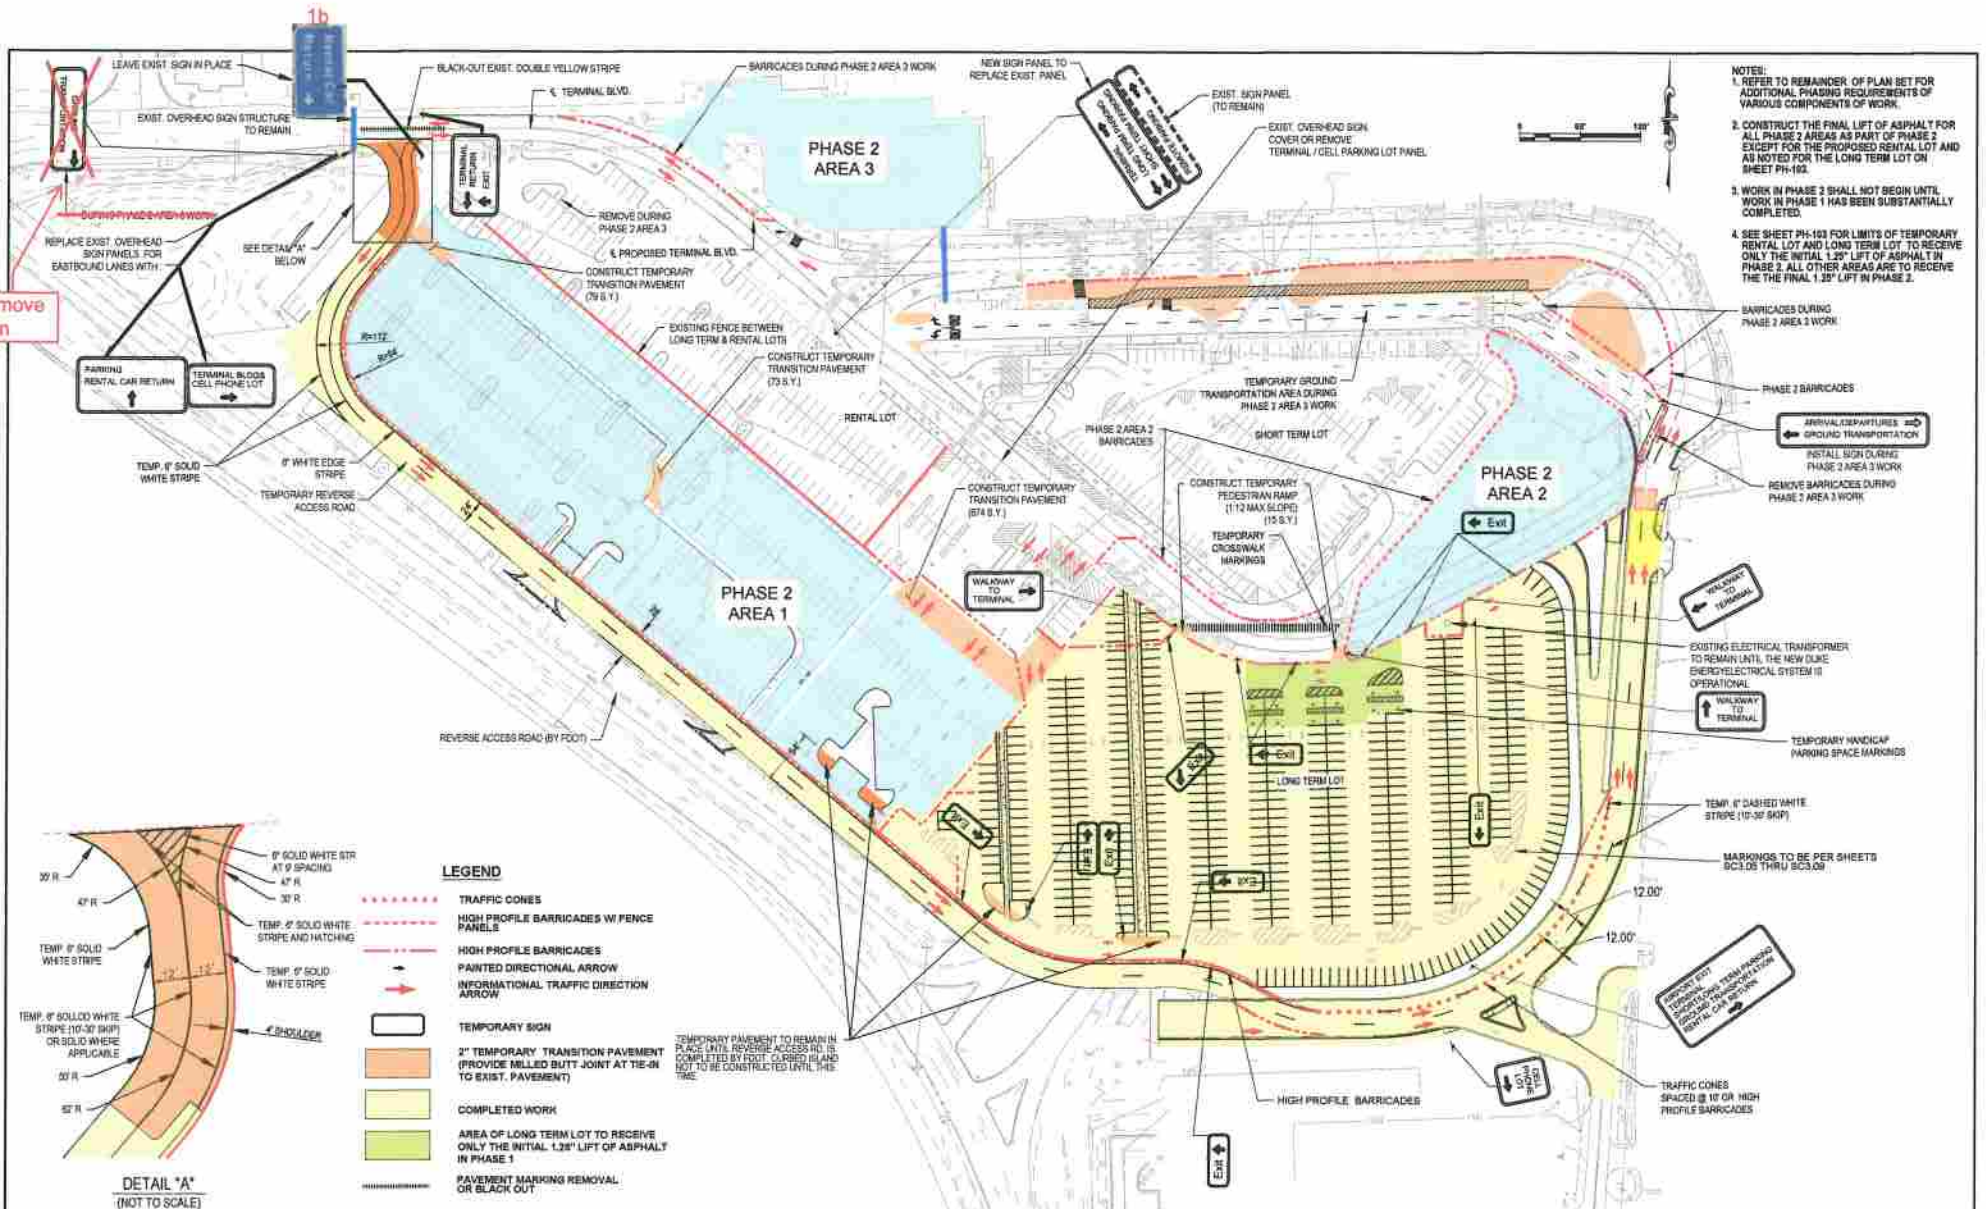

- NOTES:
1. REFER TO REMAINDER OF PLAN SET FOR ADDITIONAL PHASING REQUIREMENTS OF VARIOUS COMPONENTS OF WORK.
  2. CONSTRUCT THE FINAL LIFT OF ASPHALT FOR ALL PHASE 2 AREAS AS PART OF PHASE 2 EXCEPT FOR THE PROPOSED RENTAL LOT AND AS NOTED FOR THE LONG TERM LOT ON SHEET PH-103.
  3. WORK IN PHASE 2 SHALL NOT BEGIN UNTIL WORK IN PHASE 1 HAS BEEN SUBSTANTIALLY COMPLETED.
  4. SEE SHEET PH-103 FOR LIMITS OF TEMPORARY RENTAL LOT AND LONG TERM LOT TO RECEIVE ONLY THE INITIAL 1.25\"/>


**LEGEND**

- TRAFFIC CONES
- HIGH PROFILE BARRICADES W/ FENCE PANELS
- HIGH PROFILE BARRICADES
- PAINTED DIRECTIONAL ARROW
- INFORMATIONAL TRAFFIC DIRECTION ARROW
- TEMPORARY SIGN
- 2\"/>
- COMPLETED WORK
- AREA OF LONG TERM LOT TO RECEIVE ONLY THE INITIAL 1.25\"/>
- PAVEMENT MARKING REMOVAL OR BLACK OUT

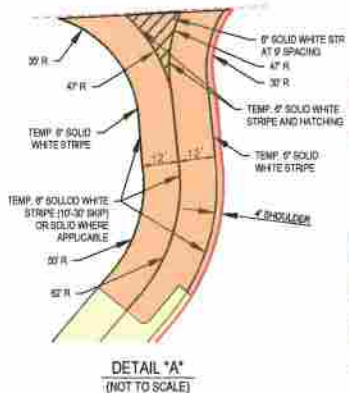


|                                                                                                                                                                                                                                                                                                                                                                                                |
|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|
| <div><div><div><div><div></div><div></div></div><div><div></div><div></div></div></div><div><div></div><div></div></div><div><div></div><div></div></div></div></div> <div><div>REVISION</div><div>DATE</div><div>DESCRIPTION</div><div>REV. BY</div></div> <div><div>7/2/18</div><div></div><div>MISCELLANEOUS REVISIONS</div><div>JLS</div></div> <div><div>CHICKER</div><div>OH</div></div> |
|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|




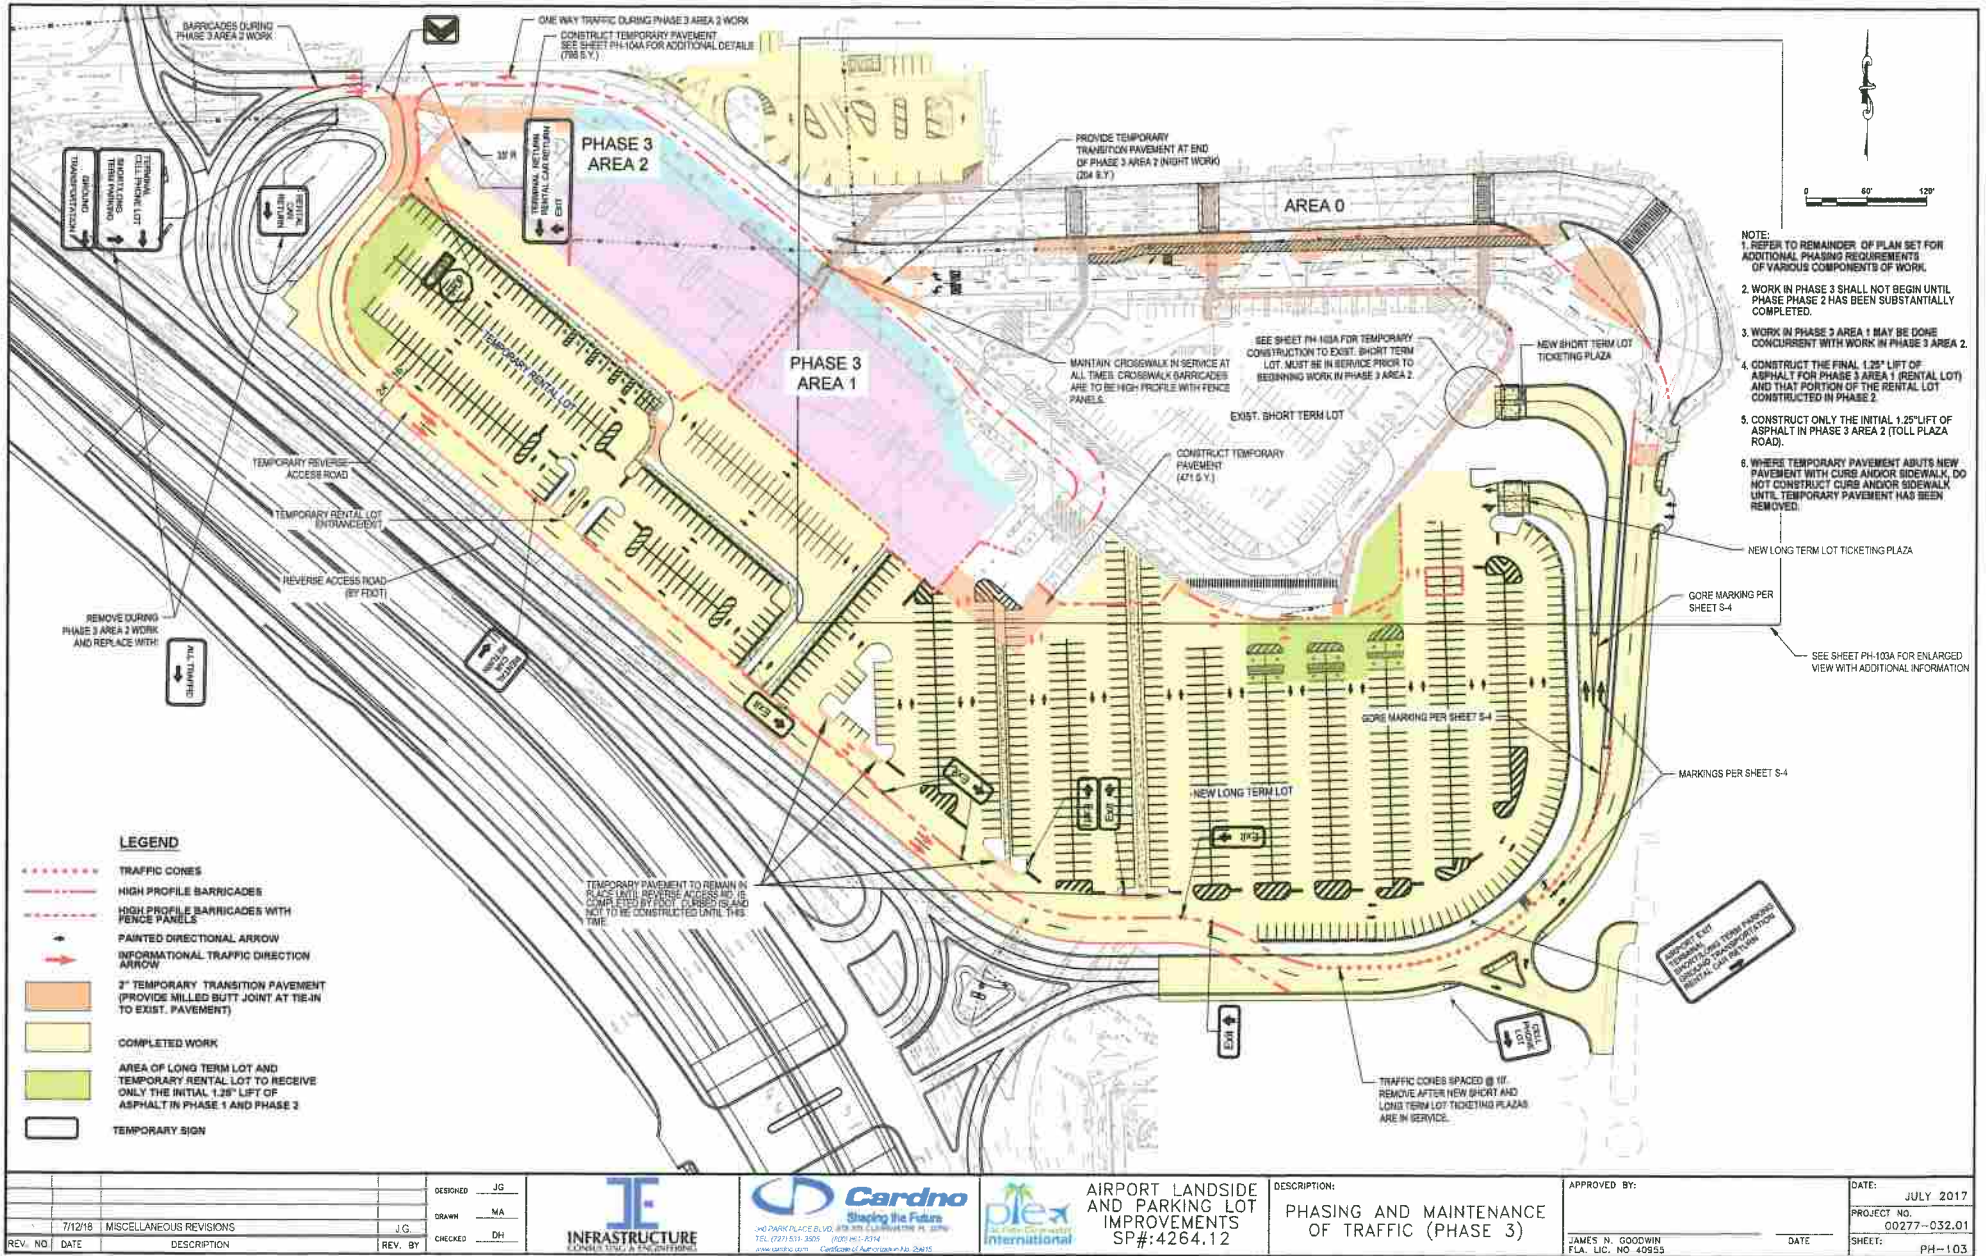




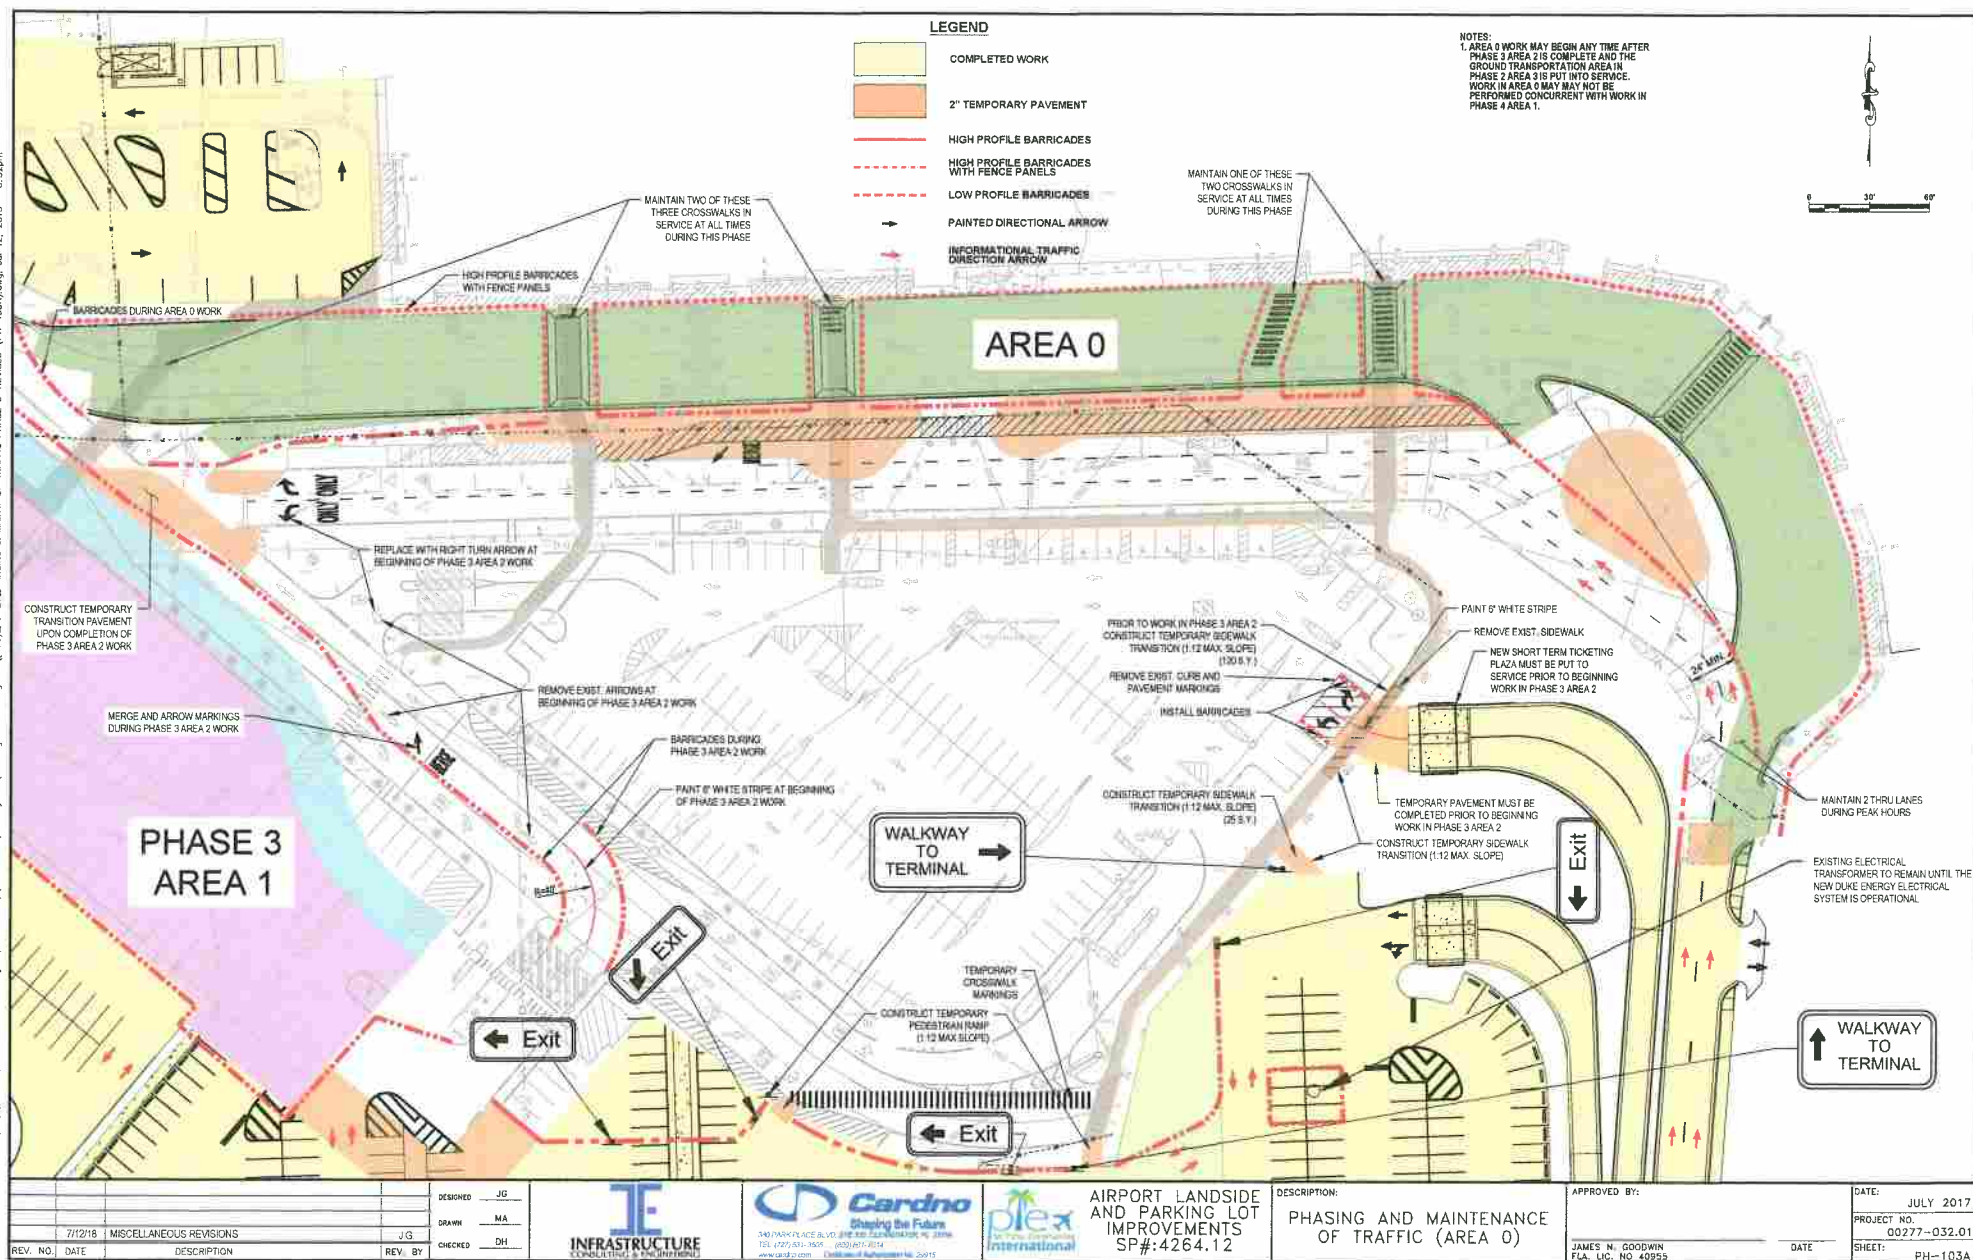



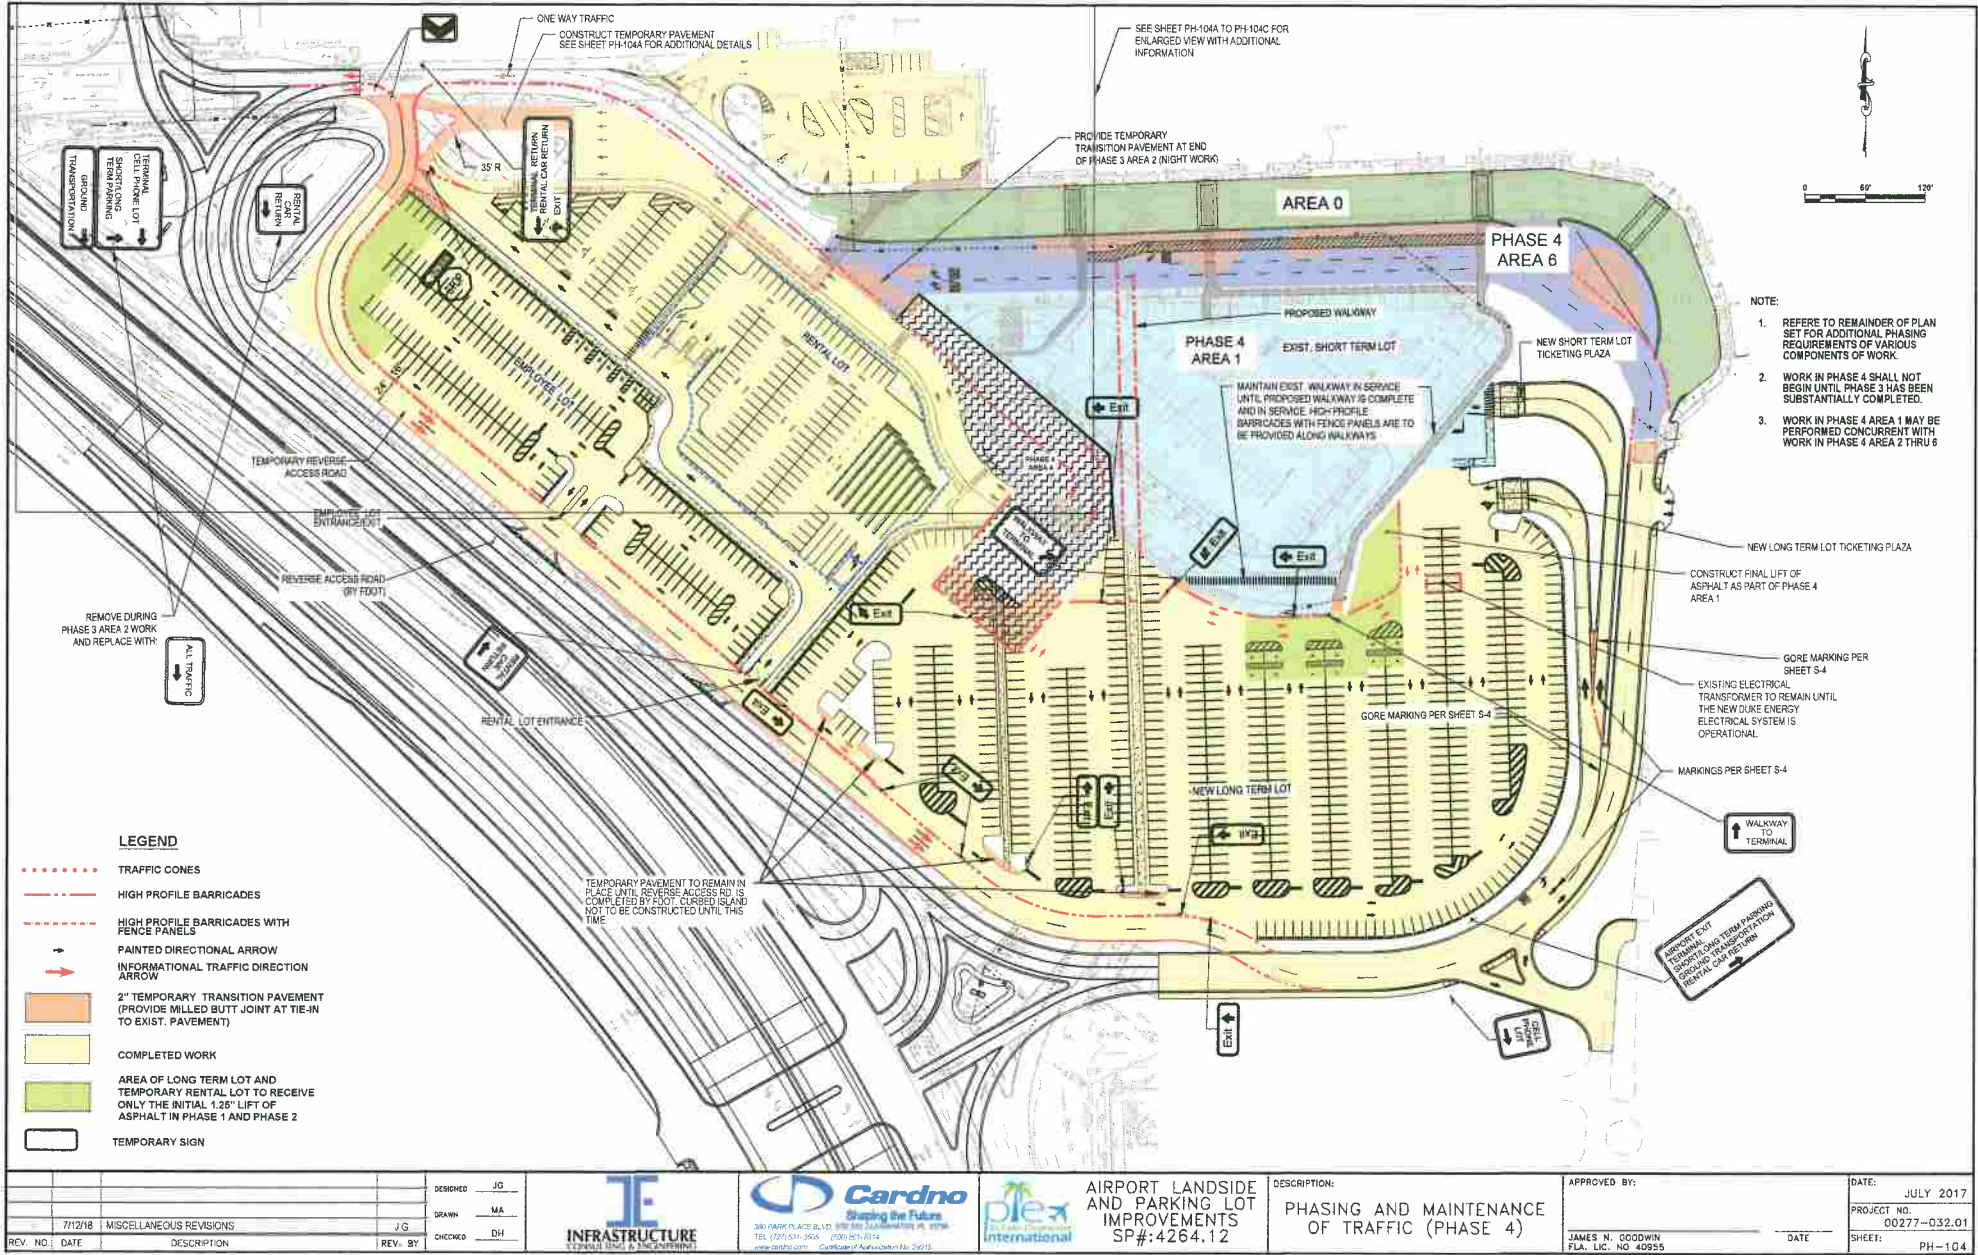



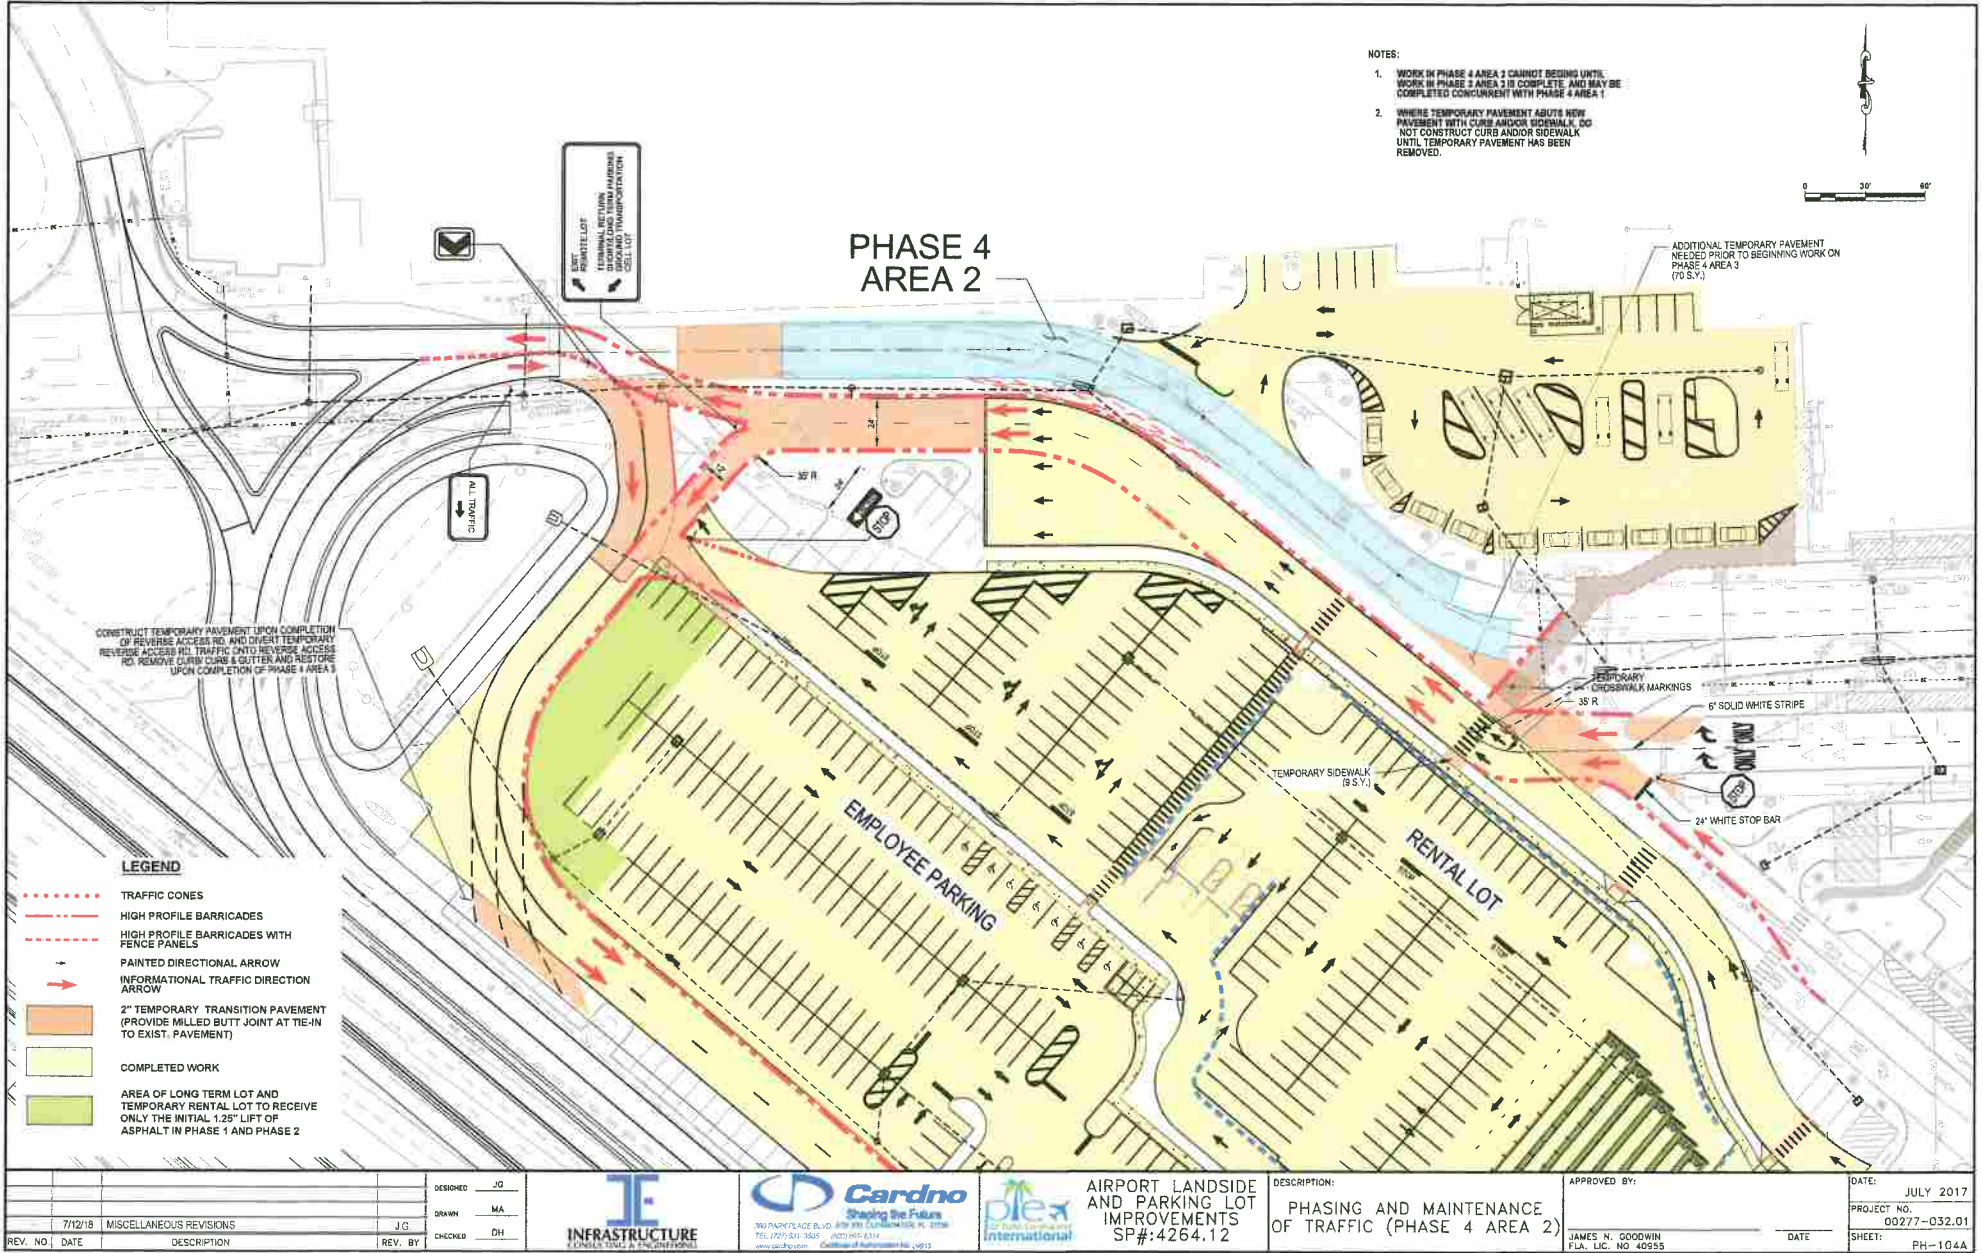




Y:\S1\_Park\_Corridor (PH)\15-27 (Landside and Parking Improvements)\3. DESIGN\Working Set\Drawings - Parking Lot\04B - PH-104B.dwg, Jul 12, 2018 - 7:13pm



|          |         |                         |         |          |    |                                                                                                                                     |                                                                                                                                                                                                                                                                              |                                                                                                                |                                                                   |                                                                            |              |              |       |           |
|----------|---------|-------------------------|---------|----------|----|-------------------------------------------------------------------------------------------------------------------------------------|------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|----------------------------------------------------------------------------------------------------------------|-------------------------------------------------------------------|----------------------------------------------------------------------------|--------------|--------------|-------|-----------|
|          |         |                         |         | DESIGNED | JG | <br>INFRASTRUCTURE<br>(CONSULTING & ENGINEERING) | <br>Cardno<br>Shaping the Future<br>110 TOWN PLACE, SUITE 100, NEW BRUNSWICK, NJ 07102<br>TEL: (732) 331-3600 (800) 291-8214<br>www.cardno.com Certificate of Accreditation to ISO 9001 | <br>Plex<br>International | AIRPORT LANDSIDE<br>AND PARKING LOT<br>IMPROVEMENTS<br>SP#4264.12 | DESCRIPTION:<br><br>PHASING AND MAINTENANCE<br>OF TRAFFIC (PHASE 4 AREA 3) | APPROVED BY: |              | DATE: | JULY 2017 |
|          |         |                         |         | DRAWN    | MA |                                                                                                                                     |                                                                                                                                                                                                                                                                              |                                                                                                                |                                                                   |                                                                            | PROJECT NO.  | C0277-032.01 |       |           |
|          |         |                         |         | CHECKED  | DH |                                                                                                                                     |                                                                                                                                                                                                                                                                              |                                                                                                                |                                                                   |                                                                            | SHEET:       | PH-104B      |       |           |
| REV. NO. | DATE    | DESCRIPTION             | REV. BY |          |    |                                                                                                                                     |                                                                                                                                                                                                                                                                              |                                                                                                                |                                                                   |                                                                            |              |              |       |           |
|          | 7/12/18 | MISCELLANEOUS REVISIONS | JG      |          |    |                                                                                                                                     |                                                                                                                                                                                                                                                                              |                                                                                                                |                                                                   |                                                                            |              |              |       |           |



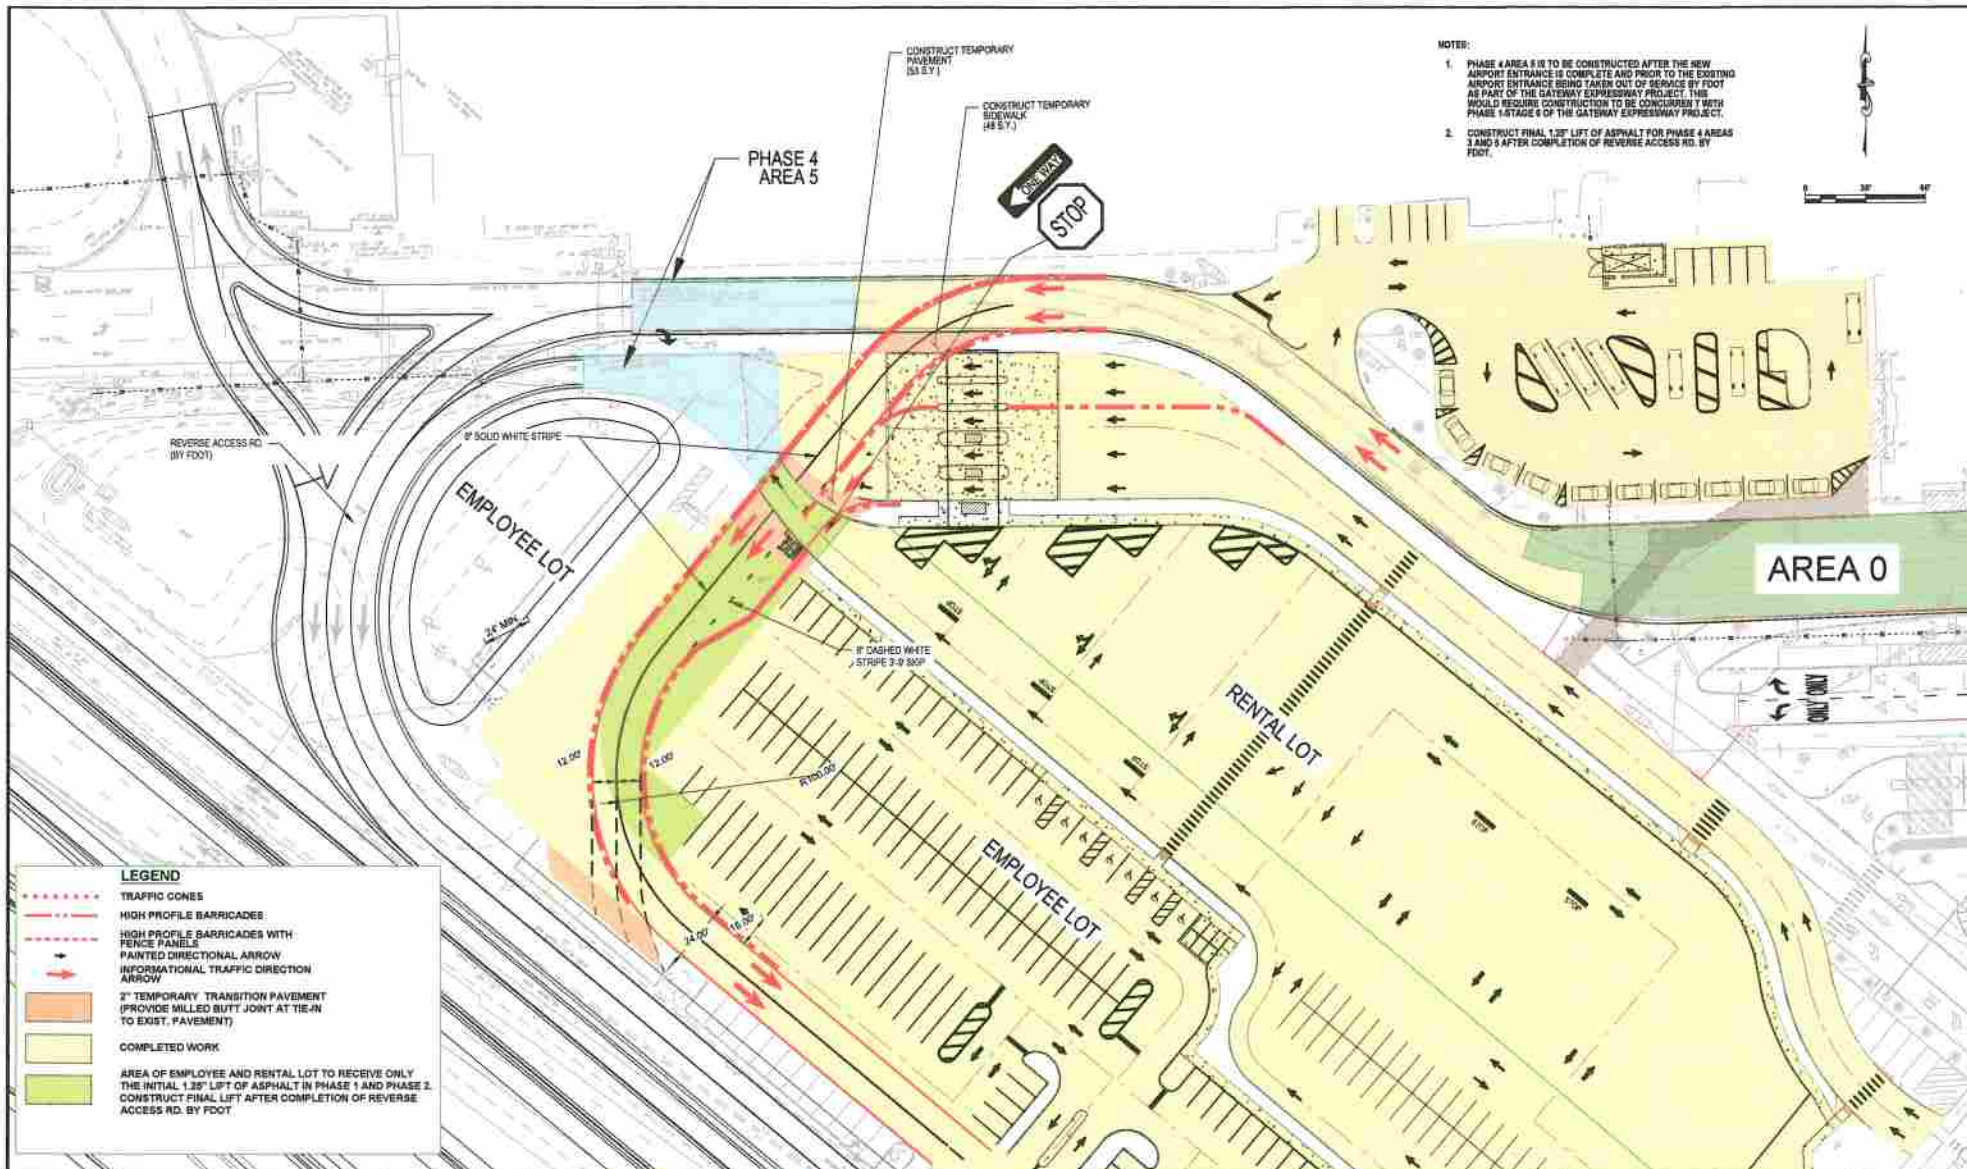

|          |      |             |         |          |    |                                                                                                                                                         |                                                                                                                                             |                                                                                                                                                           |                                                                    |              |                                                        |              |                                         |         |           |
|----------|------|-------------|---------|----------|----|---------------------------------------------------------------------------------------------------------------------------------------------------------|---------------------------------------------------------------------------------------------------------------------------------------------|-----------------------------------------------------------------------------------------------------------------------------------------------------------|--------------------------------------------------------------------|--------------|--------------------------------------------------------|--------------|-----------------------------------------|---------|-----------|
|          |      |             |         | DESIGNED | JG | <br><b>INFRASTRUCTURE</b><br><small>CONSTRUCTION MANAGEMENT</small> | <br><b>Cardno</b><br><small>Shaping the Future</small> | <br><b>Plex International</b><br><small>THE FINEST EXPERTISE</small> | AIRPORT LANDSIDE<br>AND PARKING LOT<br>IMPROVEMENTS<br>SP#:4264.12 | DESCRIPTION: | PHASING AND MAINTENANCE<br>OF TRAFFIC (PHASE 4 AREA 5) | APPROVED BY: | JAMES N. GOODWIN<br>FIA, LIC. NO. 49859 | DATE:   | JULY 2012 |
|          |      |             |         | DRAWN    | MA |                                                                                                                                                         |                                                                                                                                             |                                                                                                                                                           |                                                                    | PROJECT NO.  |                                                        | 00277-032.0  |                                         |         |           |
| REV. NO. | DATE | DESCRIPTION | REV. BY | CHECKED  | DH |                                                                                                                                                         |                                                                                                                                             |                                                                                                                                                           |                                                                    | DATE         |                                                        | SHEET:       |                                         | PH-1040 |           |

**ATTACHMENT "B"**

**Summary of New Pay Items and Quantity Revisions to Existing Pay Items**



# CHANGE ORDER #1 - APPENDIX B – Revised Bid Submittal Sheets

Bid No.: 167-0342-CP(PF)

Bid Title: AIRPORT LANDSIDE AND PARKING LOT IMPROVEMENTS PID# 0015466A

|                                      |           |                                                                     | ORIGINAL CONTRACT |      |                |                          | CHANGE IN CONTRACT   |      |                |                  |
|--------------------------------------|-----------|---------------------------------------------------------------------|-------------------|------|----------------|--------------------------|----------------------|------|----------------|------------------|
| Item No.                             | Spec. No. | Item Description                                                    | BID Quantity      | Unit | Unit Value     | Original Contract Amount | Change In Quantities | Unit | Unit Value     | Change in Amount |
| GENERAL CONSTRUCTION OPERATIONS      |           |                                                                     |                   |      |                |                          |                      |      |                |                  |
| 1                                    | 101 1     | MOBILIZATION                                                        | 1                 | LS   | \$1,100,000.00 | \$1,100,000.00           | 0.00                 | LS   | \$1,100,000.00 | \$0.00           |
| 1A                                   | 101 1     | SURVEY AND LAYOUT BY CONTRACTOR                                     | 1                 | LS   | \$120,000.00   | \$120,000.00             | 0.00                 | LS   | \$120,000.00   | \$0.00           |
| 2                                    | 102 1     | MAINTENANCE OF TRAFFIC                                              | 1                 | LS   | \$400,000.00   | \$400,000.00             | 0.00                 | LS   | \$400,000.00   | \$0.00           |
| 2A                                   | 900-0201* | OFFICE FOR THE ENGINEER (LARGER), 1,500 SQ FT                       | 550               | DA   | \$152.00       | \$83,600.00              | 149.00               | DA   | \$152.00       | \$22,648.00      |
| 2B                                   | 102       | PCMS VARIABLE MESSAGE BOARD                                         |                   |      |                |                          | 360.00               | DA   | \$14.70        | \$5,292.00       |
| 2C                                   | 102 1     | Maintenance of Traffic - RePhasing                                  |                   |      |                |                          | 1.00                 | LS   | \$319,300.00   | \$319,300.00     |
| SECTION SUBTOTAL COST                |           |                                                                     |                   |      |                | \$1,703,600.00           | \$347,240.00         |      |                |                  |
| EROSION CONTROL, CLEARING & GRUBBING |           |                                                                     |                   |      |                |                          |                      |      |                |                  |
| EROSION CONTROL                      |           |                                                                     |                   |      |                |                          |                      |      |                |                  |
| 3                                    | 0104 10 3 | SEDIMENT BARRIER                                                    | 12,000            | LF   | \$2.00         | \$24,000.00              | 0.00                 | LF   | \$2.00         | \$0.00           |
| 4                                    | 0104 11   | FLOATING TURBIDITY BARRIER                                          | 200               | LF   | \$8.00         | \$1,600.00               | 0.00                 | LF   | \$8.00         | \$0.00           |
| 5                                    | 0104 15   | SOIL TRACKING PREVENTION DEVICE                                     | 6                 | EA   | \$2,500.00     | \$15,000.00              | 0.00                 | EA   | \$2,500.00     | \$0.00           |
| 6                                    | 0104 18   | INLET PROTECTION SYSTEM                                             | 123               | EA   | \$80.00        | \$9,840.00               | 0.00                 | EA   | \$80.00        | \$0.00           |
| Subtotal                             |           |                                                                     |                   |      |                | \$80,440.00              | \$0.00               |      |                |                  |
| CLEARING & GRUBBING                  |           |                                                                     |                   |      |                |                          |                      |      |                |                  |
| 7                                    | 110 1 1   | CLEARING & GRUBBING                                                 | 21                | AC   | \$15,305.00    | \$321,405.00             | 0.00                 | AC   | \$15,305.00    | \$0.00           |
| 8                                    | 0110 4    | CURB REMOVAL                                                        | 3,450             | SY   | \$6.00         | \$20,700.00              | 0.00                 | SY   | \$6.00         | \$0.00           |
| 9                                    | 0110 4    | CONCRETE REMOVAL                                                    | 2,800             | SY   | \$6.00         | \$16,800.00              | 0.00                 | SY   | \$6.00         | \$0.00           |
| Subtotal                             |           |                                                                     |                   |      |                | \$368,905.00             | \$0.00               |      |                |                  |
| SECTION TOTAL COST                   |           |                                                                     |                   |      |                | \$409,345.00             | \$0.00               |      |                |                  |
| GRADING AND SITE WORK                |           |                                                                     |                   |      |                |                          |                      |      |                |                  |
| FINAL GRADING                        |           |                                                                     |                   |      |                |                          |                      |      |                |                  |
| 10                                   | 0120 1    | REGULAR EXCAVATION                                                  | 13,613            | CY   | \$6.00         | \$81,678.00              | 0.00                 | CY   | \$6.00         | \$0.00           |
| 11                                   | 0120 4    | SUBSOIL EXCAVATION (UNSUITABLE MATERIAL, CONTINGENCY)               | 1100              | CY   | \$10.00        | \$11,000.00              | 0.00                 | CY   | \$10.00        | \$0.00           |
| 12                                   | 0120 6    | EMBANKMENT                                                          | 24,645            | CY   | \$17.00        | \$418,965.00             | 0.00                 | CY   | \$17.00        | \$0.00           |
| 13                                   | 120-0810* | DEWATERING                                                          | 1                 | LS   | \$20,000.00    | \$20,000.00              | 0.00                 | LS   | \$20,000.00    | \$0.00           |
| Subtotal                             |           |                                                                     |                   |      |                | \$631,643.00             | \$0.00               |      |                |                  |
| SITE WORK                            |           |                                                                     |                   |      |                |                          |                      |      |                |                  |
| 14                                   | 0160 4    | TYPE B STABILIZATION                                                | 78,200            | SY   | \$2.50         | \$195,500.00             | 0.00                 | SY   | \$2.50         | \$0.00           |
| 15                                   | 285704    | OPTIONAL BASE, BASE GROUP 04                                        | 1,500             | SY   | \$21.00        | \$31,500.00              | 6145.00              | SY   | \$21.00        | \$129,045.00     |
| 16                                   | 0285706   | OPTIONAL BASE, BASE GROUP 06                                        | 65,200            | SY   | \$17.00        | \$1,108,400.00           | 1200.00              | SY   | \$17.00        | \$20,400.00      |
| 17                                   | 0285710   | OPTIONAL BASE, BASE GROUP 10 (TYPE B12.5 ONLY)                      | 5,600             | SY   | \$29.00        | \$162,400.00             | 0.00                 | SY   | \$29.00        | \$0.00           |
| 18                                   | 0285710   | OPTIONAL BASE, BASE GROUP 10                                        | 6,200             | SY   | \$29.00        | \$179,800.00             | 0.00                 | SY   | \$29.00        | \$0.00           |
| 19                                   | 0327 70 6 | MILLING EXIST ASPH PAVT, 1 1/2" AVG DEPTH                           | 3,200             | SY   | \$3.00         | \$9,600.00               | 1500.00              | SY   | \$3.00         | \$4,500.00       |
| 19A                                  | 102       | TEMPORARY PAVEMENT SUBCONTRACTOR MOBILIZATION                       |                   | EA   | \$2,500.00     | \$0.00                   | 5.00                 | EA   | \$2,500.00     | \$12,500.00      |
| 20                                   | 0334 1 13 | SUPERPAVE ASPHALTIC CONC, TRAFFIC C                                 | 10,400            | TN   | \$95.00        | \$988,000.00             | 890.00               | TN   | \$95.00        | \$84,550.00      |
| 21                                   | 0337 7 43 | ASPHALT CONCRETE FRICTION COURSE, TRAFFIC C, FC-12.5, PG 76-22, PMA | 1,000             | TN   | \$116.00       | \$116,000.00             | 0.00                 | TN   | \$116.00       | \$0.00           |
| 22                                   | 0339 1    | MISCELLANEOUS ASPHALT PAVEMENT                                      | 1                 | TN   | \$250.00       | \$250.00                 | 0.00                 | TN   | \$250.00       | \$0.00           |
| 23                                   | 0350 4 3  | REINFORCED CEMENT CONCRETE PAVEMENT, 7"                             | 1,500             | SY   | \$83.00        | \$124,500.00             | 0.00                 | SY   | \$83.00        | \$0.00           |
| 24                                   | 350 0207* | CONCRETE CLASS NS, GRAVITY WALL                                     | 7                 | CY   | \$939.00       | \$6,573.00               | 4.00                 | CY   | \$939.00       | \$3,756.00       |
| 25                                   | 0400 0 11 | PEDESTRIAN/ BICYCLE RAILING, ALUMINUM ONLY, 42" TYPE 1              | 85                | LF   | \$73.00        | \$6,205.00               | 22.00                | LF   | \$73.00        | \$1,606.00       |
| 26                                   | 0515 2311 | CONCRETE CURB & GUTTER, TYPE F                                      | 6,000             | LF   | \$25.00        | \$150,000.00             | 0.00                 | LF   | \$25.00        | \$0.00           |
| 27                                   | 0520 1 10 | CONCRETE CURB, TYPE D                                               | 11,500            | LF   | \$12.00        | \$138,000.00             | 0.00                 | LF   | \$12.00        | \$0.00           |
| 28                                   | 0520 2 4  | CONCRETE SIDEWALK AND DRIVEWAYS, 4" THICK                           | 4,200             | SY   | \$34.00        | \$142,800.00             | 6.00                 | SY   | \$34.00        | \$204.00         |
| 29                                   | 0522 1    | CONC SIDEWALK AND DRIVEWAYS, 6" THICK                               | 43                | SY   | \$83.00        | \$3,569.00               | 0.00                 | SY   | \$83.00        | \$0.00           |
| 30                                   | 0522 2    | DETECTABLE WARNINGS                                                 | 600               | SF   | \$29.00        | \$17,400.00              | 0.00                 | SF   | \$29.00        | \$0.00           |
| 31                                   | 0527 2    | BUMPER GUARDS, CONCRETE (PARKING LOT WHEEL STOPS)                   | 429               | EA   | \$71.00        | \$30,459.00              | 0.00                 | EA   | \$71.00        | \$0.00           |
| Subtotal                             |           |                                                                     |                   |      |                | \$3,410,966.00           | \$266,661.00         |      |                |                  |
| SECTION TOTAL COST                   |           |                                                                     |                   |      |                | \$3,942,699.00           | \$266,661.00         |      |                |                  |

# CHANGE ORDER #1 - APPENDIX B – Revised Bid Submittal Sheets

Bid No.: 167-0342-CP(PF)

Bid Title: AIRPORT LANDSIDE AND PARKING LOT IMPROVEMENTS PID# 0015466A

|                               |            |                                                                                                           | ORIGINAL CONTRACT |      |              |                          | CHANGE IN CONTRACT   |      |              |                  |
|-------------------------------|------------|-----------------------------------------------------------------------------------------------------------|-------------------|------|--------------|--------------------------|----------------------|------|--------------|------------------|
| Item No.                      | Spec. No.  | Item Description                                                                                          | BID Quantity      | Unit | Unit Value   | Original Contract Amount | Change In Quantities | Unit | Unit Value   | Change in Amount |
| SIGNING AND PAVEMENT MARKINGS |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
| SIGNING AND PAVEMENT MARKINGS |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
| 32                            | 700 1 11   | SINGLE POST SIGN, F&I GROUND MOUNT, UP TO 12 SF                                                           | 151               | AS   | \$284.00     | \$42,884.00              | 10.00                | AS   | \$284.00     | \$2,840.00       |
| 33                            |            | LEFT BLANK INTENTIONALLY                                                                                  |                   |      |              |                          |                      |      |              |                  |
| 34                            | 700 1 12   | SINGLE POST SIGN, F&I GROUND MOUNT, 12-20 SF                                                              | 19                | AS   | \$777.00     | \$14,763.00              | 5.00                 | AS   | \$777.00     | \$3,885.00       |
| 35                            | 700 1 13   | SINGLE POST SIGN, F&I GROUND MOUNT, 21-30 SF                                                              | 2                 | AS   | \$1,999.00   | \$3,998.00               | 0.00                 | AS   | \$1,999.00   | \$0.00           |
| 36                            | 700 1 60   | SINGLE POST SIGN, REMOVE                                                                                  | 28                | AS   | \$1.00       | \$28.00                  | 0.00                 | AS   | \$1.00       | \$0.00           |
| 37                            | 700-2-14   | MULTI- POST SIGN, F&I GROUND MOUNT, 31-50 SF                                                              | 1                 | AS   | \$4,270.00   | \$4,270.00               | 0.00                 | AS   | \$4,270.00   | \$0.00           |
| 38                            | 700 2 15   | MULTI- POST SIGN, F&I GROUND MOUNT, 51-100 SF                                                             | 4                 | AS   | \$6,977.00   | \$27,908.00              | 0.00                 | AS   | \$6,977.00   | \$0.00           |
| 39                            | 700 2 60   | MULTI- POST SIGN, REMOVE                                                                                  | 3                 | AS   | \$750.00     | \$2,250.00               | 0.00                 | AS   | \$750.00     | \$0.00           |
| 40                            | 700 3 204  | SIGN PANEL, FURNISH & INSTALL OVERHEAD MOUNT, 31-50 SF                                                    | 1                 | EA   | \$1,900.00   | \$1,900.00               | 0.00                 | EA   | \$1,900.00   | \$0.00           |
| 41                            | 700 3 205  | SIGN PANEL, FURNISH & INSTALL OVERHEAD MOUNT, 51-100 SF                                                   | 2                 | EA   | \$2,400.00   | \$4,800.00               | 0.00                 | EA   | \$2,400.00   | \$0.00           |
| 42                            | 700 3 604  | SIGN PANEL, REMOVE, 31-50 SF                                                                              | 6                 | EA   | \$500.00     | \$3,000.00               | 0.00                 | EA   | \$500.00     | \$0.00           |
| 43                            | 700 4 125  | OVERHEAD STATIC SIGN STRUCTURE, FURNISH & INSTALL, SPAN, 51-100 FT                                        | 1                 | EA   | \$105,000.00 | \$105,000.00             | 0.00                 | EA   | \$105,000.00 | \$0.00           |
| 44                            | 700 4 620  | OVERHEAD STATIC SIGN STRUCTURE, REMOVE SPAN                                                               | 2                 | EA   | \$8,000.00   | \$16,000.00              | 1.00                 | EA   | \$8,000.00   | \$8,000.00       |
| 45                            | 715-11137  | LUMINAIRE, SIGN MOUNT                                                                                     | 5                 | EA   | \$3,175.00   | \$15,875.00              | 0.00                 | EA   | \$3,175.00   | \$0.00           |
| 46                            | 700 8 134  | FRONT ACCESS DYNAMIC MESSAGE SIGN, FURNISH & INSTALL- WITH UPS, FULL COLOR, 31-50 SF                      | 1                 | EA   | \$25,000.00  | \$25,000.00              | 0.00                 | EA   | \$25,000.00  | \$0.00           |
| 46A                           | 700 11**   | BILLBOARD, F&I (TWO-SIDED 10'X20' LED DYNAMIC MESSAGE SIGN, DESIGN OF FOUNDATION TO BE INCLUDED IN PRICE) | 1                 | LS   | \$154,146.00 | \$154,146.00             | 0.00                 | LS   | \$154,146.00 | \$0.00           |
| 47                            | 700 8 600  | FRONT ACCESS DYNAMIC MESSAGE SIGN, REMOVE                                                                 | 2                 | EA   | \$5,500.00   | \$11,000.00              | 0.00                 | EA   | \$5,500.00   | \$0.00           |
| 48                            | 706 3      | RETRO-REFLECTIVE PAVEMENT MARKERS                                                                         | 253               | EA   | \$7.00       | \$1,771.00               | 300.00               | EA   | \$7.00       | \$2,100.00       |
|                               |            | BI-DIRECTIONAL WHITE/RED                                                                                  |                   |      |              |                          |                      |      |              |                  |
|                               |            | BI-DIRECTIONAL YELLOW/YELLOW                                                                              |                   |      |              |                          |                      |      |              |                  |
| 49                            | 710 11111  | PAINTED PAVEMENT MARKING, STD, WHITE, SOLID, 6"                                                           | 5.00              | GM   | \$3,538.00   | \$17,690.00              | 2.00                 | GM   | \$3,538.00   | \$7,076.00       |
| 50                            | 710 11123  | PAINTED PAVEMENT MARKING, STD, WHITE, SOLID, 12"                                                          | 2,532             | LF   | \$2.00       | \$5,064.00               | 500.00               | LF   | \$2.00       | \$1,000.00       |
| 51                            | 710 11125  | PAINTED PAVEMENT MARKING, STD, WHITE, SOLID, 24"                                                          | 1,590             | LF   | \$4.00       | \$6,360.00               | 200.00               | LF   | \$4.00       | \$800.00         |
| 52                            | 710 11211  | PAINTED PAVEMENT MARKING, STD, YELLOW, SOLID, 6"                                                          | 0.01              | GM   | \$3,538.00   | \$35.38                  | 1.00                 | GM   | \$3,538.00   | \$3,538.00       |
| 53                            | 710 11160  | PAINTED PAVEMENT MARKING, STD, WHITE, MESSAGE                                                             | 60                | EA   | \$90.00      | \$5,400.00               | 20.00                | EA   | \$90.00      | \$1,800.00       |
| 54                            | 710 11170  | PAINTED PAVEMENT MARKING, STD, WHITE, ARROWS                                                              | 148               | EA   | \$45.00      | \$6,660.00               | 25.00                | EA   | \$45.00      | \$1,125.00       |
| 55                            | 710 11190  | PAINTED PAVEMENT MARKINGS, STANDARD, WHITE, ISLAND NOSE                                                   | 34                | SF   | \$5.00       | \$170.00                 | 0.00                 | SF   | \$5.00       | \$0.00           |
| 56A                           | 710        | CONFLICTING STRIPE REMOVAL/BLACKOUT                                                                       |                   |      |              |                          | 750.00               | SF   | \$5.00       | \$3,750.00       |
| 56                            | 711 11123  | THERMOPLASTIC, STANDARD, WHITE, SOLID, 12" FOR SPEED TABLE ARROWS                                         | 420               | LF   | \$9.00       | \$3,780.00               | 0.00                 | LF   | \$9.00       | \$0.00           |
| 57                            | 711 11124  | THERMOPLASTIC, STANDARD, WHITE, SOLID, 18" FOR DIAGONALS AND CHEVRONS                                     | 290               | LF   | \$5.00       | \$1,450.00               | 0.00                 | LF   | \$5.00       | \$0.00           |
| 58                            | 711 11141  | THERMOPLASTIC, STANDARD, WHITE, 2-4 DOTTED GUIDELINE/ 6-10 GAP EXTENSION, 6"                              | 0.397             | GM   | \$6,224.00   | \$2,470.93               | 0.00                 | GM   | \$6,224.00   | \$0.00           |
| 59                            | 711 11241  | THERMOPLASTIC, STANDARD, YELLOW, 2-4 DOTTED GUIDE LINE /6-10 DOTTED EXTENSION LINE, 6"                    | 0.009             | GM   | \$7,040.00   | \$63.36                  | 0.00                 | GM   | \$7,040.00   | \$0.00           |
| 60                            | 711 14123  | THERMOPLASTIC, PREFORMED, WHITE, SOLID, 12" FOR CROSSWALK                                                 | 625               | LF   | \$9.00       | \$5,625.00               | 0.00                 | LF   | \$9.00       | \$0.00           |
| 61                            | 711 14125  | THERMOPLASTIC, PREFORMED, WHITE, SOLID, 24" FOR CROSSWALK                                                 | 505               | LF   | \$15.00      | \$7,575.00               | 0.00                 | LF   | \$15.00      | \$0.00           |
| 62                            | 711 14160  | THERMOPLASTIC, PREFORMED, WHITE, MESSAGE ONLY                                                             | 2                 | EA   | \$390.00     | \$780.00                 | 0.00                 | EA   | \$390.00     | \$0.00           |
|                               |            | MERGE                                                                                                     |                   |      |              |                          |                      |      |              |                  |
| 63                            | 711 14 170 | THERMOPLASTIC, PREFORMED, WHITE, ARROWS                                                                   | 40                | EA   | \$225.00     | \$9,000.00               | 0.00                 | EA   | \$225.00     | \$0.00           |
|                               |            | DIRECTIONAL ARROW, LEFT                                                                                   |                   |      |              |                          |                      |      |              |                  |
|                               |            | DIRECTIONAL ARROW, THRU                                                                                   |                   |      |              |                          |                      |      |              |                  |
|                               |            | MERGE                                                                                                     |                   |      |              |                          |                      |      |              |                  |
| 64                            | 711 16 101 | THERMOPLASTIC, STANDARD-OTHER SURFACES, WHITE, SOLID, 6"                                                  | 0.595             | GM   | \$6,406.00   | \$3,811.57               | 0.00                 | GM   | \$6,406.00   | \$0.00           |
| 65                            | 711 16 102 | THERMOPLASTIC, STANDARD-OTHER SURFACES, WHITE, SOLID, 8"                                                  | 0.116             | GM   | \$8,180.00   | \$948.88                 | 0.00                 | GM   | \$8,180.00   | \$0.00           |
| 66                            | 711 16 131 | THERMOPLASTIC, OTHER SURFACES, WHITE, SKIP, 6", 10-30 SKIP                                                | 0.346             | GM   | \$2,367.00   | \$818.98                 | 0.00                 | GM   | \$2,367.00   | \$0.00           |
| 67                            | 711 16 201 | THERMOPLASTIC, STANDARD-OTHER SURFACES, YELLOW, SOLID, 6"                                                 | 0.57              | GM   | \$6,460.00   | \$3,682.20               | 0.00                 | GM   | \$6,460.00   | \$0.00           |
| 68                            | 711 16 202 | THERMOPLASTIC, STANDARD-OTHER SURFACES, YELLOW, SOLID, 8"                                                 | 0.023             | GM   | \$7,544.00   | \$173.51                 | 0.00                 | GM   | \$7,544.00   | \$0.00           |
| SECTION TOTAL COST            |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |
|                               |            |                                                                                                           |                   |      |              |                          |                      |      |              |                  |



# **CHANGE ORDER #1 - APPENDIX B – Revised Bid Submittal Sheets**

Bid No.: 167-0342-CP(PF)

Bid Title: AIRPORT LANDSIDE AND PARKING LOT IMPROVEMENTS PID# 0015466A

|                          |             |                                                                    | ORIGINAL CONTRACT |      |            |                          | CHANGE IN CONTRACT   |      |            |                  |
|--------------------------|-------------|--------------------------------------------------------------------|-------------------|------|------------|--------------------------|----------------------|------|------------|------------------|
| Item No.                 | Spec. No.   | Item Description                                                   | BID Quantity      | Unit | Unit Value | Original Contract Amount | Change in Quantities | Unit | Unit Value | Change in Amount |
| DRAINAGE                 |             |                                                                    |                   |      |            |                          |                      |      |            |                  |
| STORM DRAINAGE           |             |                                                                    |                   |      |            |                          |                      |      |            |                  |
| 69A                      | 0425 10     | YARD DRAIN                                                         | 1                 | EA   | \$2,675.00 | \$2,675.00               | 0.00                 | EA   | \$2,675.00 | \$0.00           |
| 69                       | 0425 1341   | INLETS, CURB, TYPE P-4, <10'                                       | 1                 | EA   | \$2,794.00 | \$2,794.00               | 0.00                 | EA   | \$2,794.00 | \$0.00           |
| 70                       | 0425 1351   | INLETS, CURB, TYPE P-5, <10'                                       | 5                 | EA   | \$3,638.00 | \$18,190.00              | 0.00                 | EA   | \$3,638.00 | \$0.00           |
| 71                       | 0425 1361   | INLETS, CURB, TYPE P-6, <10'                                       | 10                | EA   | \$3,062.00 | \$30,620.00              | 0.00                 | EA   | \$3,062.00 | \$0.00           |
| 72                       | 0425 1451   | INLETS, CURB, TYPE J-5, <10'                                       | 5                 | EA   | \$3,638.00 | \$18,190.00              | 0.00                 | EA   | \$3,638.00 | \$0.00           |
| 73                       | 0425 1461   | INLETS, CURB, TYPE J-6, <10'                                       | 3                 | EA   | \$3,062.00 | \$9,186.00               | 0.00                 | EA   | \$3,062.00 | \$0.00           |
| 74                       | 0425 1521   | INLETS, DT BOT, TYPE C, <10'                                       | 7                 | EA   | \$2,896.00 | \$20,272.00              | 0.00                 | EA   | \$2,896.00 | \$0.00           |
| 75                       | 0425 1541   | INLETS, DT BOT, TYPE D, <10'                                       | 2                 | EA   | \$4,302.00 | \$8,604.00               | 0.00                 | EA   | \$4,302.00 | \$0.00           |
| 76                       | 0425 1543   | INLETS, DT BOTTOM, TYPE D, J BOT, <10'                             | 1                 | EA   | \$7,670.00 | \$7,670.00               | 0.00                 | EA   | \$7,670.00 | \$0.00           |
| 77                       | 0425 1561   | INLETS, DT BOT, TYPE F, <10'                                       | 1                 | EA   | \$3,627.00 | \$3,627.00               | 0.00                 | EA   | \$3,627.00 | \$0.00           |
| 78                       | 0425 1563   | INLETS, DT BOTTOM, TYPE F, J BOT, <10'                             | 2                 | EA   | \$5,847.00 | \$11,694.00              | 0.00                 | EA   | \$5,847.00 | \$0.00           |
| 79                       | 0425 1573   | INLETS, DT BOTTOM, TYPE G, J BOT, <10'                             | 1                 | EA   | \$8,684.00 | \$8,684.00               | 0.00                 | EA   | \$8,684.00 | \$0.00           |
| 80                       | 0425 1711   | INLETS, GUTTER, TYPE V, <10'                                       | 19                | EA   | \$4,145.00 | \$78,755.00              | 0.00                 | EA   | \$4,145.00 | \$0.00           |
| 81                       | 0425 1713   | INLETS, GUTTER, TYPE V, J BOT, <10'                                | 5                 | EA   | \$5,533.00 | \$27,665.00              | 0.00                 | EA   | \$5,533.00 | \$0.00           |
| 82                       | 0425 1910   | INLETS, CLOSED FLUME                                               | 1                 | EA   | \$5,553.00 | \$5,553.00               | 0.00                 | EA   | \$5,553.00 | \$0.00           |
| 83                       | 0425 2 61   | MANHOLES, P-8, <10'                                                | 1                 | EA   | \$8,265.00 | \$8,265.00               | 0.00                 | EA   | \$8,265.00 | \$0.00           |
| 84                       | 0425 2 71   | MANHOLES, J-7, <10'                                                | 1                 | EA   | \$4,131.00 | \$4,131.00               | 0.00                 | EA   | \$4,131.00 | \$0.00           |
| 85                       | 0425 2 91   | MANHOLES, J-8, <10'                                                | 3                 | EA   | \$4,132.00 | \$12,396.00              | 1.00                 | EA   | \$4,132.00 | \$4,132.00       |
| LEFT BLANK INTENTIONALLY |             |                                                                    |                   |      |            |                          |                      |      |            |                  |
| 87                       | 0425 5      | MANHOLE, ADJUST                                                    | 2                 | EA   | \$1,017.00 | \$2,034.00               | 0.00                 | EA   | \$1,017.00 | \$0.00           |
| 88A                      | 430175112   | PIPE CULVERT, OPTIONAL MATERIAL, ROUND, 12" S/CD                   | 46                | LF   | \$120.00   | \$5,520.00               | 0.00                 | LF   | \$120.00   | \$0.00           |
| 88                       | 430175118   | PIPE CULVERT, OPTIONAL MATERIAL, ROUND, 18" S/CD                   | 2705              | LF   | \$99.00    | \$267,795.00             | (89.00)              | LF   | \$99.00    | (\$8,811.00)     |
| 89                       | 430175124   | PIPE CULVERT, OPTIONAL MATERIAL, ROUND, 24" S/CD                   | 1384              | LF   | \$104.00   | \$143,936.00             | 0.00                 | LF   | \$104.00   | \$0.00           |
| 90                       | 430175130   | PIPE CULVERT, OPTIONAL MATERIAL, ROUND, 30" S/CD                   | 589               | LF   | \$120.00   | \$70,680.00              | (51.00)              | LF   | \$120.00   | (\$6,120.00)     |
| 90A                      | 430175130   | PIPE CULVERT, OPTIONAL MATERIAL, ROUND, 36" S/CD                   | 0                 | LF   | \$179.00   | \$0.00                   | 51.00                | LF   | \$179.00   | \$9,129.00       |
| 91                       | 430175142   | PIPE CULVERT, OPTIONAL MATERIAL, ROUND, 42" S/CD                   | 497               | LF   | \$179.00   | \$88,963.00              | 0.00                 | LF   | \$179.00   | \$0.00           |
| 92                       | 430175148   | PIPE CULVERT, OPTIONAL MATERIAL, ROUND, 48" S/CD                   | 841               | LF   | \$214.00   | \$179,974.00             | 0.00                 | LF   | \$214.00   | \$0.00           |
| 93                       | 430175236   | PIPE CULVERT, OPT MATERIAL, OTHER SHAPE - ELIP/ARCH, 36" S/CD      | 70                | LF   | \$246.00   | \$17,220.00              | 0.00                 | LF   | \$246.00   | \$0.00           |
| 94                       | 430175242   | PIPE CULVERT, OPT MATERIAL, OTHER SHAPE - ELIP/ARCH, 42" S/CD      | 319               | LF   | \$261.00   | \$83,259.00              | 0.00                 | LF   | \$261.00   | \$0.00           |
| 95                       | 430175248   | PIPE CULVERT, OPT MATERIAL, OTHER SHAPE - ELIP/ARCH, 48" S/CD      | 792               | LF   | \$313.00   | \$247,896.00             | 64.00                | LF   | \$313.00   | \$20,032.00      |
| 96                       | 430982133   | MITERED END SECTION, OPTIONAL ROUND, 30" CD                        | 1                 | EA   | \$4,165.00 | \$4,165.00               | 0.00                 | EA   | \$4,165.00 | \$0.00           |
| 97                       | 430982141   | MITERED END SECTION, OPTIONAL ROUND, 48" CD                        | 1                 | EA   | \$4,971.00 | \$4,971.00               | 0.00                 | EA   | \$4,971.00 | \$0.00           |
| LEFT BLANK INTENTIONALLY |             |                                                                    |                   |      |            |                          |                      |      |            |                  |
| 98                       | 4302010600* | PIPE CULVERT, POLYVINYL CHLORIDE (PVC), ROUND, 6" ID (CONTINGENCY) | 200               | LF   | \$37.00    | \$7,400.00               | 0.00                 | LF   | \$37.00    | \$0.00           |
| 98A                      | 1055 11154  | UTILITY FITTING, F&I, CONCRETE, CAP/PLUG 8-19.9" (12")             | 1                 | EA   | \$137.00   | \$137.00                 | 0.00                 | EA   | \$137.00   | \$0.00           |
| Subtotal                 |             |                                                                    |                   |      |            | \$1,402,921.00           |                      |      |            | \$18,362.00      |
| TEMPORARY STORM DRAINAGE |             |                                                                    |                   |      |            |                          |                      |      |            |                  |
| 99                       | 0425 1563   | INLETS, DITCH BOTTOM, TYPE F, J BOT, <10'                          | 2                 | EA   | \$5,165.00 | \$10,330.00              | 0.00                 | EA   | \$5,165.00 | \$0.00           |
| 100                      | 0425 2 61   | MANHOLES, P-8, <10'                                                | 1                 | EA   | \$3,999.00 | \$3,999.00               | 0.00                 | EA   | \$3,999.00 | \$0.00           |
| 101                      | 430175115   | PIPE CULVERT, OPTIONAL MATERIAL, ROUND, 15" S/CD                   | 16                | LF   | \$79.00    | \$1,264.00               | 0.00                 | LF   | \$79.00    | \$0.00           |
| 102                      | 430175130   | PIPE CULVERT, OPTIONAL MATERIAL, ROUND, 30" S/CD                   | 114               | LF   | \$121.00   | \$13,794.00              | 0.00                 | LF   | \$121.00   | \$0.00           |
| 103                      | 430175148   | PIPE CULVERT, OPTIONAL MATERIAL, ROUND, 48" S/CD                   | 85                | LF   | \$197.00   | \$16,745.00              | 0.00                 | LF   | \$197.00   | \$0.00           |
| Subtotal                 |             |                                                                    |                   |      |            | \$46,132.00              |                      |      |            | \$0.00           |
| SECTION TOTAL COST       |             |                                                                    |                   |      |            | \$1,449,053.00           |                      |      |            | \$18,362.00      |

# CHANGE ORDER #1 - APPENDIX B - Revised Bid Submittal Sheets

Bid No.: 167-0342-CR(PF)

Bid Title: AIRPORT LANDSIDE AND PARKING LOT IMPROVEMENTS PID# 0015466A

|                            |              |                                                                    | ORIGINAL CONTRACT |      |             |                          | CHANGE IN CONTRACT   |      |             |                  |
|----------------------------|--------------|--------------------------------------------------------------------|-------------------|------|-------------|--------------------------|----------------------|------|-------------|------------------|
| Item No.                   | Spec. No.    | Item Description                                                   | BID Quantity      | Unit | Unit Value  | Original Contract Amount | Change In Quantities | Unit | Unit Value  | Change in Amount |
| UTILITIES, WATER AND SEWER |              |                                                                    |                   |      |             |                          |                      |      |             |                  |
| WATER                      |              |                                                                    |                   |      |             |                          |                      |      |             |                  |
| 104                        | 1080 11112   | UTILITY FIXTURES, F&I, 0 - 1.9", SAMPLE POINT (HOSE BIB, DOG PARK) | 2                 | EA   | \$246.00    | \$492.00                 | 0.00                 | EA   | \$246.00    | \$0.00           |
| 105                        | 1050 11222   | UTILITY PIPE, F&I, PVC, WATER / SEWER, 2 - 4.9" (2")               | 30                | LF   | \$19.00     | \$570.00                 | 0.00                 | LF   | \$19.00     | \$0.00           |
| 106                        | 1050 11223   | UTILITY PIPE, F&I, PVC, WATER/SEWER, 5-7.9" (6")                   | 340               | LF   | \$49.00     | \$16,660.00              | 0.00                 | LF   | \$49.00     | \$0.00           |
| 106A                       | 1080 11407   | UTILITY FIXTURES, F&I, 8-19.9", LINE STOP ASSEMBLY (8")            |                   |      |             |                          | 2.00                 | EA   | \$3,750.00  | \$7,500.00       |
| 106B                       | 1080 11407   | UTILITY FIXTURES, F&I, 8-19.9", LINE STOP ASSEMBLY (14")           |                   |      |             |                          | 1.00                 | EA   | \$5,500.00  | \$5,500.00       |
| 107                        | 1050 11224   | UTILITY PIPE, F&I, PVC, WATER/SEWER, 8-19.9 (8")                   | 2,460             | LF   | \$48.00     | \$118,080.00             | 0.00                 | LF   | \$48.00     | \$0.00           |
| 107A                       | 1050 11224   | UTILITY PIPE, F&I, PVC, WATER/SEWER, 8-19.9 (12")                  | 270               | LF   | \$59.00     | \$15,930.00              | 330.00               | LF   | \$59.00     | \$19,470.00      |
| 108                        | 1050 11224   | UTILITY PIPE, F&I, PVC, WATER/SEWER, 8-19.9 (14")                  | 330               | LF   | \$60.00     | \$19,800.00              | (330.00)             | LF   | \$60.00     | (\$19,800.00)    |
| 108A                       | 1050 11321   | UTILITY PIPE, F&I, PE, WATER/SEWER, 0 - 1.9" (3/4")                | 130               | LF   | \$17.00     | \$2,210.00               | 0.00                 | LF   | \$17.00     | \$0.00           |
| 108B                       | 1050 11321   | UTILITY PIPE, F&I, PE, WATER/SEWER, 0 - 1.9" (1")                  | 120               | LF   | \$17.00     | \$2,040.00               | 0.00                 | LF   | \$17.00     | \$0.00           |
| 109                        | 1055 11214   | UTILITY FITTING, F&I, PVC, ELBOW, 8.0-19.9"                        | 12                | EA   | \$186.00    | \$2,232.00               | 0.00                 | EA   | \$186.00    | \$0.00           |
| 110                        | 1055 11224   | UTILITY FITTING, F&I, PVC, TEE, 8.0 -19.9"                         | 14                | EA   | \$168.00    | \$2,352.00               | 0.00                 | EA   | \$168.00    | \$0.00           |
| 111                        | 1055 11234   | UTILITY FITTING, F&I, PVC, REDUCER, 8.0-19.9"                      | 5                 | EA   | \$151.00    | \$755.00                 | 0.00                 | EA   | \$151.00    | \$0.00           |
| 111A                       | 1055 11253   | UTILITY FITTING, F&I, PVC, CAP/PLUG 5.0-7.9" (6")                  | 2                 | EA   | \$79.00     | \$158.00                 | 0.00                 | EA   | \$79.00     | \$0.00           |
| 111B                       | 1055 11254   | UTILITY FITTING, F&I, PVC, CAP/PLUG 8-19.9" (12")                  | 1                 | EA   | \$140.00    | \$140.00                 | 0.00                 | EA   | \$140.00    | \$0.00           |
| 111C                       | 1055 16      | UTILITY FITTING, REMOVE & DISPOSE, PVC, CAP/PLUG 8.0 -19.9" (8")   | 1                 | EA   | \$87.00     | \$87.00                  | 0.00                 | EA   | \$87.00     | \$0.00           |
| 111D                       | 1055 16      | UTILITY FITTING, REMOVE & DISPOSE, PVC, CAP/PLUG 8.0 -19.9" (12")  | 1                 | EA   | \$87.00     | \$87.00                  | 0.00                 | EA   | \$87.00     | \$0.00           |
| 111E                       | 1055 16      | UTILITY FITTING, REMOVE & DISPOSE, PVC, CAP/PLUG 8.0 -19.9" (16")  | 1                 | EA   | \$87.00     | \$87.00                  | 0.00                 | EA   | \$87.00     | \$0.00           |
| 112                        | 1080 11204   | UTILITY FIXTURES, F&I, 2-4.9", VALVE ASSEMBLY                      | 1                 | EA   | \$656.00    | \$656.00                 | 0.00                 | EA   | \$656.00    | \$0.00           |
| 112A                       | 1080 11304   | UTIL FIXT, F&I, 5-7.9", VALVE ASSEMBLY                             | 14                | EA   | \$902.00    | \$12,628.00              | 0.00                 | EA   | \$902.00    | \$0.00           |
| 113                        | 1080 11404   | UTIL FIXT, F&I, 8-19.9", VALVE ASSEMBLY                            | 18                | EA   | \$2,097.00  | \$37,746.00              | 0.00                 | EA   | \$2,097.00  | \$0.00           |
| 113A                       | 1080 11303   | UTILITY FITTING, F&I, TAPPING SLEEVE, 5.0-7.9" (6")                | 2                 | EA   | \$3,284.00  | \$6,568.00               | 0.00                 | EA   | \$3,284.00  | \$0.00           |
| 113B                       | 1080 11403   | UTILITY FITTING, F&I, TAPPING SLEEVE, 8.0-19.9" (8")               | 3                 | EA   | \$3,415.00  | \$10,245.00              | 0.00                 | EA   | \$3,415.00  | \$0.00           |
| 113C                       | 1080 11403   | UTILITY FITTING, F&I, TAPPING SLEEVE, 8.0-19.9" (14")              | 2                 | EA   | \$7,228.00  | \$14,456.00              | 0.00                 | EA   | \$7,228.00  | \$0.00           |
| 113D                       | 1080 11102   | UTILITY FIXTURES, F&I, 0 - 1.9", BACKFLOW ASSEMBLY                 | 3                 | EA   | \$523.00    | \$1,569.00               | 0.00                 | EA   | \$523.00    | \$0.00           |
| 113E                       | 1080 11402   | UTILITY FIXTURES, F&I, 8.0 - 19.9", BACKFLOW ASSEMBLY (8")         | 2                 | EA   | \$2,837.00  | \$5,674.00               | 0.00                 | EA   | \$2,837.00  | \$0.00           |
| 113F                       | 1080 11405   | UTIL FIXT, F&I, 8-19.9", BLOWOFF ASSEMBLY                          | 2                 | EA   | \$2,482.00  | \$4,964.00               | 0.00                 | EA   | \$2,482.00  | \$0.00           |
| 114                        | 1080 11409   | UTILITY FIXTURES, F&I, 8-19.9", MECHANICAL JOINT RESTRAINT         | 100               | EA   | \$81.00     | \$8,100.00               | 0.00                 | EA   | \$81.00     | \$0.00           |
| 114A                       | 1080 11112   | UTILITY FIXTURES, F&I, 0 - 1.9", SAMPLE POINT                      | 3                 | EA   | \$519.00    | \$1,557.00               | 0.00                 | EA   | \$519.00    | \$0.00           |
| 114B                       | 1080 11212   | UTILITY FIXTURES, F&I, 2 - 4.9", SAMPLE POINT (2")                 | 3                 | EA   | \$384.00    | \$1,152.00               | 0.00                 | EA   | \$384.00    | \$0.00           |
| 114C                       | 1080 11312   | UTILITY FIXTURES, F&I, 5.0 - 7.9", SAMPLE POINT (6")               | 10                | EA   | \$536.00    | \$5,360.00               | 0.00                 | EA   | \$536.00    | \$0.00           |
| 114D                       | 1080 11412   | UTILITY FIXTURES, F&I, 8.0 - 19.9", SAMPLE POINT                   | 8                 | EA   | \$548.00    | \$4,384.00               | 0.00                 | EA   | \$548.00    | \$0.00           |
| 115                        | 1644113 08   | FIRE HYDRANT, F&I, STD. 2 HOSE, 1PUMP, 6"                          | 7                 | EA   | \$2,893.00  | \$20,251.00              | 0.00                 | EA   | \$2,893.00  | \$0.00           |
| 115A                       | 1644113 999* | FIRE DEPARTMENT CONNECTION                                         | 1                 | EA   | \$2,751.00  | \$2,751.00               | 0.00                 | EA   | \$2,751.00  | \$0.00           |
| Subtotal                   |              |                                                                    |                   |      |             |                          | \$319,741.00         |      |             |                  |
|                            |              |                                                                    |                   |      |             |                          | \$12,670.00          |      |             |                  |
| SANITARY                   |              |                                                                    |                   |      |             |                          |                      |      |             |                  |
| 116                        | 1050 11223   | UTILITY PIPE, F&I, PVC, WATER/SEWER, 5-7.9" (6")                   | 710               | LF   | \$103.00    | \$73,130.00              | (365.00)             | LF   | \$103.00    | (\$37,595.00)    |
| 117                        | 1050 11224   | UTILITY PIPE, F&I, PVC, WATER/SEWER, 8-19.9 (8")                   | 280               | LF   | \$60.00     | \$16,800.00              | 0.00                 | LF   | \$60.00     | \$0.00           |
| 118                        | 1050 11224   | UTILITY PIPE, F&I, PVC, WATER/SEWER 8-19.9 (10")                   | 2,350             | LF   | \$71.00     | \$166,850.00             | (306.00)             | LF   | \$71.00     | (\$21,726.00)    |
| 119                        | 1055 11273   | UTILITY FITTING, F&I, PVC, CLEANOUT                                | 2                 | EA   | \$68.00     | \$136.00                 | 0.00                 | EA   | \$68.00     | \$0.00           |
|                            |              | LEFT BLANK INTENTIONALLY                                           |                   |      |             |                          |                      |      |             |                  |
| 121A                       | 0425 2 41    | MANHOLES, P-7, <10'                                                | 4                 | EA   | \$3,985.00  | \$15,940.00              | 0.00                 | EA   | \$3,985.00  | \$0.00           |
| 121                        | 0425 2 42    | MANHOLES, P-7, >10'                                                | 6                 | EA   | \$3,985.00  | \$23,910.00              | (2.00)               | EA   | \$3,985.00  | (\$7,970.00)     |
| 122                        | 0425 999**   | GREASE TRAP, F&I                                                   | 1                 | LS   | \$14,831.00 | \$14,831.00              | 0.00                 | LS   | \$14,831.00 | \$0.00           |
| Subtotal                   |              |                                                                    |                   |      |             |                          | \$311,597.00         |      |             |                  |
|                            |              |                                                                    |                   |      |             |                          | (\$67,291.00)        |      |             |                  |
| SECTION TOTAL COST         |              |                                                                    |                   |      |             |                          | \$631,338.00         |      |             |                  |
|                            |              |                                                                    |                   |      |             |                          | (\$64,621.00)        |      |             |                  |

# **CHANGE ORDER #1 - APPENDIX B – Revised Bid Submittal Sheets**

Bid No.: 167-0342-CP(PF)

Bid Title : AIRPORT LANDSIDE AND PARKING LOT IMPROVEMENTS PID# 0015466A

|             |               |                                               | ORIGINAL CONTRACT |      |             |                          | CHANGE IN CONTRACT   |            |             |                  |
|-------------|---------------|-----------------------------------------------|-------------------|------|-------------|--------------------------|----------------------|------------|-------------|------------------|
| Item No.    | Spec. No.     | Item Description                              | BID Quantity      | Unit | Unit Value  | Original Contract Amount | Change In Quantities | Unit       | Unit Value  | Change in Amount |
| LANDSCAPING |               |                                               |                   |      |             |                          |                      |            |             |                  |
| LANDSCAPING |               |                                               |                   |      |             |                          |                      |            |             |                  |
| 123         | 581-900**     | GREEN ASH, 12' HT.                            | 59                | EA   | \$448.00    | \$26,432.00              | (1.00)               | EA         | \$448.00    | (\$448.00)       |
| 124         | 581-901**     | FLORIDA ELM, 12' HT.                          | 71                | EA   | \$318.00    | \$22,578.00              | 1.00                 | EA         | \$318.00    | \$318.00         |
| 125         | 0580-4283     | ROYAL PALM, 12' OVERALL HIGHT/8' CLT.         | 33                | EA   | \$847.00    | \$27,951.00              | 0.00                 | EA         | \$847.00    | \$0.00           |
| 126         | 0580-5142     | SIOUX CRAPE MYRTLE, 8-10' OVERALL HEIGHT      | 8                 | EA   | \$285.00    | \$2,280.00               | 0.00                 | EA         | \$285.00    | \$0.00           |
| 127         | 581-0154*     | FRINGE TREE, 10' HT.                          | 53                | EA   | \$529.00    | \$28,037.00              | 0.00                 | EA         | \$529.00    | \$0.00           |
| 128         | 0580-5142     | MIAMI CRAPE MYRTLE, 8-10' OVERALL HEIGHT      | 38                | EA   | \$272.00    | \$10,336.00              | 0.00                 | EA         | \$272.00    | \$0.00           |
| 129         | 581-0113*     | BALD CYPRESS, 10' HT.                         | 34                | EA   | \$283.00    | \$9,622.00               | 0.00                 | EA         | \$283.00    | \$0.00           |
| 130         | 581-0295*     | DAHOON HOLLY, 8' HT./5' SPR.                  | 59                | EA   | \$278.00    | \$16,402.00              | 0.00                 | EA         | \$278.00    | \$0.00           |
| 131         | 580-902**     | AMERICAN HOLLY, 8' HT./5' SPR.                | 25                | EA   | \$259.00    | \$6,475.00               | 0.00                 | EA         | \$259.00    | \$0.00           |
| 132         | 581-0110*     | CABBAGE PALM, 12' OVERALL HEIGHT/8' CLT.      | 97                | EA   | \$411.00    | \$39,867.00              | 0.00                 | EA         | \$411.00    | \$0.00           |
| 133         | 581-903**     | DWARF SCHEFFLERA, 24" HT.                     | 163               | EA   | \$10.00     | \$1,630.00               | 0.00                 | EA         | \$10.00     | \$0.00           |
| 134         | 581-904**     | PODOCARPUS, 24" HT.                           | 365               | EA   | \$10.00     | \$3,650.00               | 0.00                 | EA         | \$10.00     | \$0.00           |
| 135         | 581-905**     | MRS. SCHILLERS DELIGHT VIBURNUM, 24" HT.      | 51                | EA   | \$10.00     | \$510.00                 | 0.00                 | EA         | \$10.00     | \$0.00           |
| 136         | 581-906**     | JAPANESE PRIVET, 24" HT.                      | 42                | EA   | \$9.00      | \$378.00                 | 0.00                 | EA         | \$9.00      | \$0.00           |
| 137         | 581-907**     | DWARF BURFORD HOLLY, 24" HT.                  | 430               | EA   | \$10.00     | \$4,300.00               | 0.00                 | EA         | \$10.00     | \$0.00           |
| 138         | 0580-6171     | INDIAN HAWTHORNE, 24" HT.                     | 310               | EA   | \$9.00      | \$2,790.00               | 0.00                 | EA         | \$9.00      | \$0.00           |
| 139         | 581-908**     | WHEELER'S DWARF JAPANESE MOCK ORANGE, 18" HT. | 103               | EA   | \$11.00     | \$1,133.00               | 0.00                 | EA         | \$11.00     | \$0.00           |
| 140         | 581-909**     | ANNUALS, 8" SPACING                           | 485               | EA   | \$3.00      | \$1,455.00               | (38.00)              | EA         | \$3.00      | (\$114.00)       |
| 141         | 581-910**     | HAPPY RETURNS DAYLILY, 1 GAL.                 | 121               | EA   | \$4.00      | \$484.00                 | 0.00                 | EA         | \$4.00      | \$0.00           |
| 142         | 581-0310      | MUHLI GRASS, 24" HT.                          | 228               | EA   | \$9.00      | \$2,052.00               | 2.00                 | EA         | \$9.00      | \$18.00          |
| 143         | 581-911**     | CAST IRON PLANT, 12" HT.                      | 38                | EA   | \$9.00      | \$342.00                 | 0.00                 | EA         | \$9.00      | \$0.00           |
| 144         | 581-912**     | NATAL PLUM 'EMERALD BLANKET', 8" HT.          | 594               | EA   | \$4.00      | \$2,376.00               | 0.00                 | EA         | \$4.00      | \$0.00           |
| 145         | 581-913**     | VARIEGATED LILY TURF, 1 GAL.                  | 406               | EA   | \$4.00      | \$1,624.00               | 19.00                | EA         | \$4.00      | \$76.00          |
| 146         | 575-0101*     | ARGENTINE BAHIA SOD                           | 153,764           | SF   | \$0.38      | \$58,430.32              | 25099.00             | SF         | \$0.38      | \$9,537.62       |
| 147         | 570-0100*     | MULCHING                                      | 4,215             | SY   | \$5.00      | \$21,075.00              | 0.00                 | SY         | \$5.00      | \$0.00           |
| 148         | 570-6000*     | TOPSOIL                                       | 1,386             | CY   | \$28.00     | \$38,808.00              | 0.00                 | CY         | \$28.00     | \$0.00           |
| 149         | 0721 75 999** | FLAGPOLE                                      | 1                 | LS   | \$2,500.00  | \$2,500.00               | 0.00                 | LS         | \$2,500.00  | \$0.00           |
| 149A        | 0715 11 1**   | LUMINAIRE (FLAGPOLE GROUND LIGHTS)            | 3                 | EA   | \$202.00    | \$606.00                 | 0.00                 | EA         | \$202.00    | \$0.00           |
| 149B        | 570-999**     | TILLING                                       | 1                 | LS   | \$30,748.00 | \$30,748.00              | 0.00                 | LS         | \$30,748.00 | \$0.00           |
| Subtotal    |               |                                               |                   |      |             |                          | \$364,871.32         | \$9,387.62 |             |                  |



# CHANGE ORDER #1 - APPENDIX B – Revised Bid Submittal Sheets

Bid No.: 167-0342-CP(PF)

Bid Title: AIRPORT LANDSIDE AND PARKING LOT IMPROVEMENTS PID# 0015466A

|                    |              |                                                                                                  | ORIGINAL CONTRACT |      |             |                          | CHANGE IN CONTRACT   |      |             |                  |
|--------------------|--------------|--------------------------------------------------------------------------------------------------|-------------------|------|-------------|--------------------------|----------------------|------|-------------|------------------|
| Item No.           | Spec. No.    | Item Description                                                                                 | BID Quantity      | Unit | Unit Value  | Original Contract Amount | Change In Quantities | Unit | Unit Value  | Change in Amount |
| IRRIGATION         |              |                                                                                                  |                   |      |             |                          |                      |      |             |                  |
| 150                | 0590 3       | IRRIGATION CONTROLLER: RAINBIRD ESPLXD-200 STATION W/ PEDESTAL, IQ CENTRAL CONTROL & RAIN SENSOR | 1                 | EA   | \$6,946.00  | \$6,946.00               | 0.00                 | EA   | \$6,946.00  | \$0.00           |
| 151                | 0590 4       | BACKFLOW PREVENTOR ASSEMBLY. INCLUDES EVERYTHING LISTED IN DETAIL                                | 1                 | EA   | \$1,500.00  | \$1,500.00               | 0.00                 | EA   | \$1,500.00  | \$0.00           |
| 152                | 0590 901**   | 3" MAINLINE - CLASS 200 PVC                                                                      | 3,436             | LF   | \$9.00      | \$30,924.00              | 2851.00              | LF   | \$9.00      | \$25,659.00      |
| 153                | 0590 902**   | LATERAL PIPE - CLASS 200                                                                         | 12,177            | LF   | \$4.75      | \$57,840.75              | 13235.00             | LF   | \$4.75      | \$62,866.25      |
| 154                | 0590 903**   | JOINT RESTRAINTS                                                                                 | 35                | EA   | \$109.00    | \$3,815.00               | 0.00                 | EA   | \$109.00    | \$0.00           |
| 155                | 0590 904**   | SURGE PROTECTORS. INCLUDES DECODER AND GROUNDING PLATES                                          | 19                | EA   | \$258.00    | \$4,902.00               | 0.00                 | EA   | \$258.00    | \$0.00           |
| 156                | 0590 905**   | 14 GAUAGE DIRECT BURIAL WIRE                                                                     | 3,436             | LF   | \$1.00      | \$3,436.00               | 2851.00              | LF   | \$1.00      | \$2,851.00       |
| 157                | 0590 906**   | 1" PRESSURE REFUGULATING ELECTRIC REMOTE CONTROL VALVE                                           | 2                 | EA   | \$593.00    | \$1,186.00               | 0.00                 | EA   | \$593.00    | \$0.00           |
| 158                | 0590 907**   | 1.5" PRESSURE REFUGULATING ELECTRIC REMOTE CONTROL VALVE                                         | 52                | EA   | \$650.00    | \$33,800.00              | (1.00)               | EA   | \$650.00    | (\$650.00)       |
| 159                | 0590 908**   | 1" COMMERCIAL CONTROL ZONE KIT                                                                   | 24                | EA   | \$443.00    | \$10,632.00              | (1.00)               | EA   | \$443.00    | (\$443.00)       |
| 160                | 0590 909**   | SPRAY HEADS: RAINBIRD: 1806-S-PRS                                                                | 1,482             | EA   | \$26.00     | \$38,532.00              | 12.00                | EA   | \$26.00     | \$312.00         |
| 161                | 0590 910**   | ROTORS: RAINBIRD 5004-SAM-PRS                                                                    | 176               | EA   | \$33.00     | \$5,808.00               | 4.00                 | EA   | \$33.00     | \$132.00         |
| 162                | 0590 911**   | DRIPLINE, 1/2" DIA RAINBIRD BLACK STRIP TUBING (XBS 500P)                                        | 200               | LF   | \$1.00      | \$200.00                 | 27000.00             | LF   | \$1.00      | \$27,000.00      |
| 163                | 0590 912**   | RAINBIRD QUICK COUPLER MODEL 5 LRC. INCLUDES VALVE BOX                                           | 18                | EA   | \$323.00    | \$5,814.00               | 0.00                 | EA   | \$323.00    | \$0.00           |
| 164                | 0590 913**   | RESILIENT WEDGE ISOLATION VALVE. INCLUDES VALVE BOX                                              | 22                | EA   | \$650.00    | \$14,300.00              | 1.00                 | EA   | \$650.00    | \$650.00         |
| 165                | 0590 914**   | PAIGE DECODER CABLE FUSE DEVICE                                                                  | 4                 | EA   | \$317.00    | \$1,268.00               | 0.00                 | EA   | \$317.00    | \$0.00           |
| 166                | 0590 915**   | FLOW SENSOR (FS200P). INCLUDES DECODER                                                           | 1                 | EA   | \$860.00    | \$860.00                 | 0.00                 | EA   | \$860.00    | \$0.00           |
| 167                | 0590 916**   | MASTER VALVE. INCLUDES VALVE BOX & DECODER                                                       | 1                 | EA   | \$955.00    | \$955.00                 | 0.00                 | EA   | \$955.00    | \$0.00           |
| 168A               | 0591 1.3     | 6" UNDERPAVEMENT SLEEVING                                                                        |                   |      |             |                          | 1045.00              | LF   | \$9.75      | \$10,188.75      |
| 168                | 0591 1.2     | 4" UNDERPAVEMENT SLEEVING                                                                        | 720               | LF   | \$5.00      | \$3,600.00               | (363.00)             | LF   | \$5.00      | (\$1,815.00)     |
| 169                | 0591 1.1     | 2" UNDERPAVEMENT SLEEVING                                                                        | 758               | LF   | \$3.00      | \$2,274.00               | 977.00               | LF   | \$3.00      | \$2,931.00       |
| 170                | 0751 37      | TRASH RECEPTACLE                                                                                 | 33                | EA   | \$ 761.00   | \$25,113.00              | 0.00                 | EA   | \$ 761.00   | \$0.00           |
| Subtotal           |              |                                                                                                  |                   |      |             | \$263,706.76             |                      |      |             | \$129,682.00     |
| DOG PARK           |              |                                                                                                  |                   |      |             |                          |                      |      |             |                  |
| 171                | 0285998**    | DECOMPOSED GRANITE                                                                               | 1,325             | SF   | \$3.00      | \$3,975.00               | 0.00                 | SF   | \$3.00      | \$0.00           |
| 171A               | 0285998**    | ARTIFICIAL TURF, ALTERNASCAPES, EASY TURF                                                        |                   |      |             |                          | 3105.00              | SF   | \$15.00     | \$46,575.00      |
| 172                | 0285999**    | ABC STONE BASE                                                                                   | 16                | SY   | \$200.00    | \$3,200.00               | 0.00                 | SY   | \$200.00    | \$0.00           |
| 173                | 0751 997*    | PET WASTE STATION: TERRABOUND SOLUNTIONS, SENTRY DOG WASTE STATION                               | 2                 | EA   | \$22,260.00 | \$44,520.00              | 0.00                 | EA   | \$22,260.00 | \$0.00           |
| 174                | 0751 998*    | PET DUAL WATER FOUNTAIN: TERRABOUND SOLUTIONS, SURFACE MOUNT                                     | 2                 | EA   | \$3,500.00  | \$7,000.00               | 0.00                 | EA   | \$3,500.00  | \$0.00           |
| 175                | 0751 999*    | 4" METAL EDGING                                                                                  | 400               | LF   | \$6.00      | \$2,400.00               | 0.00                 | LF   | \$6.00      | \$0.00           |
| 176                | 550 10 999** | 5' TALL BLACK ALUMINUM FENCE INCLUDES GATES                                                      | 400               | LF   | \$50.00     | \$20,000.00              | 0.00                 | LF   | \$50.00     | \$0.00           |
| 177                | 522 1        | CONCRETE SIDEWALKS AND DRIVEWAYS, 4" THICK                                                       | 18                | SY   | \$147.00    | \$2,646.00               | 0.00                 | SY   | \$147.00    | \$0.00           |
| Subtotal           |              |                                                                                                  |                   |      |             | \$83,741.00              |                      |      |             | \$46,675.00      |
| SECTION TOTAL COST |              |                                                                                                  |                   |      |             | \$702,318.07             |                      |      |             | \$186,644.62     |

# CHANGE ORDER #1 - APPENDIX B - Revised Bid Submittal Sheets

Bid No.: 167-0342-CP(PF)

Bid Title: AIRPORT LANDSIDE AND PARKING LOT IMPROVEMENTS PID# 0015466A

|                             |             |                                                                         | ORIGINAL CONTRACT |      |             |                          | CHANGE IN CONTRACT   |      |             |                  |
|-----------------------------|-------------|-------------------------------------------------------------------------|-------------------|------|-------------|--------------------------|----------------------|------|-------------|------------------|
| Item No.                    | Spec. No.   | Item Description                                                        | BID Quantity      | Unit | Unit Value  | Original Contract Amount | Change in Quantities | Unit | Unit Value  | Change in Amount |
| ELECTRICAL & COMMUNICATIONS |             |                                                                         |                   |      |             |                          |                      |      |             |                  |
| COMMUNICATIONS              |             |                                                                         |                   |      |             |                          |                      |      |             |                  |
| 178                         | 1050 11212  | UTILITY PIPE, F&I, PVC, CASING / CONDUIT, 2-4 9"                        | 11,160            | LF   | \$16.00     | \$178,560.00             | 735.00               | LF   | \$16.00     | \$11,760.00      |
| 178A                        | 630 2 12    | CONDUIT, FURNISH & INSTALL, DIRECTIONAL BORE (4 RUNS OF 4" @ 210')      | 840               | LF   | \$52.00     | \$43,680.00              | 0.00                 | LF   | \$52.00     | \$0.00           |
| 179                         | 0633 1122   | FIBER OPTIC CABLE, F&I, UNDERGROUND, 13-48 FIBERS                       | 15,000            | LF   | \$5.00      | \$75,000.00              | 455.00               | LF   | \$5.00      | \$2,275.00       |
| 180                         | 0633 2 32   | FIBER OPTIC CONNECTION, INSTALL, TERMINATION                            | 372               | EA   | \$44.00     | \$16,368.00              | 0.00                 | EA   | \$44.00     | \$0.00           |
| 181                         | 0633 3 16   | FIBER OPTIC CONNECTION HARDWARE, F&I, PATCH PANEL- FIELD TERMINATED     | 7                 | EA   | \$7,556.00  | \$52,892.00              | 0.00                 | EA   | \$7,556.00  | \$0.00           |
| 182                         | 0635 2 12   | PULL & SPLICE BOX, F&I, 24" X 36" COVER SIZE                            | 17                | EA   | \$3,860.00  | \$65,620.00              | 0.00                 | EA   | \$3,860.00  | \$0.00           |
| 183                         | 0676 2132   | ITS CABINET, FURNISH & INSTALL, BASE MOUNT, 336S, 24" W X 46" H X 22" D | 5                 | EA   | \$3,247.00  | \$16,235.00              | 0.00                 | EA   | \$3,247.00  | \$0.00           |
| 184                         | 0680 106    | SYSTEM CONTROL EQUIPMENT,F&I, COMMUNICATION INTERFACE                   | 5                 | EA   | \$6,950.00  | \$34,750.00              | 0.00                 | EA   | \$6,950.00  | \$0.00           |
| 185                         | 0682 113    | ITS CCTV CAMERA, F&I, DOME ENCLOSURE - NON PRESSURIZED                  | 5                 | EA   | \$10,207.00 | \$51,035.00              | 0.00                 | EA   | \$10,207.00 | \$0.00           |
| 186                         | 0682 901**  | DIRECT BURIAL CAMERA POLE                                               | 5                 | EA   | \$3,571.00  | \$17,855.00              | 0.00                 | EA   | \$3,571.00  | \$0.00           |
| 187                         | 0682 902**  | SECURITY CONTROLLERS                                                    | 3                 | EA   | \$18,040.00 | \$54,120.00              | 0.00                 | EA   | \$18,040.00 | \$0.00           |
| 188                         | 0682 903**  | BARRIER SECURITY GATE                                                   | 4                 | EA   | \$2,528.00  | \$10,112.00              | 0.00                 | EA   | \$2,528.00  | \$0.00           |
| 189                         | 0682 904**  | DATA OUTLETS - EXIT PLAZA                                               | 7                 | EA   | \$481.00    | \$3,367.00               | 0.00                 | EA   | \$481.00    | \$0.00           |
| 190                         | 0682 905**  | ACCESS CONTROL CARD READER AND VEHICLE PEDESTAL                         | 2                 | EA   | \$5,842.00  | \$11,684.00              | 0.00                 | EA   | \$5,842.00  | \$0.00           |
| 191                         | 0682 906**  | ACCESS CONTROL DURESS BUTTON - EXIT PLAZA                               | 3                 | EA   | \$1,786.00  | \$5,358.00               | 0.00                 | EA   | \$1,786.00  | \$0.00           |
| 192                         | 0682 907**  | TOLL BOOTH WALL MOUNTED DATA CABINET                                    | 1                 | EA   | \$2,079.00  | \$2,079.00               | 0.00                 | EA   | \$2,079.00  | \$0.00           |
| 193                         | 0682 908**  | CCTV CAMERA FIXED                                                       | 4                 | EA   | \$7,470.00  | \$29,880.00              | 0.00                 | EA   | \$7,470.00  | \$0.00           |
| 194                         | 0682 909**  | VEHICLE GATE ROUGH IN                                                   | 13                | EA   | \$500.00    | \$6,500.00               | 0.00                 | EA   | \$500.00    | \$0.00           |
| 195                         | 0682 998**  | EXISTING IT INFRASTRUCTURE RE-WORK                                      | 1                 | EA   | \$10,392.00 | \$10,392.00              | 0.00                 | EA   | \$10,392.00 | \$0.00           |
| 196                         | 0682 999**  | FAA STRUCTURE REPLACEMENT                                               | 4                 | EA   | \$5,618.00  | \$22,472.00              | 0.00                 | EA   | \$5,618.00  | \$0.00           |
| 197                         | 0350 3 13   | PLAIN CEMENT CONCRETE PAVEMENT, 12" (FAA SADDLES)                       | 120               | SY   | \$304.00    | \$36,480.00              | 0.00                 | SY   | \$304.00    | \$0.00           |
| Subtotal                    |             |                                                                         |                   |      |             | \$744,439.00             |                      |      |             | \$14,035.00      |
| ELECTRICAL                  |             |                                                                         |                   |      |             |                          |                      |      |             |                  |
| 198                         | 635-2-11E   | PULL AND SPLICE BOX, ELECTRICAL                                         | 32                | EA   | \$1,085.00  | \$34,720.00              | 12.00                | EA   | \$1,085.00  | \$13,020.00      |
| 199                         | 639-3-12    | ELECTRICAL SERVICE DISCONNECT, F&I, POLE MOUNT (include unistrut)       | 3                 | EA   | \$1,486.00  | \$4,458.00               | 0.00                 | EA   | \$1,486.00  | \$0.00           |
| 200                         |             | LEFT BLANK INTENTIONALLY                                                |                   |      |             |                          |                      |      |             |                  |
| 201                         | 715-11-113  | LUMINAIRE, POLE TOP                                                     | 117               | EA   | \$557.00    | \$65,169.00              | 0.00                 | EA   | \$557.00    | \$0.00           |
| 202                         | 715-11137   | LUMINAIRE, SIGN MOUNT                                                   | 5                 | EA   | \$1,144.00  | \$5,720.00               | 0.00                 | EA   | \$1,144.00  | \$0.00           |
| 203                         | 715-1-12    | LIGHTING CONDUCTORS, INSULATED NO.8 CU                                  | 49,260            | LF   | \$1.00      | \$49,260.00              | 2390.00              | LF   | \$1.00      | \$2,390.00       |
| 204                         | 715-1-11    | LIGHTING CONDUCTORS, INSULATED NO.10 CU                                 | 815               | LF   | \$2.00      | \$1,630.00               | 0.00                 | LF   | \$2.00      | \$0.00           |
| 205                         | 715-7-11    | LOADCENTER, SECONDARY VOLTAGE                                           | 2                 | EA   | \$22,130.00 | \$44,260.00              | 0.00                 | EA   | \$22,130.00 | \$0.00           |
| 206                         | 715-7-12    | LOADCENTER, PRIMARY VOLTAGE                                             | 2                 | EA   | \$16,930.00 | \$33,860.00              | 0.00                 | EA   | \$16,930.00 | \$0.00           |
| 207                         | 715-37-1    | PHOTO ELECTRIC CONTROL ASSEMBLY                                         | 2                 | EA   | \$2,142.00  | \$4,284.00               | 0.00                 | EA   | \$2,142.00  | \$0.00           |
| 208                         | 1050-11212  | PVC UTILITY PIPE-2-4.9                                                  | 12,640            | LF   | \$17.00     | \$214,880.00             | 895.00               | LF   | \$17.00     | \$15,215.00      |
| 208A                        | 715 4 999** | POLE-STEEL 30' 140 MPH                                                  | 60                | EA   | \$3,034.00  | \$182,040.00             | 0.00                 | EA   | \$3,034.00  | \$0.00           |
| 209                         | 900-5004-16 | DIVISION 16, ELECTRICAL(XFMRS)                                          | 2                 | EA   | \$5,590.00  | \$11,180.00              | 0.00                 | EA   | \$5,590.00  | \$0.00           |
| 210                         |             | INTENTIONALLY LEFT BLANK                                                |                   |      |             |                          |                      |      |             |                  |
|                             |             | INTENTIONALLY LEFT BLANK                                                |                   |      |             |                          |                      |      |             |                  |
| 210A                        | 999-1000**  | EV CAR CHARGING STATION                                                 | 4                 | EA   | \$11,866.00 | \$47,464.00              | 0.00                 | EA   | \$11,866.00 | \$0.00           |
| Subtotal                    |             |                                                                         |                   |      |             | \$698,925.00             |                      |      |             | \$30,625.00      |
| SECTION TOTAL COST          |             |                                                                         |                   |      |             | \$1,443,364.00           |                      |      |             | \$44,660.00      |

# CHANGE ORDER #1 - APPENDIX B – Revised Bid Submittal Sheets

Bid No.: 167-0342-CP(PF)

Bid Title: AIRPORT LANDSIDE AND PARKING LOT IMPROVEMENTS PID# 0015466A

|                                                    |           |                                                                                                                                                                                                                                                                                                                                                                       | ORIGINAL CONTRACT |      |             |                          | CHANGE IN CONTRACT   |      |             |                  |
|----------------------------------------------------|-----------|-----------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|------|-------------|--------------------------|----------------------|------|-------------|------------------|
| Item No.                                           | Spec. No. | Item Description                                                                                                                                                                                                                                                                                                                                                      | BID Quantity      | Unit | Unit Value  | Original Contract Amount | Change in Quantities | Unit | Unit Value  | Change in Amount |
| TOLL/TICKETING PLAZAS & PARKING LOT ACCESS CONTROL |           |                                                                                                                                                                                                                                                                                                                                                                       |                   |      |             |                          |                      |      |             |                  |
| 211                                                | N/A       | PRE-ENGINEERED TOLL BOOTH WITHOUT RESTROOM,                                                                                                                                                                                                                                                                                                                           | 2                 | LS   | \$33,533.00 | \$67,066.00              | 0.00                 | LS   | \$33,533.00 | \$0.00           |
| 212                                                | N/A       | PRE-ENGINEERED TOLL BOOTH WITH RESTROOM                                                                                                                                                                                                                                                                                                                               | 1                 | LS   | \$52,311.00 | \$52,311.00              | 0.00                 | LS   | \$52,311.00 | \$0.00           |
| 213                                                | 10538     | 25' X 90' PRE-ENGINEERED TOLL PLAZA CANOPY, COMPLETE AND IN-PLACE INCLUDING LIGHTING, SIGNAGE AND FOUNDATIONS.                                                                                                                                                                                                                                                        | 1                 | LS   | \$95,941.00 | \$95,941.00              | 0.00                 | LS   | \$95,941.00 | \$0.00           |
| 214                                                | 10538     | 18' X 40' PRE-ENGINEERED TICKETING PLAZA CANOPY, COMPLETE AND IN-PLACE INCLUDING LIGHTING AND FOUNDATIONS.                                                                                                                                                                                                                                                            | 2                 | LS   | \$48,863.00 | \$97,726.00              | 0.00                 | LS   | \$48,863.00 | \$0.00           |
| 215                                                | 0519 7B   | TRAFFIC BOLLARDS                                                                                                                                                                                                                                                                                                                                                      | 36                | EA   | \$200.00    | \$7,200.00               | 0.00                 | EA   | \$200.00    | \$0.00           |
| 216                                                | 01210-1   | BID ALLOWANCE FOR THE PURCHASE AND DELIVERY ONLY OF 3 DOT LED BLANK-OUT SIGNS (MESSAGE: CASHIER/CLOSED), SIGNAL TECH PRODUCT ID 41013, MODEL DOT3660GR-B035DS, AND 5 SWITCHES, SIGNAL TECH PRODUCT ID 3039, MODEL SG. COST TO INSTALL SIGNS AND SWITCHES (INCLUDING WIRING) TO BE CONSIDERED INCIDENTAL AND INCLUDED IN THE COST OF THE TOLL PLAZA CANOPY STRUCTURE.  | 1                 | LS   | \$20,000.00 | \$20,000.00              | 0.00                 | LS   | \$20,000.00 | \$0.00           |
| 217                                                | 01210-2   | BID ALLOWANCE FOR THE PURCHASE, DELIVERY AND INSTALLATION OF ONE NEW GATE ARM FOR THE TOLL PLAZA, INCLUDING IN-PAVEMENT DETECTOR LOOPS.                                                                                                                                                                                                                               | 1                 | LS   | \$5,500.00  | \$5,500.00               | 0.00                 | LS   | \$5,500.00  | \$0.00           |
| 218                                                | 01210-3   | BID ALLOWANCE FOR THE RELOCATION AND INSTALLATION OF 4 EXISTING GATE ARMS FROM THE EXISTING LONG TERM AND SHORT TERM TOLL PLAZAS TO THE NEW TOLL PLAZA, INCLUDING IN-PAVEMENT DETECTOR LOOPS. ONE OF THE GATE ARMS IS TO BE RELOCATED TWICE, FIRST FROM ONE OF THE EXISTING TOLL PLAZAS TO THE INTERIM SHORT TERM LOT IN PHASE 2, AND THEN TO THE NEW TOLL PLAZA.     | 1                 | LS   | \$12,000.00 | \$12,000.00              | 0.00                 | LS   | \$12,000.00 | \$0.00           |
| 219                                                | 01210-4   | BID ALLOWANCE FOR THE RELOCATION AND INSTALLATION OF 4 EXISTING TICKET DISPENSERS AND GATE ARMS, TO BE RELOCATED TWICE, FIRST FROM THE EXISTING LONG TERM AND SHORT TERM ENTRANCE TICKETING PLAZAS TO THE TEMPORARY LONG AND SHORT TERM ENTRANCES IN PHASE 2 AND THEN TO THE NEW LONG AND SHORT TERM ENTRANCE TICKETING PLAZAS, INCLUDING IN-PAVEMENT DETECTOR LOOPS. | 1                 | LS   | \$30,000.00 | \$30,000.00              | 0.00                 | LS   | \$30,000.00 | \$0.00           |
| 220                                                | 01210-5   | BID ALLOWANCE FOR THE RELOCATION AND INSTALLATION OF 2 EXISTING CREDIT CARD MACHINES, TO BE RELOCATED FROM THE EXISTING LONG TERM AND SHORT TERM TOLL PLAZAS TO THE NEW TOLL PLAZA.                                                                                                                                                                                   | 1                 | LS   | \$3,000.00  | \$3,000.00               | 0.00                 | LS   | \$3,000.00  | \$0.00           |
| 221                                                | 01210-6   | BID ALLOWANCE FOR THE RELOCATION AND INSTALLATION OF ALL EXISTING EQUIPMENT IN THE 2 EXISTING TOLL BOOTHS TO THE NEW TOLL PLAZA BOOTHS.                                                                                                                                                                                                                               | 1                 | LS   | \$3,000.00  | \$3,000.00               | 0.00                 | LS   | \$3,000.00  | \$0.00           |
| 222                                                | 01210-7   | BID ALLOWANCE FOR THE PURCHASE, DELIVERY AND INSTALLATION OF ALL REQUIRED NEW EQUIPMENT FOR NEW TOLL PLAZA BOOTHS.                                                                                                                                                                                                                                                    | 1                 | LS   | \$20,000.00 | \$20,000.00              | 0.00                 | LS   | \$20,000.00 | \$0.00           |
| SECTION TOTAL COST                                 |           |                                                                                                                                                                                                                                                                                                                                                                       |                   |      |             | \$413,744.00             | \$0.00               |      |             |                  |
| REMOTE PARKING LOT #3                              |           |                                                                                                                                                                                                                                                                                                                                                                       |                   |      |             |                          |                      |      |             |                  |
| 1                                                  | TS-001**  | MOBILIZATION                                                                                                                                                                                                                                                                                                                                                          | 1                 | LS   | \$15,000.00 | \$15,000.00              | 0.00                 | LS   | \$15,000.00 | \$0.00           |
| 2                                                  | 102-1     | MAINTENANCE OF TRAFFIC                                                                                                                                                                                                                                                                                                                                                | 1                 | LS   | \$5,000.00  | \$5,000.00               | 0.00                 | LS   | \$5,000.00  | \$0.00           |
| EROSION CONTROL                                    |           |                                                                                                                                                                                                                                                                                                                                                                       |                   |      |             |                          |                      |      |             |                  |
| 3                                                  | 104       | EROSION AND SEDIMENT CONTROLS (SILT FENCE, INLET PROTECTION, SOIL TRACKING PREVENTION DEVICE)                                                                                                                                                                                                                                                                         | 1                 | LS   | \$2,500.00  | \$2,500.00               | 0.00                 | LS   | \$2,500.00  | \$0.00           |
| Subtotal                                           |           |                                                                                                                                                                                                                                                                                                                                                                       |                   |      |             | \$22,500.00              | \$0.00               |      |             |                  |
| CLEARING & GRUBBING                                |           |                                                                                                                                                                                                                                                                                                                                                                       |                   |      |             |                          |                      |      |             |                  |
| 4                                                  | 110-1-1   | CLEARING AND GRUBBING                                                                                                                                                                                                                                                                                                                                                 | 1                 | LS   | \$50,000.00 | \$50,000.00              | 0.00                 | LS   | \$50,000.00 | \$0.00           |
| Subtotal                                           |           |                                                                                                                                                                                                                                                                                                                                                                       |                   |      |             | \$50,000.00              | \$0.00               |      |             |                  |
| FINAL GRADING                                      |           |                                                                                                                                                                                                                                                                                                                                                                       |                   |      |             |                          |                      |      |             |                  |
| 5                                                  | 120-2     | BORROW EXCAVATION (AIRPORT STOCKPILE)                                                                                                                                                                                                                                                                                                                                 | 4,800             | CY   | \$6.00      | \$28,800.00              | (4800.00)            | CY   | \$6.00      | (\$28,800.00)    |
| 6                                                  | 120-6     | EMBANKMENT                                                                                                                                                                                                                                                                                                                                                            | 3,200             | CY   | \$4.00      | \$12,800.00              | 1300.00              | CY   | \$4.00      | \$5,200.00       |
| Subtotal                                           |           |                                                                                                                                                                                                                                                                                                                                                                       |                   |      |             | \$41,600.00              | (\$23,600.00)        |      |             |                  |



# CHANGE ORDER #1 - APPENDIX B – Revised Bid Submittal Sheets

Bid No.: 167-0342-CP(PF)

Bid Title: AIRPORT LANDSIDE AND PARKING LOT IMPROVEMENTS P/D# 0015466A

|                                                               |                   |                                                                                                                                                                                       | ORIGINAL CONTRACT |      |             |                          | CHANGE IN CONTRACT   |      |             |                  |
|---------------------------------------------------------------|-------------------|---------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|-------------------|------|-------------|--------------------------|----------------------|------|-------------|------------------|
| Item No.                                                      | Spec. No.         | Item Description                                                                                                                                                                      | BID Quantity      | Unit | Unit Value  | Original Contract Amount | Change In Quantities | Unit | Unit Value  | Change in Amount |
| <b>SITE WORK</b>                                              |                   |                                                                                                                                                                                       |                   |      |             |                          |                      |      |             |                  |
| 7                                                             | 285701            | OPTIONAL BASE, BASE GROUP 01 (4 IN ASPHALT MILLINGS COMPACTED (AIRPORT STOCKPILE))                                                                                                    | 27,000            | SY   | \$3.00      | \$81,000.00              | 0.00                 | SY   | \$3.00      | \$0.00           |
| 8                                                             | 285701            | OPTIONAL BASE, BASE GROUP 01 (4 IN ASPHALT MILLINGS COMPACTED (CONTRACTOR STOCKPILE))                                                                                                 | 5,000             | SY   | \$7.00      | \$35,000.00              | 0.00                 | SY   | \$7.00      | \$0.00           |
| 9                                                             | 160-4             | TYPE B STABILIZATION, LBR 40 (12 IN)                                                                                                                                                  | 630               | SY   | \$17.00     | \$10,710.00              | 20.00                | SY   | \$17.00     | \$340.00         |
| 10                                                            | 285-702           | OPTIONAL BASE, BASE GROUP 04                                                                                                                                                          | 600               | SY   | \$15.00     | \$9,000.00               | 15.00                | SY   | \$15.00     | \$225.00         |
| 11                                                            | 334-1-12          | SUPERPAVE ASPHALTIC CONCRETE, TRAFFIC LEVEL B                                                                                                                                         | 75                | TN   | \$153.00    | \$11,475.00              | 0.00                 | TN   | \$153.00    | \$0.00           |
| 11A                                                           | 524-1-29          | CONCRETE DITCH PAVEMENT, REINFORCED, 4"                                                                                                                                               | 76                | SY   | \$70.00     | \$5,320.00               | 0.00                 | SY   | \$70.00     | \$0.00           |
| 11B                                                           | 522-2             | CONCRETE SIDEWALK AND DRIVEWAYS, 6"                                                                                                                                                   | 0                 | SY   | \$83.00     | \$0.00                   | 9.00                 | SY   | \$83.00     | \$747.00         |
| 12                                                            | 570-1-1           | PERFORMANCE TURF                                                                                                                                                                      | 16,000            | SY   | \$1.00      | \$16,000.00              | (13750.00)           | SY   | \$1.00      | (\$13,750.00)    |
| 13                                                            | 570-1-2           | PERFORMANCE TURF, SOD                                                                                                                                                                 | 2,500             | SY   | \$3.00      | \$7,500.00               | 9000.00              | SY   | \$3.00      | \$27,000.00      |
| 14                                                            | 542-70            | WHEEL STOP                                                                                                                                                                            | 832               | EA   | \$71.00     | \$59,072.00              | (58.00)              | EA   | \$71.00     | (\$4,118.00)     |
| 15                                                            | 550-10-221        | FENCING, TYPE B, 6 IN, W/BARBED WIRE ATTACHMENT                                                                                                                                       | 2,500             | LF   | \$14.00     | \$35,000.00              | (2500.00)            | LF   | \$14.00     | (\$35,000.00)    |
| 16                                                            | 550-60-233-1      | 6 FT FENCE GATE, CANTILEVER SLIDE WITH 1FT BARBED WIRE (16')                                                                                                                          | 2                 | EA   | \$2,500.00  | \$5,000.00               | (2.00)               | EA   | \$2,500.00  | (\$5,000.00)     |
| 17                                                            | 550-60-233-2      | 6 FT FENCE GATE, CANTILEVER SLIDE WITH 1FT BARBED WIRE (18')                                                                                                                          | 1                 | EA   | \$2,500.00  | \$2,500.00               | (1.00)               | EA   | \$2,500.00  | (\$2,500.00)     |
| <b>Subtotal</b>                                               |                   |                                                                                                                                                                                       |                   |      |             | \$277,877.00             |                      |      |             | (\$32,658.00)    |
| <b>SIGNING AND PAVEMENT MARKINGS</b>                          |                   |                                                                                                                                                                                       |                   |      |             |                          |                      |      |             |                  |
| 18                                                            | 1700-1-11         | SINGLE POST SIGN, FURNISH AND INSTALL GROUND MOUNT, <12 SF                                                                                                                            | 3                 | AS   | \$284.00    | \$852.00                 | 0.00                 | AS   | \$284.00    | \$0.00           |
| 19                                                            | 1710-11-201       | PAINTED PAVEMENT MARKINGS, STANDARD, YELLOW, SOLID, 6 IN                                                                                                                              | 230               | LF   | \$1.00      | \$230.00                 | 0.00                 | LF   | \$1.00      | \$0.00           |
| 20                                                            | 1710-11-125       | PAINTED PAVEMENT MARKINGS, STANDARD, WHITE SOLID, 24 IN                                                                                                                               | 32                | LF   | \$4.00      | \$128.00                 | 0.00                 | LF   | \$4.00      | \$0.00           |
| 20A                                                           | 1710-11-160       | PAINTED PAVEMENT MARKINGS, WHITE, LEFT ARROW                                                                                                                                          |                   |      |             |                          | 1.00                 | EA   | \$45.00     | \$45.00          |
| 20B                                                           | 1710-11-170       | PAINTED PAVEMENT MARKINGS, WHITE, "ONLY" MESSAGE                                                                                                                                      |                   |      |             |                          | 1.00                 | EA   | \$90.00     | \$90.00          |
| <b>Subtotal</b>                                               |                   |                                                                                                                                                                                       |                   |      |             | \$1,210.00               |                      |      |             | \$138.00         |
| <b>STORM DRAINAGE</b>                                         |                   |                                                                                                                                                                                       |                   |      |             |                          |                      |      |             |                  |
| 21                                                            | 430-175-121       | CORRUGATED METAL PIPE, 12 IN STORM DRAIN                                                                                                                                              | 120               | LF   | \$50.00     | \$6,000.00               | (120.00)             | LF   | \$50.00     | (\$6,000.00)     |
| 21A                                                           | 430-174-215       | PIPE CULV, OPT MATL, OTHER, 15"SD (12"x18" ERCP)                                                                                                                                      |                   |      |             |                          | 135.00               | LF   | \$120.00    | \$16,200.00      |
| 21B                                                           | 430-175-124       | PIPE CULVERT, OPTIONAL MATERIAL, ROUND, 24" S/C/D                                                                                                                                     |                   |      |             |                          | 95.00                | LF   | \$104.00    | \$9,880.00       |
| 21C                                                           | 430-982-129       | MITERED END SECT, OPTIONAL RD, 24" CD                                                                                                                                                 |                   |      |             |                          | 1.00                 | EA   | \$4,971.00  | \$4,971.00       |
| 21D                                                           | 425-1551          | INLET, DT BOT, FDOT TYPE E W/SKIMMER                                                                                                                                                  |                   |      |             |                          | 1.00                 | EA   | \$3,500.00  | \$3,500.00       |
| 21E                                                           | 425-1521          | INLET, DT BOT, FDOT TYPE C W/SKIMMER                                                                                                                                                  |                   |      |             |                          | 1.00                 | EA   | \$8,265.00  | \$8,265.00       |
| <b>Subtotal</b>                                               |                   |                                                                                                                                                                                       |                   |      |             | \$6,000.00               |                      |      |             | \$36,816.00      |
| <b>ELECTRICAL</b>                                             |                   |                                                                                                                                                                                       |                   |      |             |                          |                      |      |             |                  |
| 22                                                            | TS-003**          | 12 FT MAIN GATE ARM INCL. PAD, INDUCTIVE LOOPS, CONDUITS, WIRING, MAIN AND SHUTTLE ENTRANCE                                                                                           | 1                 | EA   | \$5,000.00  | \$5,000.00               | 0.00                 | EA   | \$5,000.00  | \$0.00           |
| 23                                                            | TS-004**          | 16 FT SHUTTLE GATE ARM INCL. PAD, INDUCTIVE LOOPS, RF RECEIVER AND WIRING                                                                                                             | 1                 | EA   | \$6,000.00  | \$6,000.00               | (1.00)               | EA   | \$6,000.00  | (\$6,000.00)     |
| 24                                                            | 1050 999**        | ELECTRICAL CONNECTION TO GATE ARMS INCL. ELECTRICAL DESIGN, ALL REQUIRED PERMITS, CONDUIT, WIRING, PULL BOXES, TRENCHING, SAW CUTTING, PAVEMENT REPAIR AND ANY OTHER ASSOCIATED WORK. | 1                 | LS   | \$12,500.00 | \$12,500.00              | 0.00                 | LS   | \$12,500.00 | \$0.00           |
| <b>Subtotal</b>                                               |                   |                                                                                                                                                                                       |                   |      |             | \$23,500.00              |                      |      |             | (\$6,000.00)     |
| <b>TOLL/TICKETING PLAZAS &amp; PARKING LOT ACCESS CONTROL</b> |                   |                                                                                                                                                                                       |                   |      |             |                          |                      |      |             |                  |
| 25                                                            | 10751.35 12 999** | PASSENGER SHELTER INCL. PAD, PERMITTING, AND 4 BOLLARDS                                                                                                                               | 4                 | EA   | \$10,000.00 | \$40,000.00              | 0.00                 | EA   | \$10,000.00 | \$0.00           |
| <b>Subtotal</b>                                               |                   |                                                                                                                                                                                       |                   |      |             | \$40,000.00              |                      |      |             | \$0.00           |
| <b>LANDSCAPING</b>                                            |                   |                                                                                                                                                                                       |                   |      |             |                          |                      |      |             |                  |
| 26                                                            | 1581-903**        | DWARF SCHEFFLERA, 24" HT.                                                                                                                                                             |                   |      |             |                          | 280.00               | LS   | \$10.00     | \$2,800.00       |
| <b>Subtotal</b>                                               |                   |                                                                                                                                                                                       |                   |      |             | \$0.00                   |                      |      |             | \$2,800.00       |
| <b>SECTION TOTAL COST</b>                                     |                   |                                                                                                                                                                                       |                   |      |             | \$462,387.00             |                      |      |             | (\$21,908.00)    |

# CHANGE ORDER #1 - APPENDIX B – Revised Bid Submittal Sheets

Bid No.: 167-0342-CP(PF)

Bid Title: AIRPORT LANDSIDE AND PARKING LOT IMPROVEMENTS PID# 0015466A

| Item No. | Spec. No. | Item Description | ORIGINAL CONTRACT |      |            |                          | CHANGE IN CONTRACT   |      |            |                  |
|----------|-----------|------------------|-------------------|------|------------|--------------------------|----------------------|------|------------|------------------|
|          |           |                  | BID Quantity      | Unit | Unit Value | Original Contract Amount | Change In Quantities | Unit | Unit Value | Change in Amount |

ADDITIONAL COSTS FOR NEW PAY ITEMS AND QUANTITY ADJUSTMENTS TO EXISTING PAY ITEMS (EXCLUDING MOT REPHASING) \$492,655.62

|                           |                  |                                                                                                                                                                                                  |   |    |              |                        |              |    |              |                       |
|---------------------------|------------------|--------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------------|---|----|--------------|------------------------|--------------|----|--------------|-----------------------|
| <b>ALLOWANCES</b>         |                  |                                                                                                                                                                                                  |   |    |              |                        |              |    |              |                       |
| <b>ALLOWANCES</b>         |                  |                                                                                                                                                                                                  |   |    |              |                        |              |    |              |                       |
| 1                         | ALLOWANCE        | TRASH COMPACTOR ENCLOSURE (15' X 30') - CONSTRUCT CONCRETE SLAB, PERIMETER WALLS, GATE AND ASSOCIATED ELECTRICAL COMPONENTS                                                                      | 1 | LS | \$30,000.00  | \$30,000.00            | (1.00)       | LS | \$30,000.00  | (\$30,000.00)         |
| 2                         | ALLOWANCE        | CONSTRUCT PERMANENT AREA LIGHTING FOR REMOTE PARKING LOT #2 - EIGHT (8) LIGHT POLES WITH TWO (2) LED FIXTURES EACH AND ASSOCIATED SERVICE DROP AND OVERHEAD WIRING                               | 1 | LS | \$35,000.00  | \$35,000.00            | (1.00)       | LS | \$35,000.00  | (\$35,000.00)         |
| 3                         | ALLOWANCE        | RELOCATION OF TWO (2) EXISTING AIRPORT MONUMENT SIGNS. (INCLUDES FOUNDATION DESIGN AND CONSTRUCTION)                                                                                             | 1 | LS | \$60,000.00  | \$60,000.00            | (1.00)       | LS | \$60,000.00  | (\$60,000.00)         |
| 4                         | ALLOWANCE        | PROVIDE ONE (1) PORTABLE CHANGEABLE MESSAGE SIGN. (TO BE TURNED OVER TO OWNER AT THE END OF THE CONTRACT)                                                                                        | 1 | LS | \$15,000.00  | \$15,000.00            | (1.00)       | LS | \$15,000.00  | (\$15,000.00)         |
| 5                         | ALLOWANCE        | PROVIDE TWO (2) 12'X12' DIGITAL MESSAGE SIGNS. (DAKTRONICS OR APPROVED EQUAL), SIGN STRUCTURE, FOUNDATION DESIGN AND CONSTRUCTION, AND ASSOCIATED ELECTRICAL AND DATA COMPONENTS.                | 1 | LS | \$200,000.00 | \$200,000.00           | (1.00)       | LS | \$200,000.00 | (\$200,000.00)        |
| 6                         | ALLOWANCE        | PROVIDE EIGHT (8) PORTABLE LIGHT BANKS FOR TEMPORARY REMOTE PARKING LOT #3 FOR 120 CALENDAR DAYS (MONTHS OF NOVEMBER/DECEMBER 2017 AND 2018). CONTRACTOR OPERATES, PROVIDES FUEL, AND MAINTAINS. | 1 | LS | \$50,000.00  | \$50,000.00            | (1.00)       | LS | \$50,000.00  | (\$50,000.00)         |
| 7                         | Relocate Existin | COVERED PEDESTRIAN WALKWAY                                                                                                                                                                       | 1 | LS | \$450,000.00 | \$450,000.00           | (1.00)       | LS | \$450,000.00 | (\$450,000.00)        |
| 8                         | ALLOWANCE        | PARKING LOT DIRECTIONAL SIGNAGE PROGRAM                                                                                                                                                          | 1 | LS | \$50,000.00  | \$50,000.00            | (1.00)       | LS | \$50,000.00  | (\$50,000.00)         |
| 9                         | ALLOWANCE        | ON-SITE ELECTRICAL AND COMMUNICATION SERVICES EXTENTIONS                                                                                                                                         | 1 | LS | \$75,000.00  | \$75,000.00            | (1.00)       | LS | \$75,000.00  | (\$75,000.00)         |
| <b>SECTION TOTAL COST</b> |                  |                                                                                                                                                                                                  |   |    |              | <b>\$966,000.00</b>    |              |    |              | <b>(\$966,000.00)</b> |
| <b>OWNERS CONTINGENCY</b> |                  |                                                                                                                                                                                                  |   |    |              |                        |              |    |              |                       |
| <b>OWNERS CONTINGENCY</b> |                  |                                                                                                                                                                                                  |   |    |              |                        |              |    |              |                       |
| 1                         | CONTINGENCY      | OWNER'S CONTINGENCY                                                                                                                                                                              | 1 | LS | \$600,000.00 | \$600,000.00           | (1.00)       | LS | \$600,000.00 | (\$600,000.00)        |
| 2                         | 999-0000         | UNSPECIFIED WORK                                                                                                                                                                                 |   |    |              |                        | 1,072,444.38 | EA | \$1.00       | \$1,072,444.38        |
| <b>SECTION TOTAL COST</b> |                  |                                                                                                                                                                                                  |   |    |              | <b>\$600,000.00</b>    |              |    |              | <b>\$472,444.38</b>   |
| <b>TOTAL BASE BID</b>     |                  |                                                                                                                                                                                                  |   |    |              | <b>\$13,236,899.88</b> |              |    |              | <b>\$319,300.00</b>   |
